



CO 119 Safety, Mobility & Bikeway Delivery: CM/GC

Project Dashboard

The purpose of this document is to provide a progress and financial update pertaining to the design and construction of the CO 119 Project and the following associated project numbers:

- **Design:** Project Number 21497
- **Construction Package 1:** Project Number 25959
- **Construction Package 2:** Project Number 25960
- **Construction Package 3:** Project Number 25961


Milestone Dates

Design






Construction Package 1

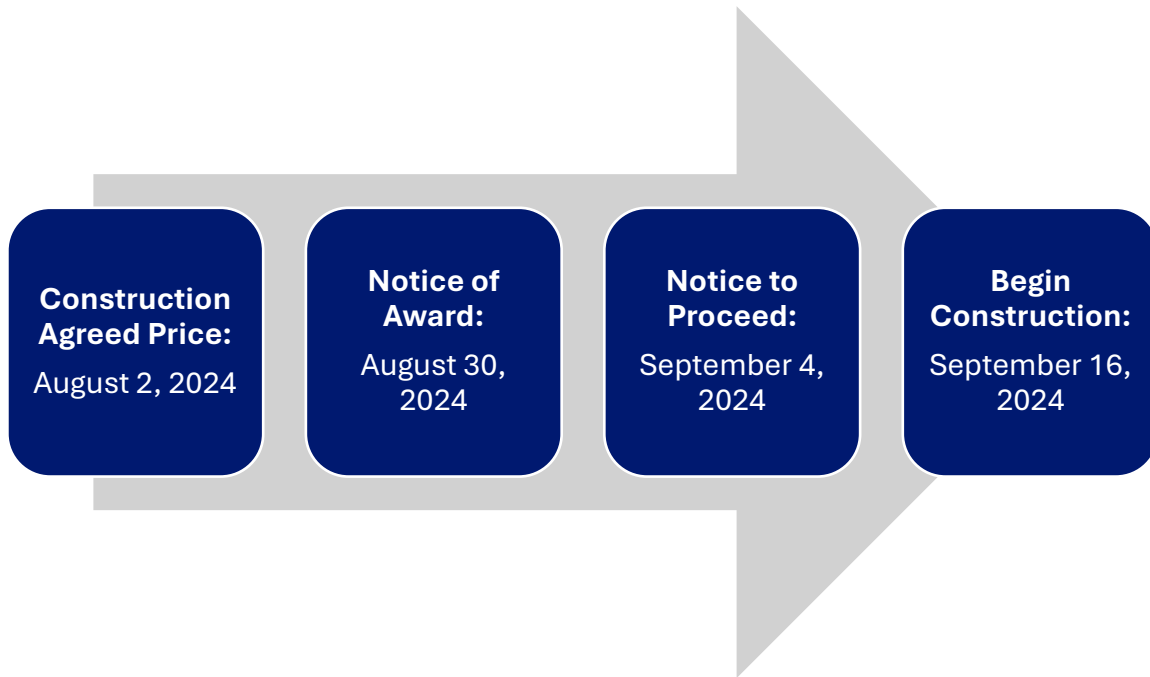


Construction Package 2

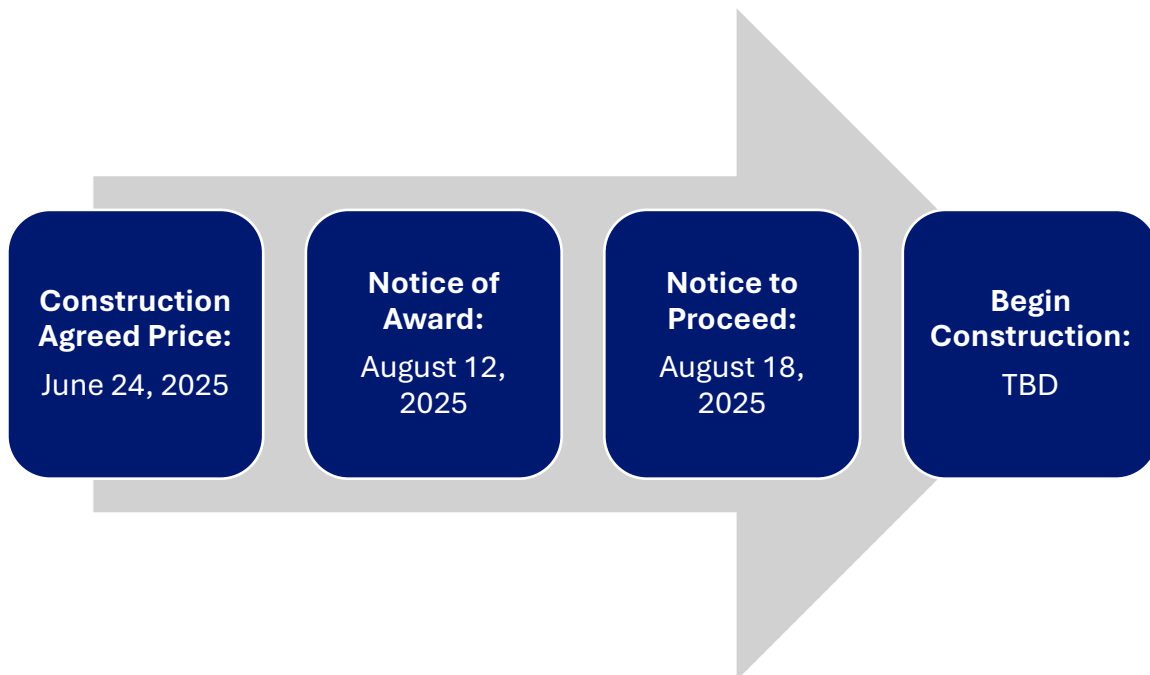




Construction Package 3



Project Progress by Percent

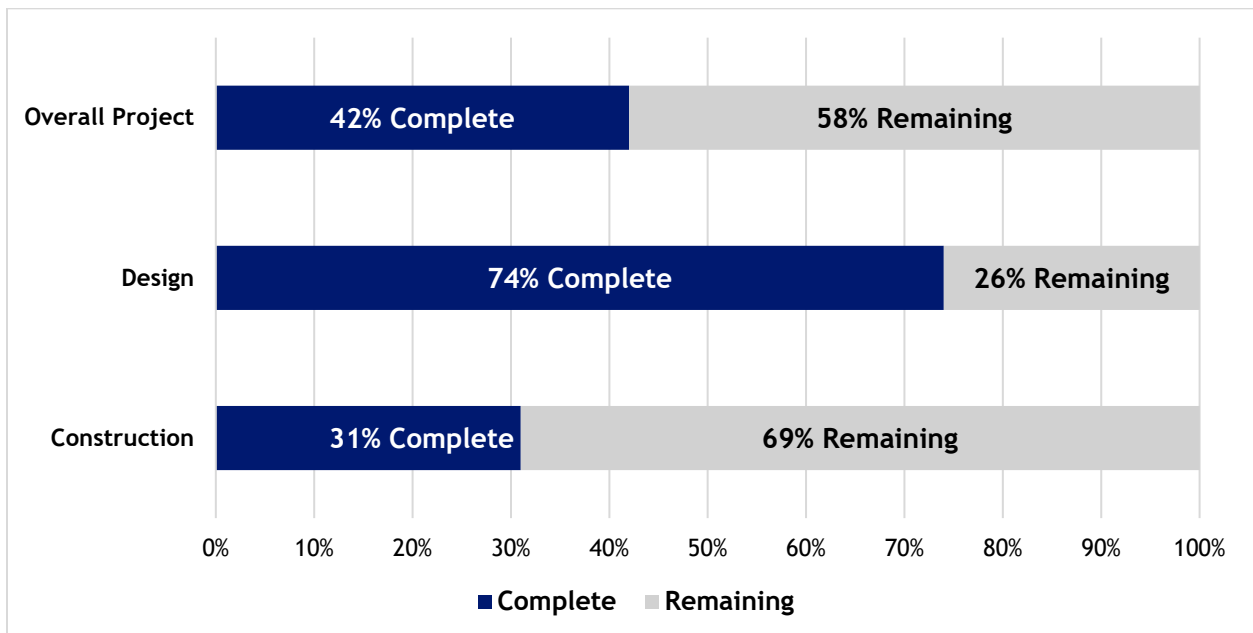





Financial Contract Information

The following bar charts display the project construction payments versus remaining funds, the current contract total, and the original contract amount for Construction Package 1, 2, and 3. Six change orders have been approved.


Construction Package 1

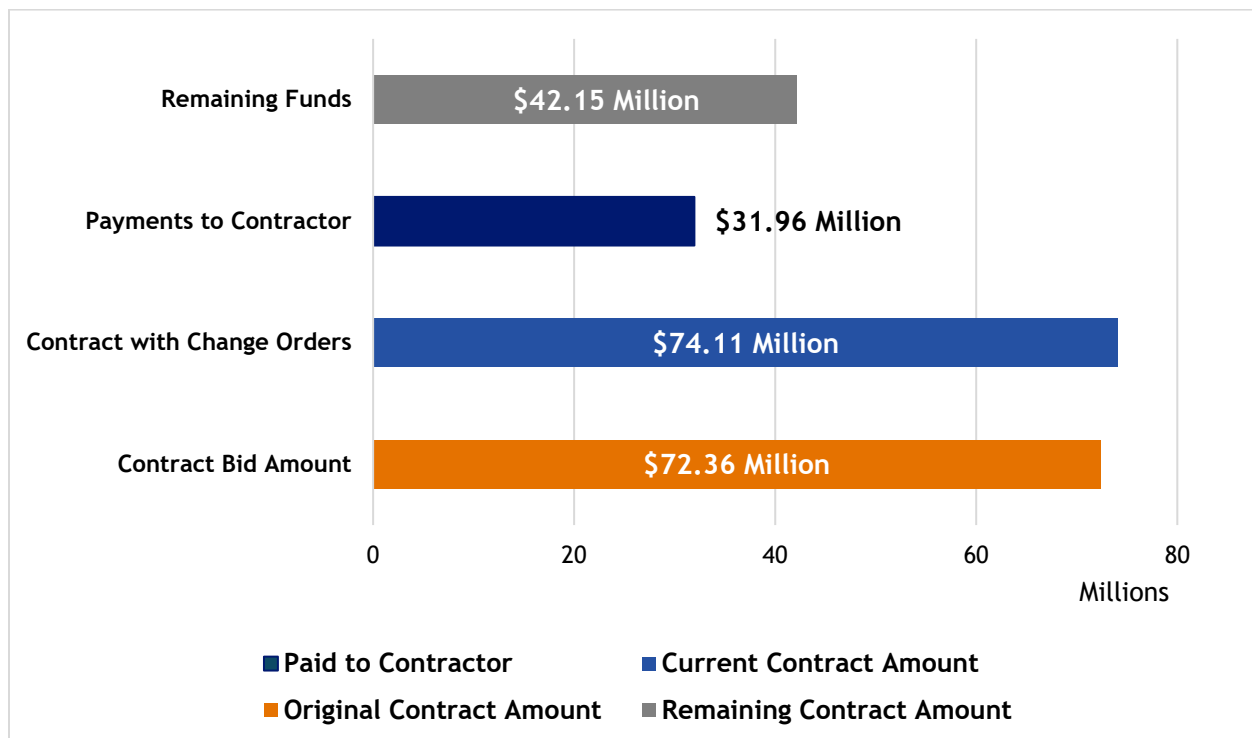

Construction Package 2

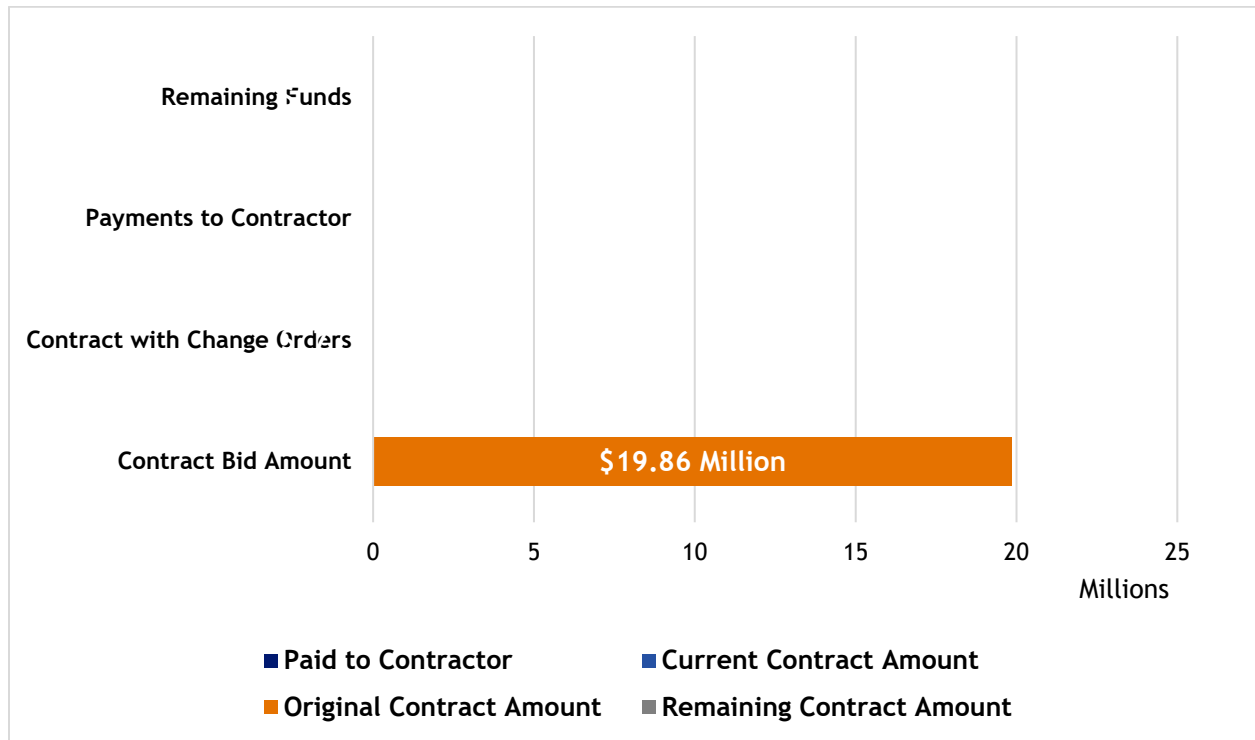

Construction Package 3






Contract Time


Design

The CMGC Preconstruction Contract was executed on October 11, 2023, and is expected to finish by February 15, 2027. The total contract time is 1,223 days.

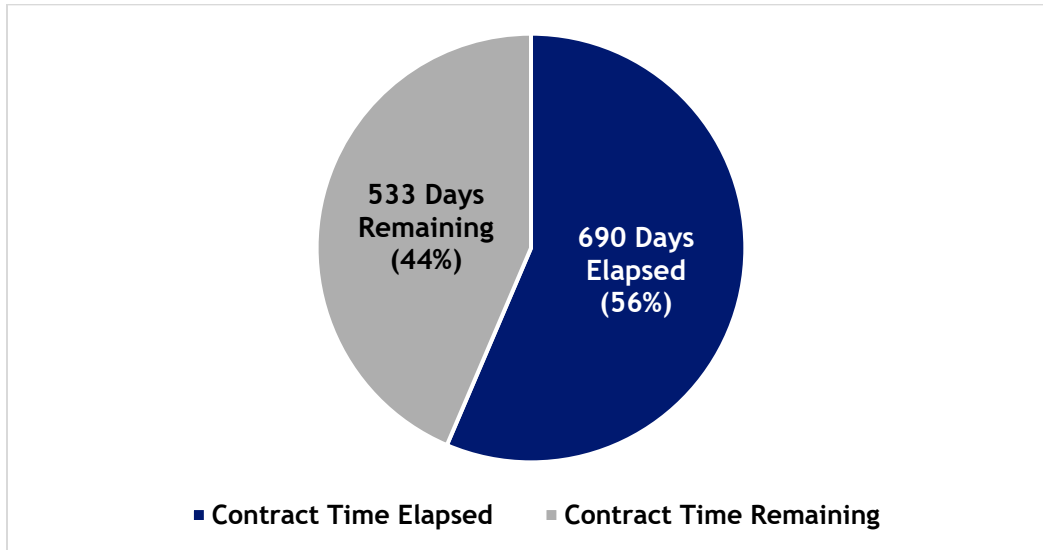

Construction Package 1


Construction for CP1 began on September 16, 2024, and is expected to finish by December 01, 2026. The total contract time is 806 days.

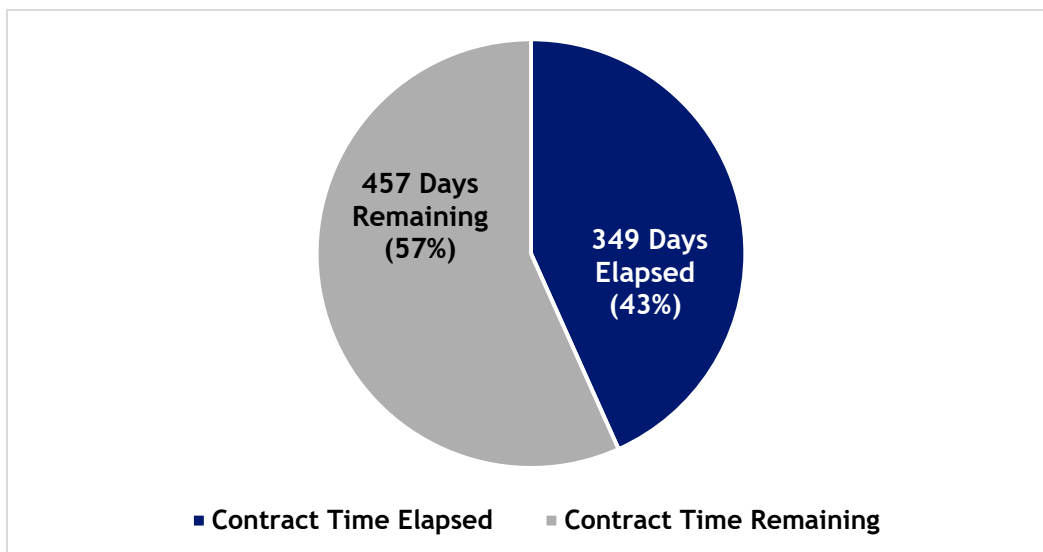



Construction Package 2

Construction Package 2 is expected to begin in mid September 2025 and finish by December 01, 2026. The total contract time is 442 days.

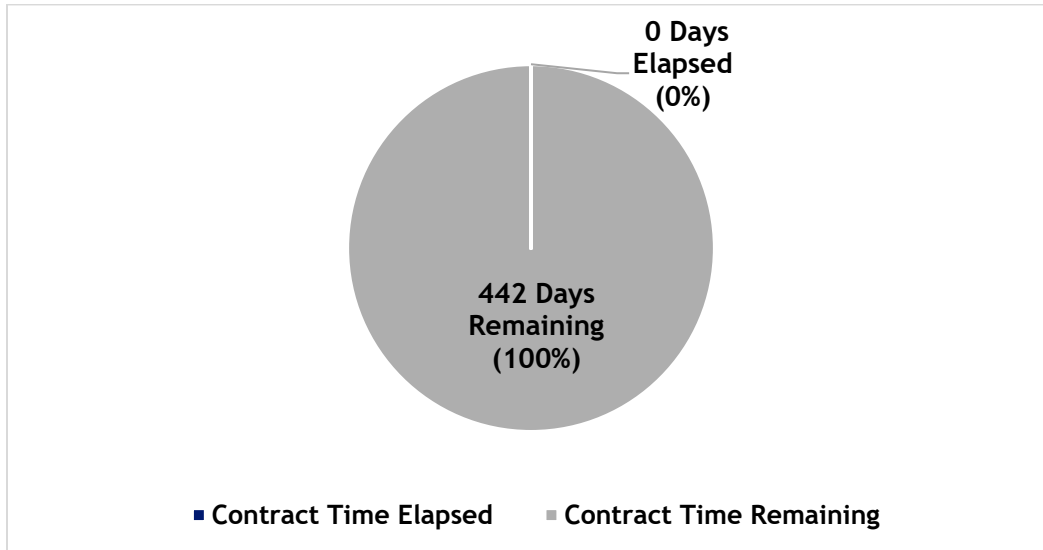

Construction Package 3

Construction Package 3 is expected to begin in May 2026 and finish by October 1, 2027. The total contract time is 518 days.

