



# CO 119 Safety & Mobility CM/GC Project Dashboard for November 2025

## Project Dashboard

The purpose of this document is to provide a progress and financial update pertaining to the design and construction of the CO 119 Project and the following associated project numbers:

- **Design:** Project Number 21497
- **Construction Package 1:** Project Number 25959
- **Construction Package 2:** Project Number 25960
- **Construction Package 3:** Project Number 25961

## Milestone Dates

### Design





**Construction Package 1**

**Construction Agreed Price:**  
August 2, 2024

**Notice of Award:**  
August 30, 2024

**Notice to Proceed:**  
September 4, 2024

**Begin Construction:**  
September 16, 2024

**Construction Package 2**

**Construction Agreed Price:**  
June 24, 2025


**Notice of Award:**  
August 12, 2025

**Notice to Proceed:**  
August 18, 2025


**Begin Construction:**  
September 22, 2025



## Construction Package 3

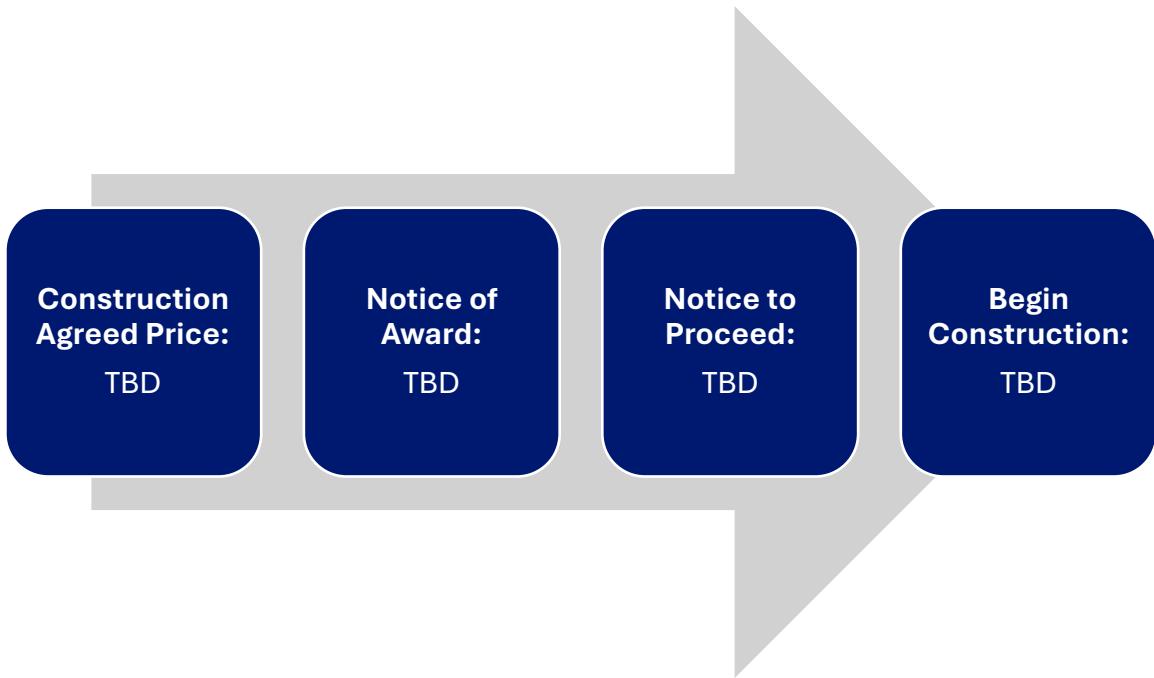

## Project Progress by Percent

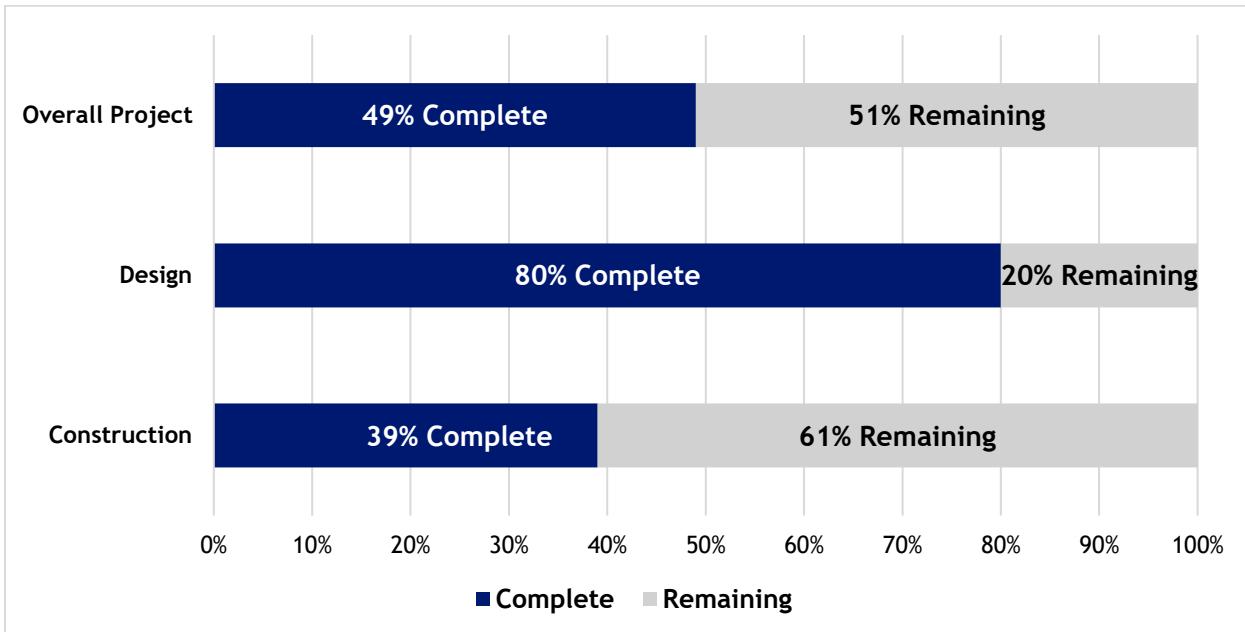




## Financial Contract Information


The following bar charts display the project construction payments versus remaining funds, the current contract total, and the original contract amount for Construction Package 1, 2, and 3. Seven change orders have been approved.

### Construction Package 1

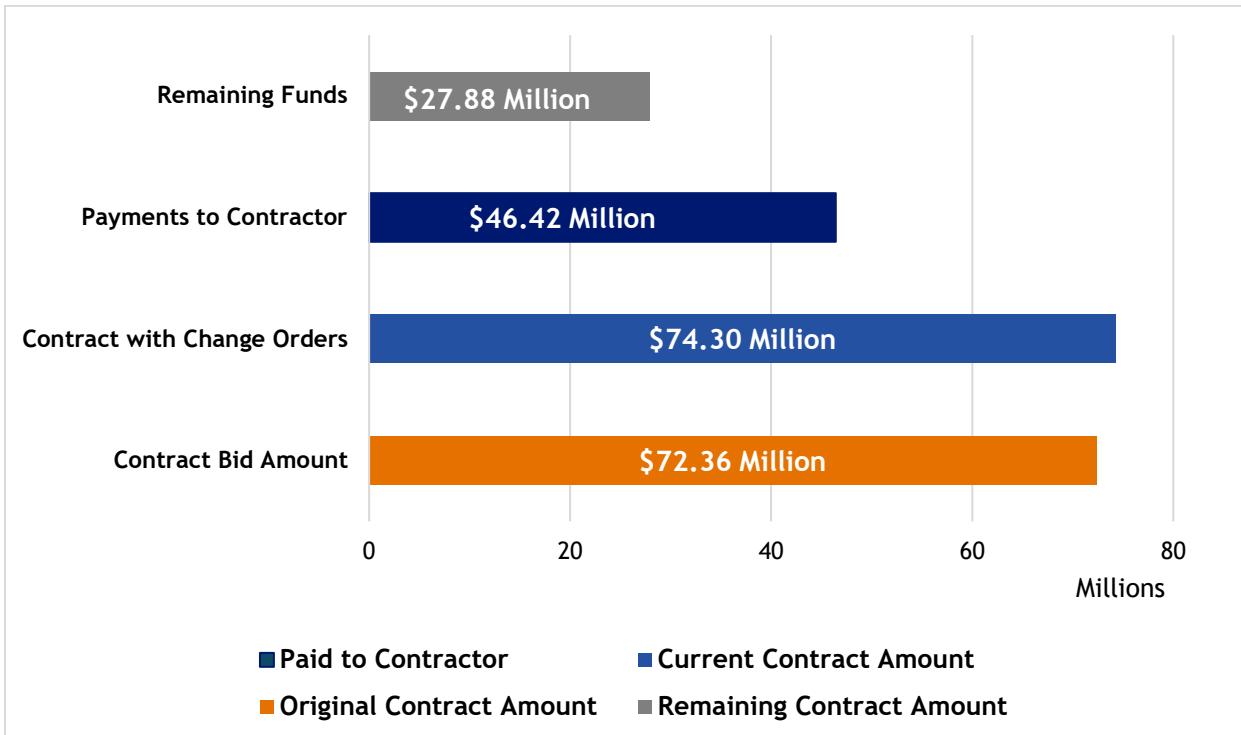




## Construction Package 2

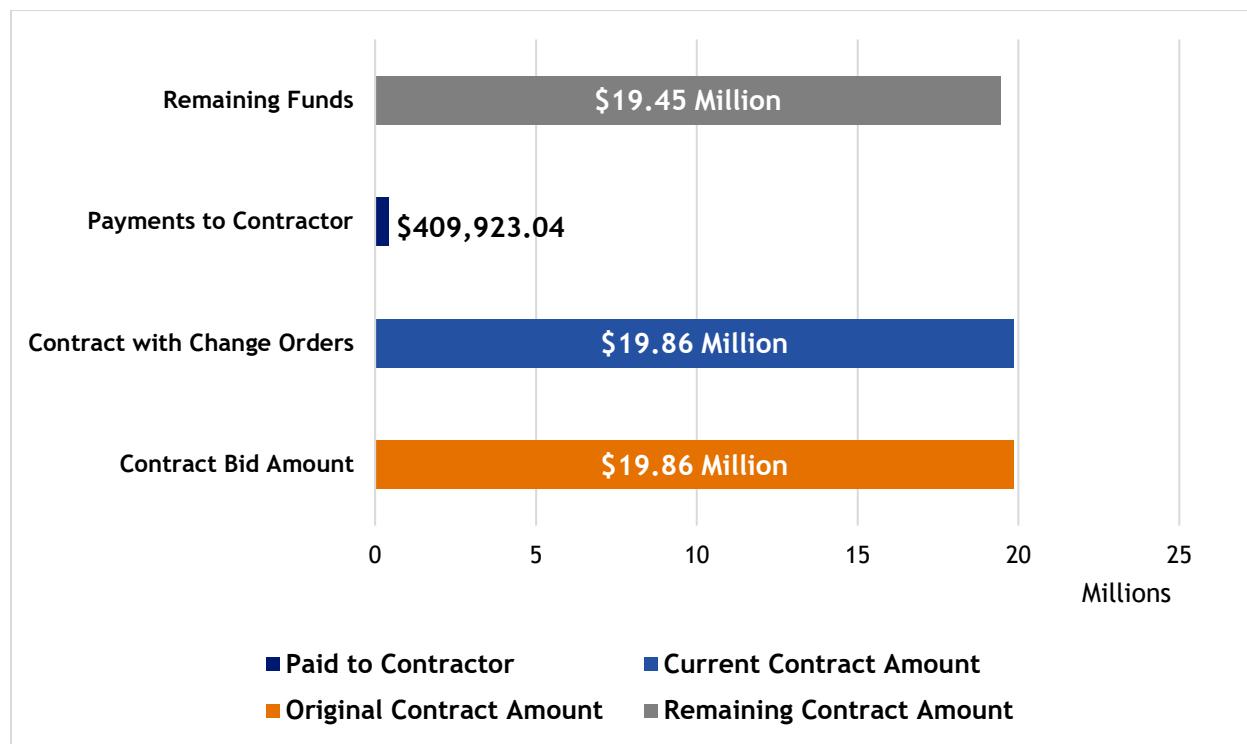

## Construction Package 3






## Contract Time


### Design

The CMGC Preconstruction Contract was executed on October 11, 2023, and is expected to finish by February 15, 2027. The total contract time is 1,223 days.

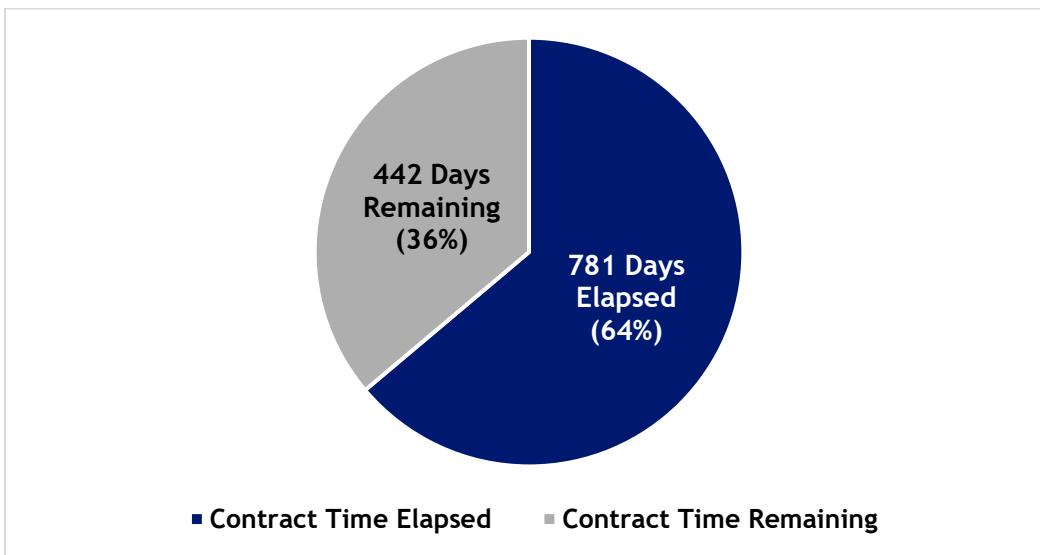

### Construction Package 1


Construction for CP1 began on September 16, 2024, and is expected to finish by December 01, 2026. The total contract time is 806 days.

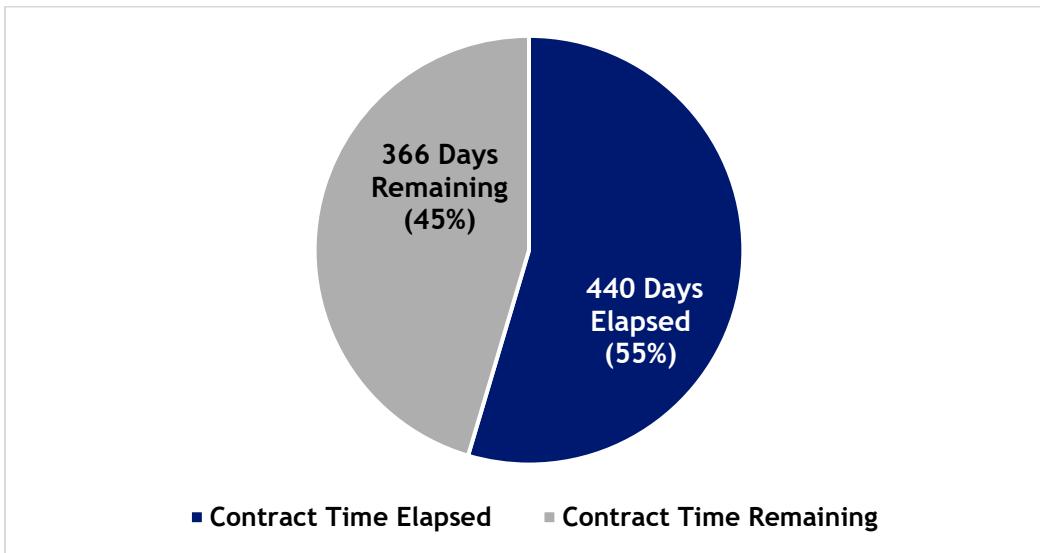



## Construction Package 2

Construction Package 2 started on September 22, 2025, and is expected to finish by December 01, 2026. The total contract time is 435 days.

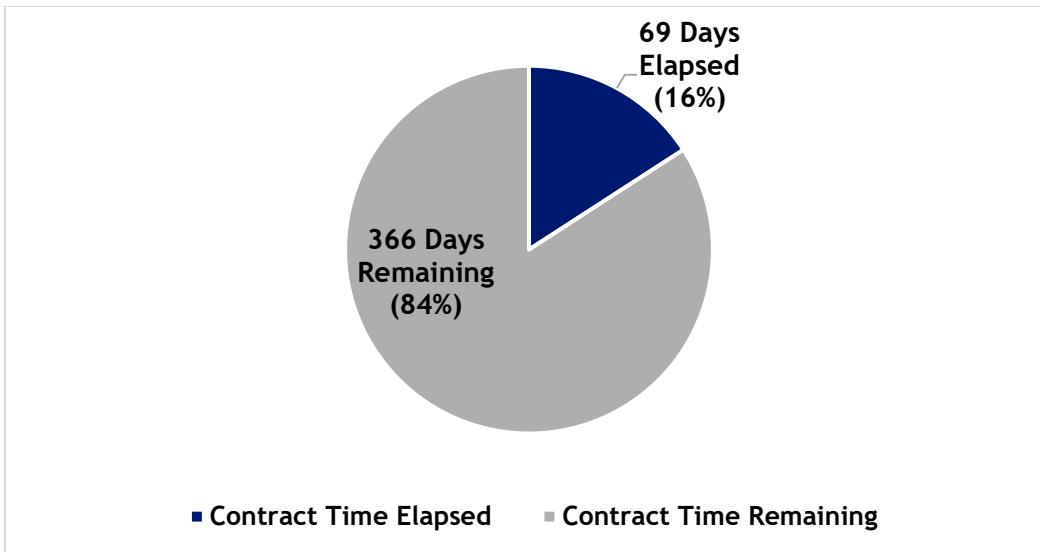

## Construction Package 3

Construction Package 3 is expected to begin in mid-August 2026 and finish by October 1, 2027. The total contract time is 412 days.

