



CO 119 Safety & Mobility CM/GC Project Dashboard for May 2026

Project Dashboard

The purpose of this document is to provide a progress and financial update pertaining to the design and construction of the CO 119 Project and the following associated project numbers:

- **Design:** Project Number 21497
- **Construction Package 1:** Project Number 25959
- **Construction Package 2:** Project Number 25960
- **Construction Package 3:** Project Number 25961


Milestone Dates

Design






Construction Package 1

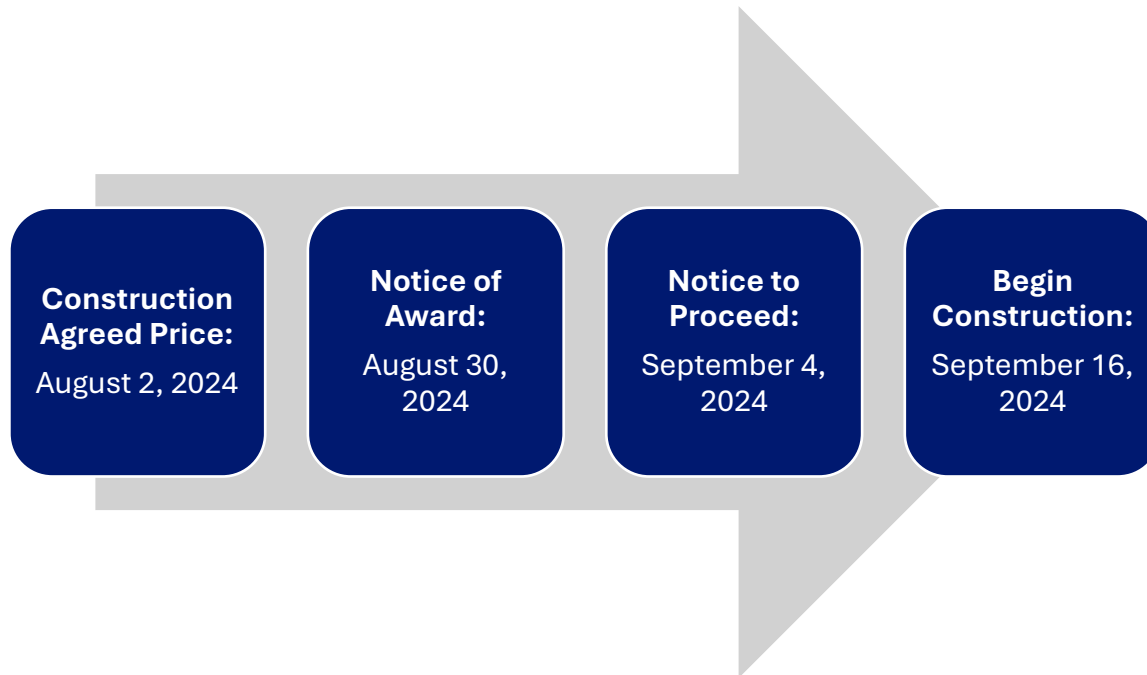


Construction Package 2

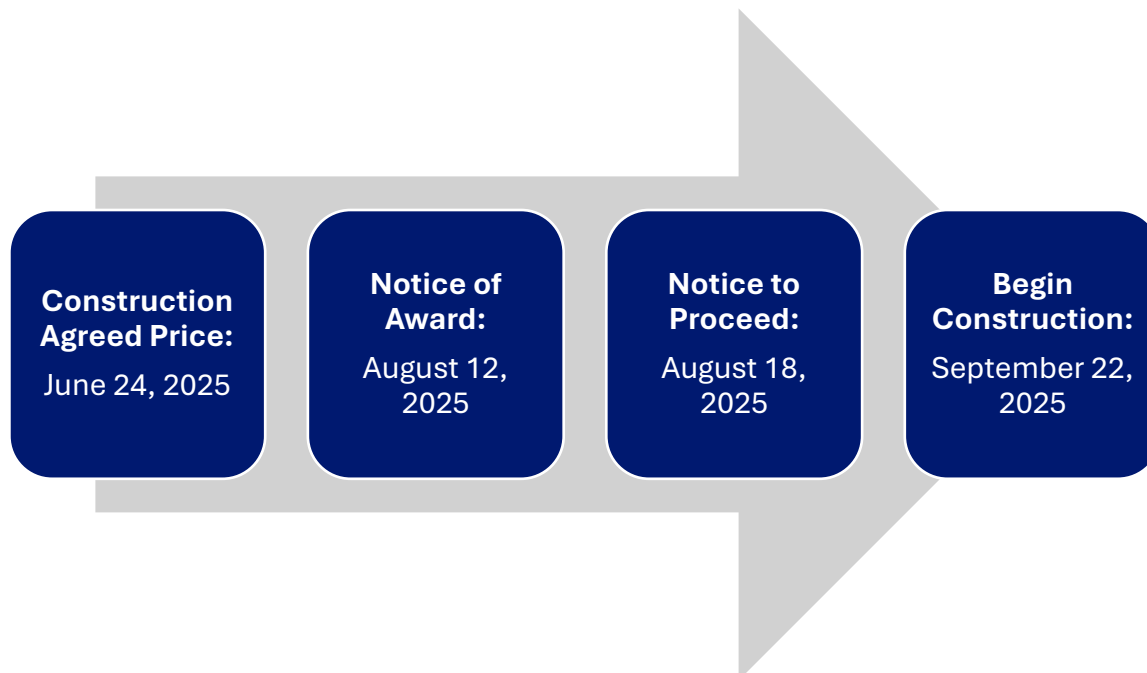




Construction Package 3

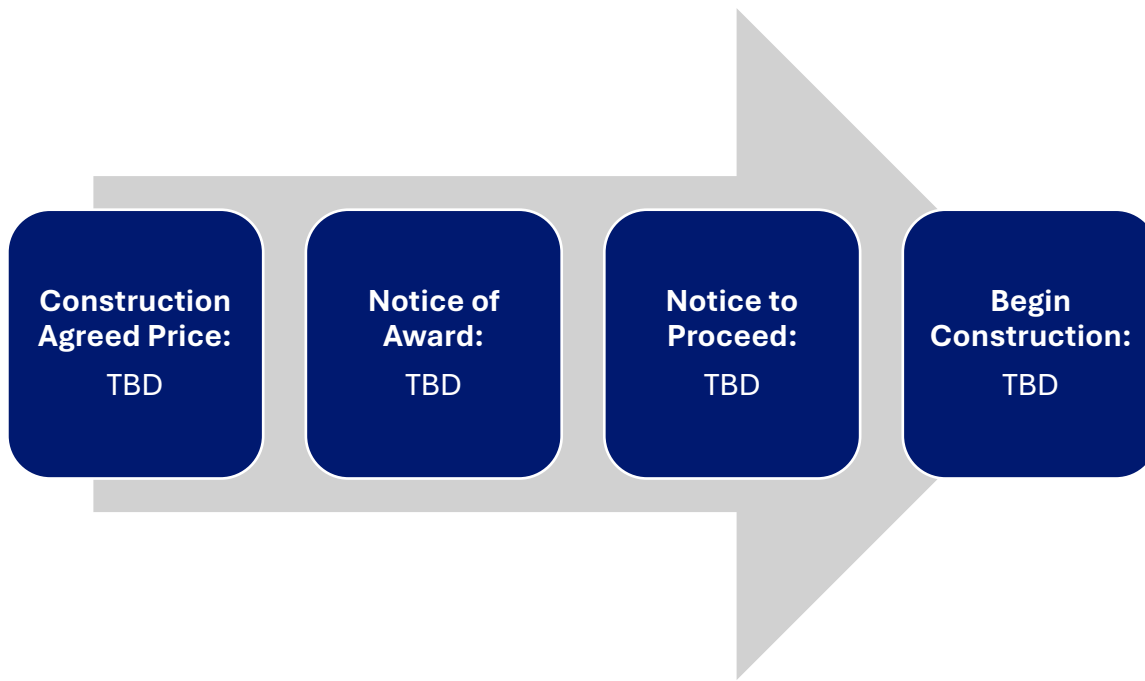

Project Progress by Percent

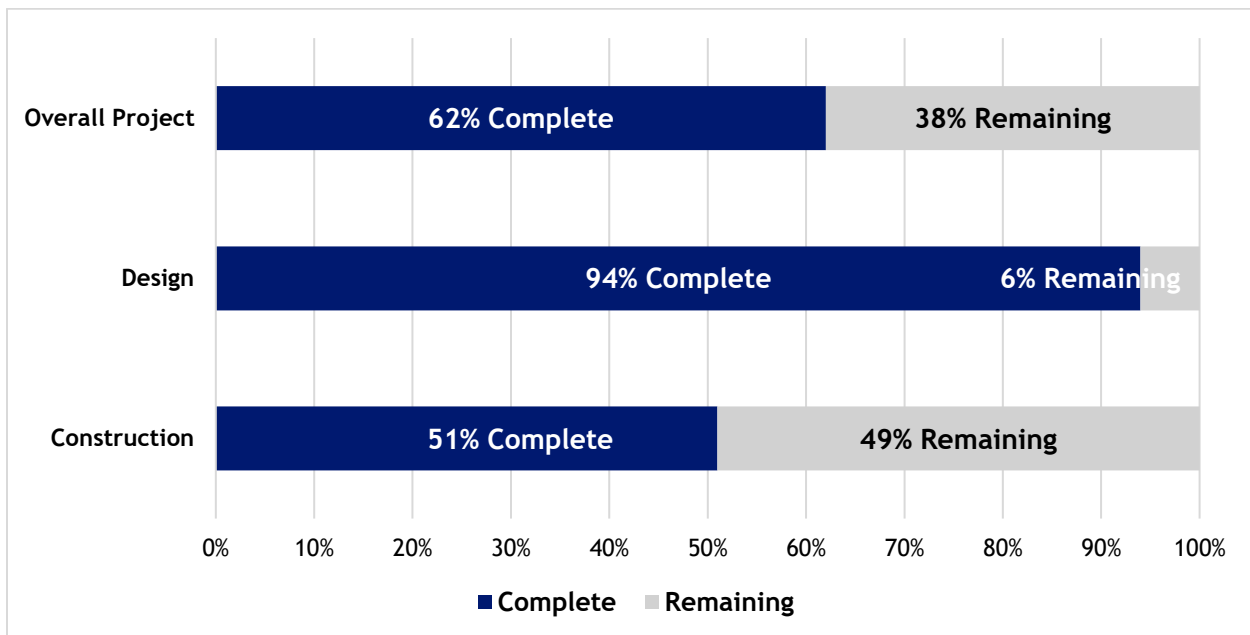




Financial Contract Information


The following bar charts display the project construction payments versus remaining funds, the current contract total, and the original contract amount for Construction Package 1, 2, and 3. Nine change orders have been approved.

Construction Package 1

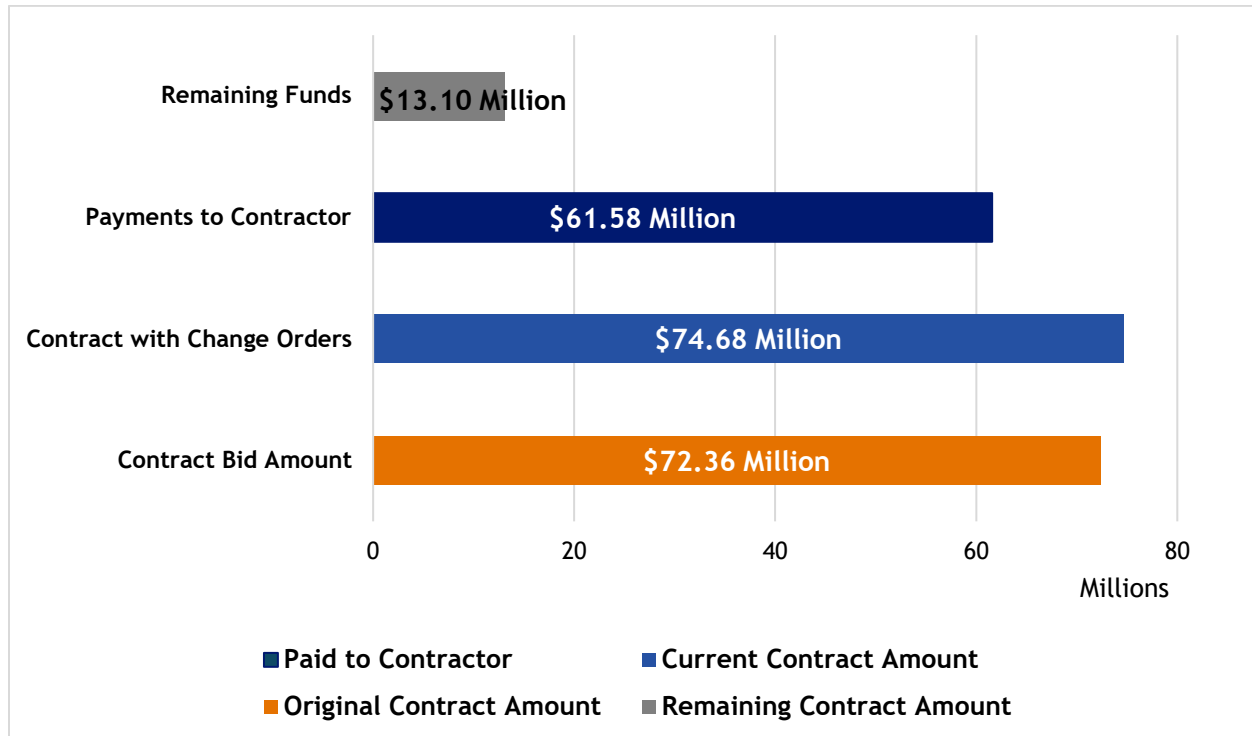




Construction Package 2

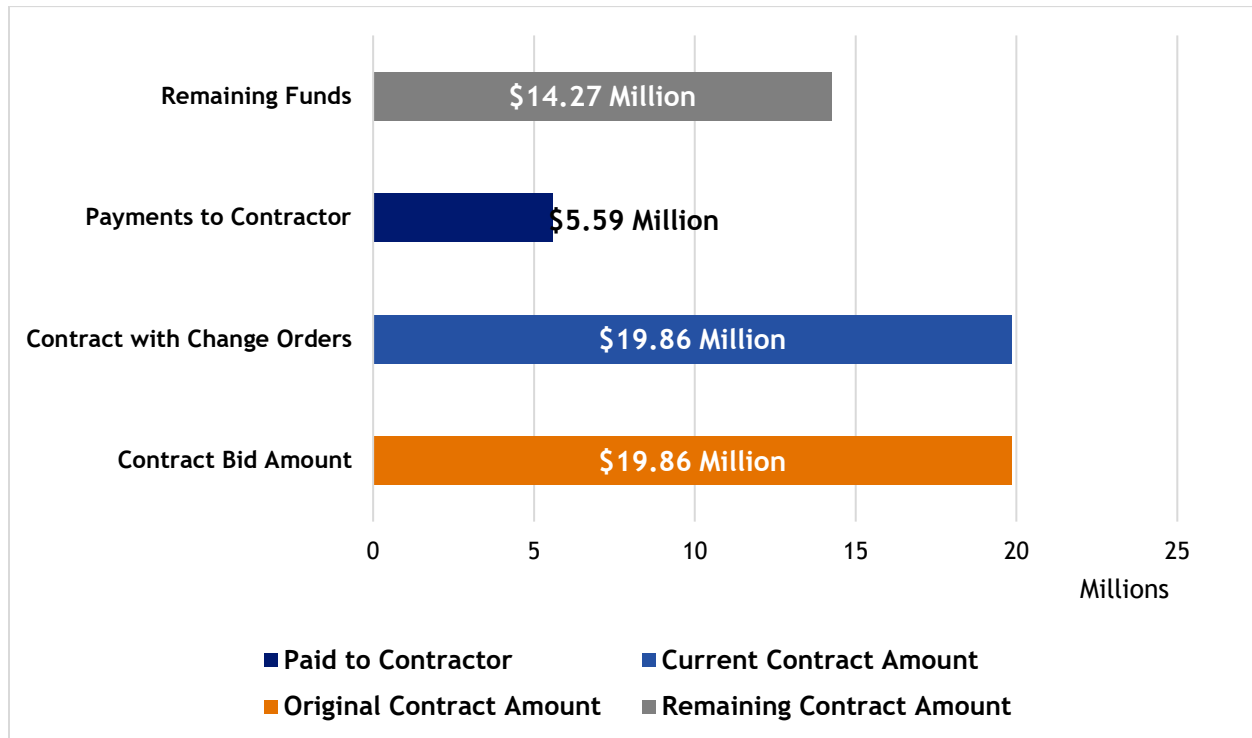

Construction Package 3






Contract Time


Design

The CMGC Preconstruction Contract was executed on October 11, 2023, and is expected to finish by February 15, 2027. The total contract time is 1,223 days.

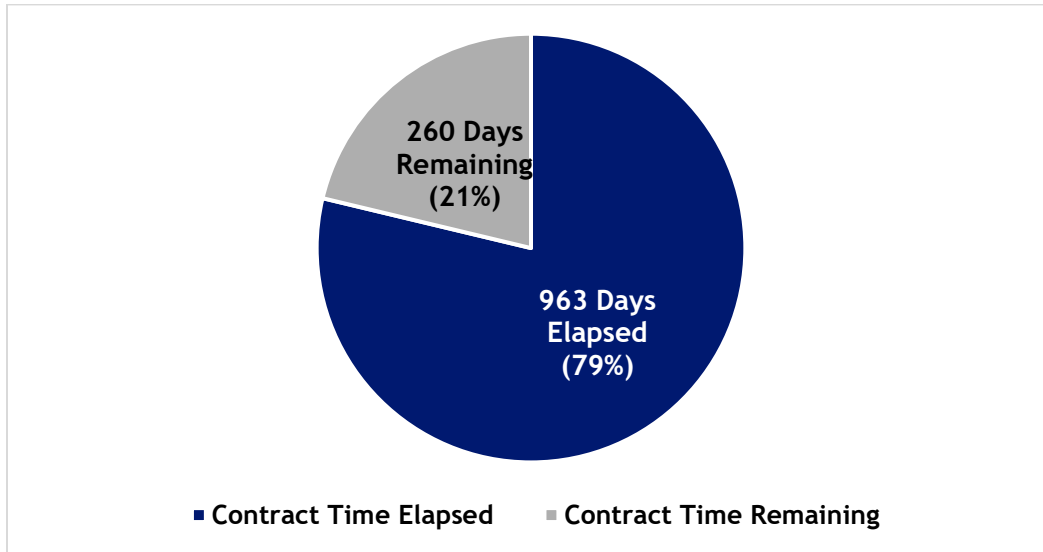

Construction Package 1


Construction for CP1 began on September 16, 2024, and is expected to finish by December 01, 2026. The total contract time is 806 days.

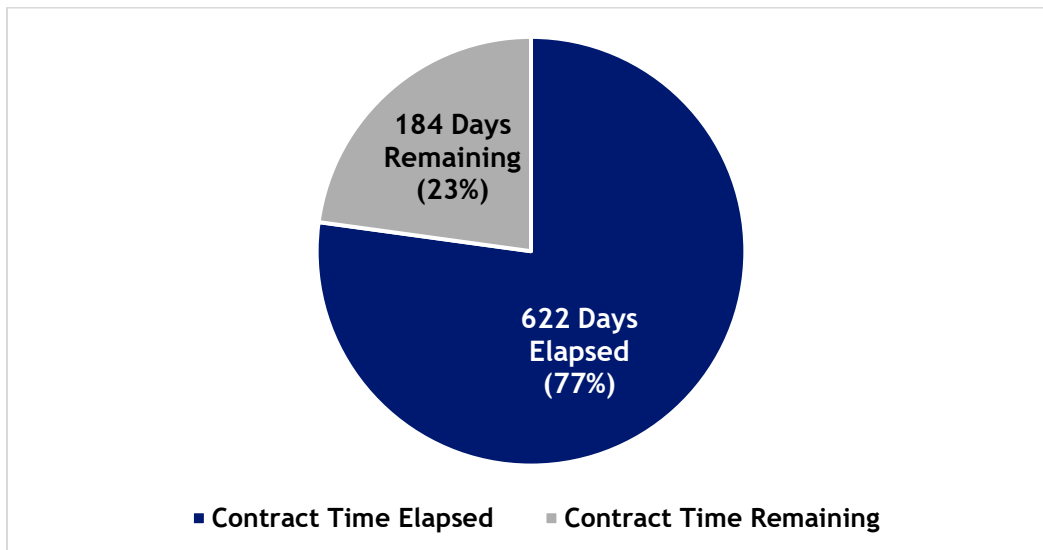



Construction Package 2

Construction Package 2 started on September 22, 2025, and is expected to finish by December 01, 2026. The total contract time is 435 days.

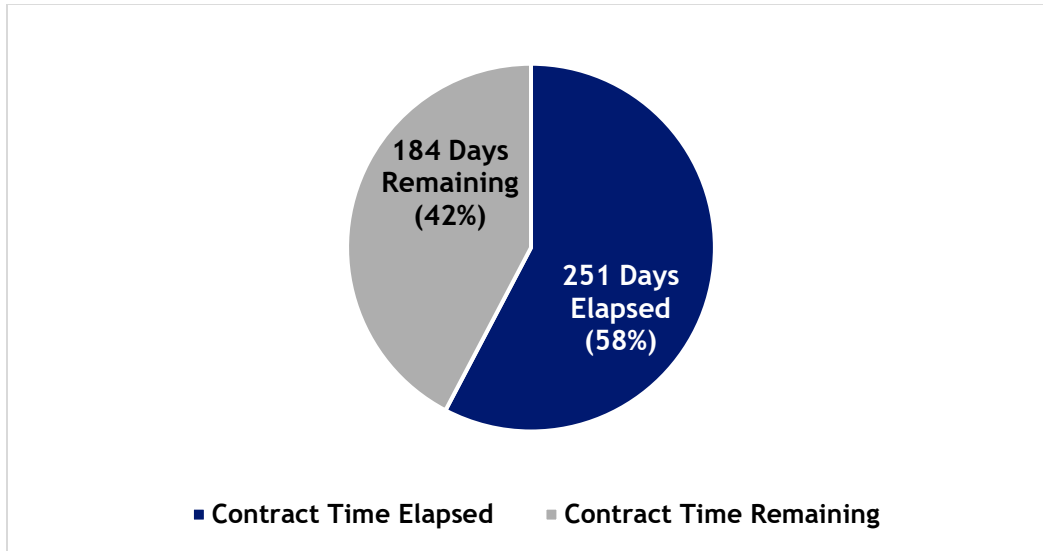

Construction Package 3

Construction Package 3 is expected to begin in late-August 2026 and finish by December 31, 2027. The total contract time is 493 days.

