


Project Name: I-70 Floyd Hill East Section
Project Number: 25174
Date: July 2025 Update

I-70 Floyd Hill East Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

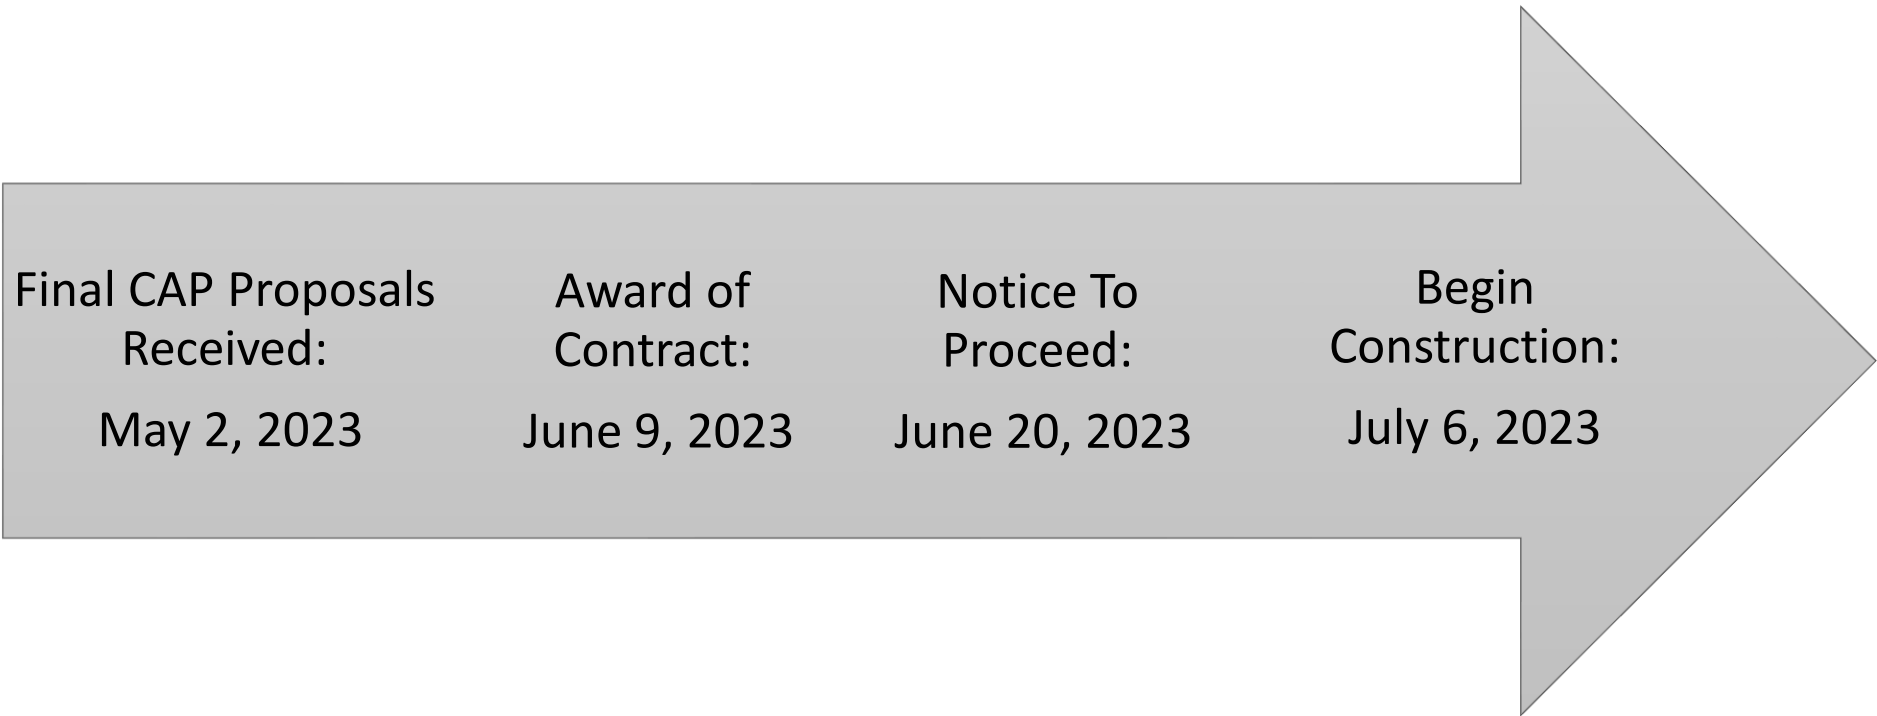

Final CAP Proposals Received: May 2, 2023
Award of Contract: June 9, 2023
Notice To Proceed: June 20, 2023
Begin Construction: July 6, 2023


Project Name: I-70 Floyd Hill East Section

Project Number: 25174

Date: July 2025 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

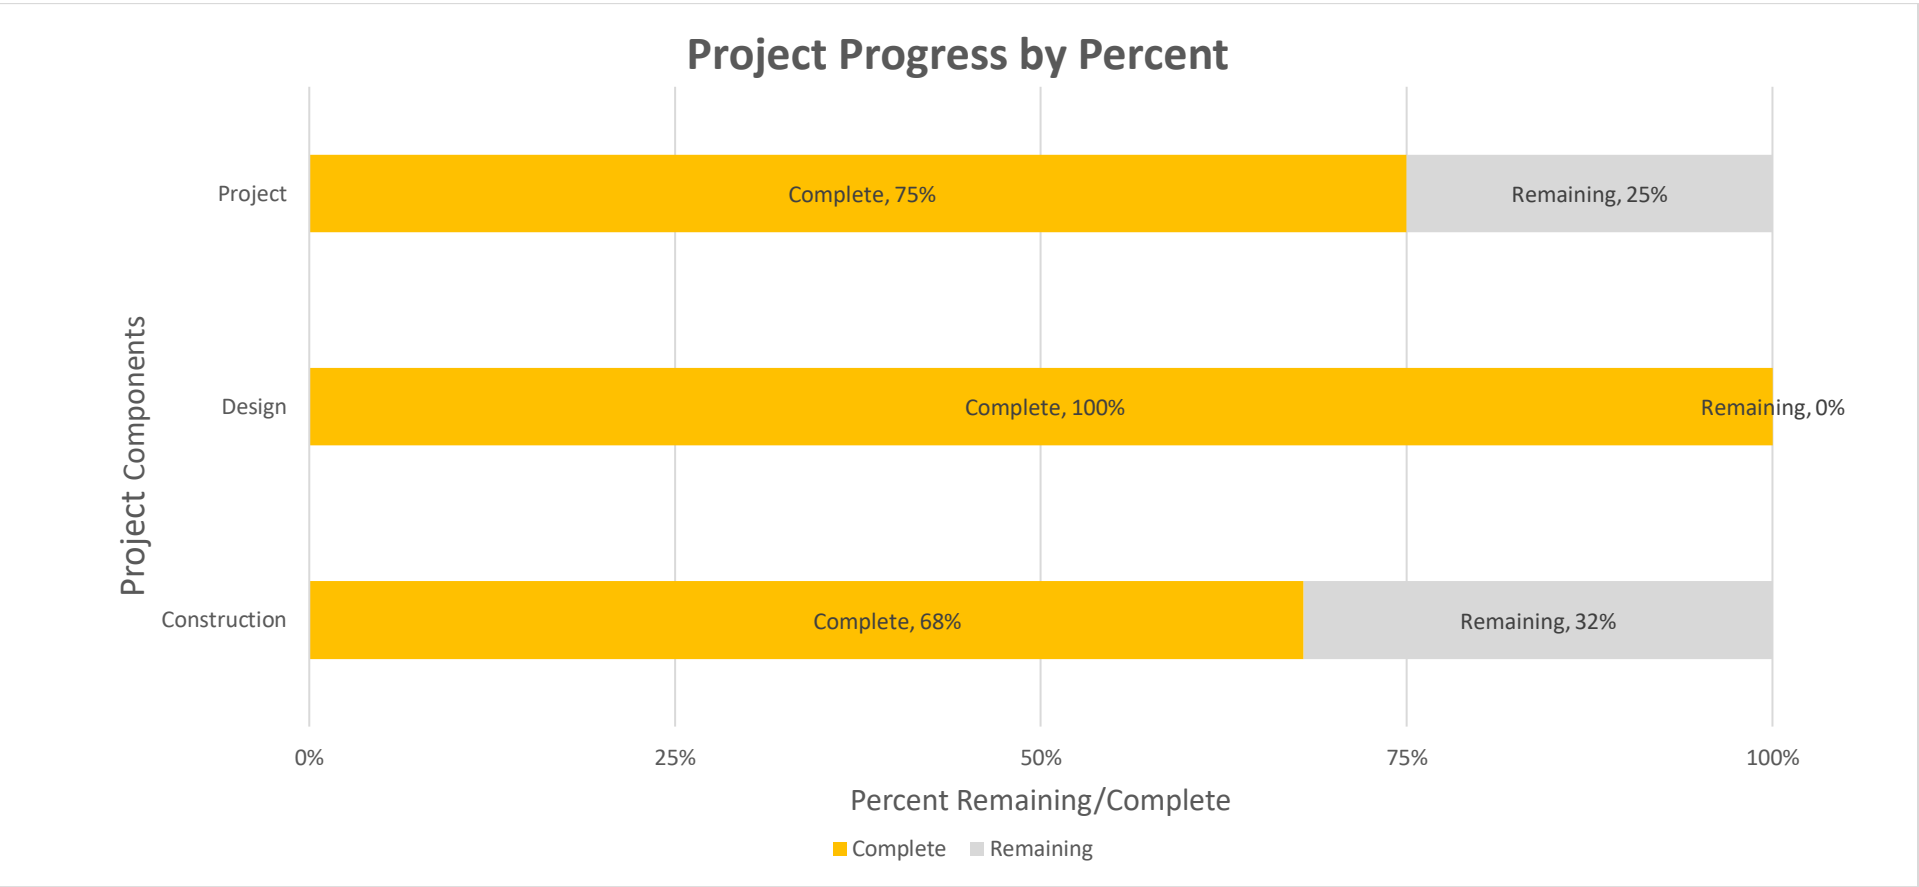

Overall Project: 75% Complete, 25% Remaining

Design: 100% Complete, 0% Remaining

Construction: 68% Complete, 32% Remaining


Project Name: I-70 Floyd Hill East Section

Project Number: 25174

Date: July 2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

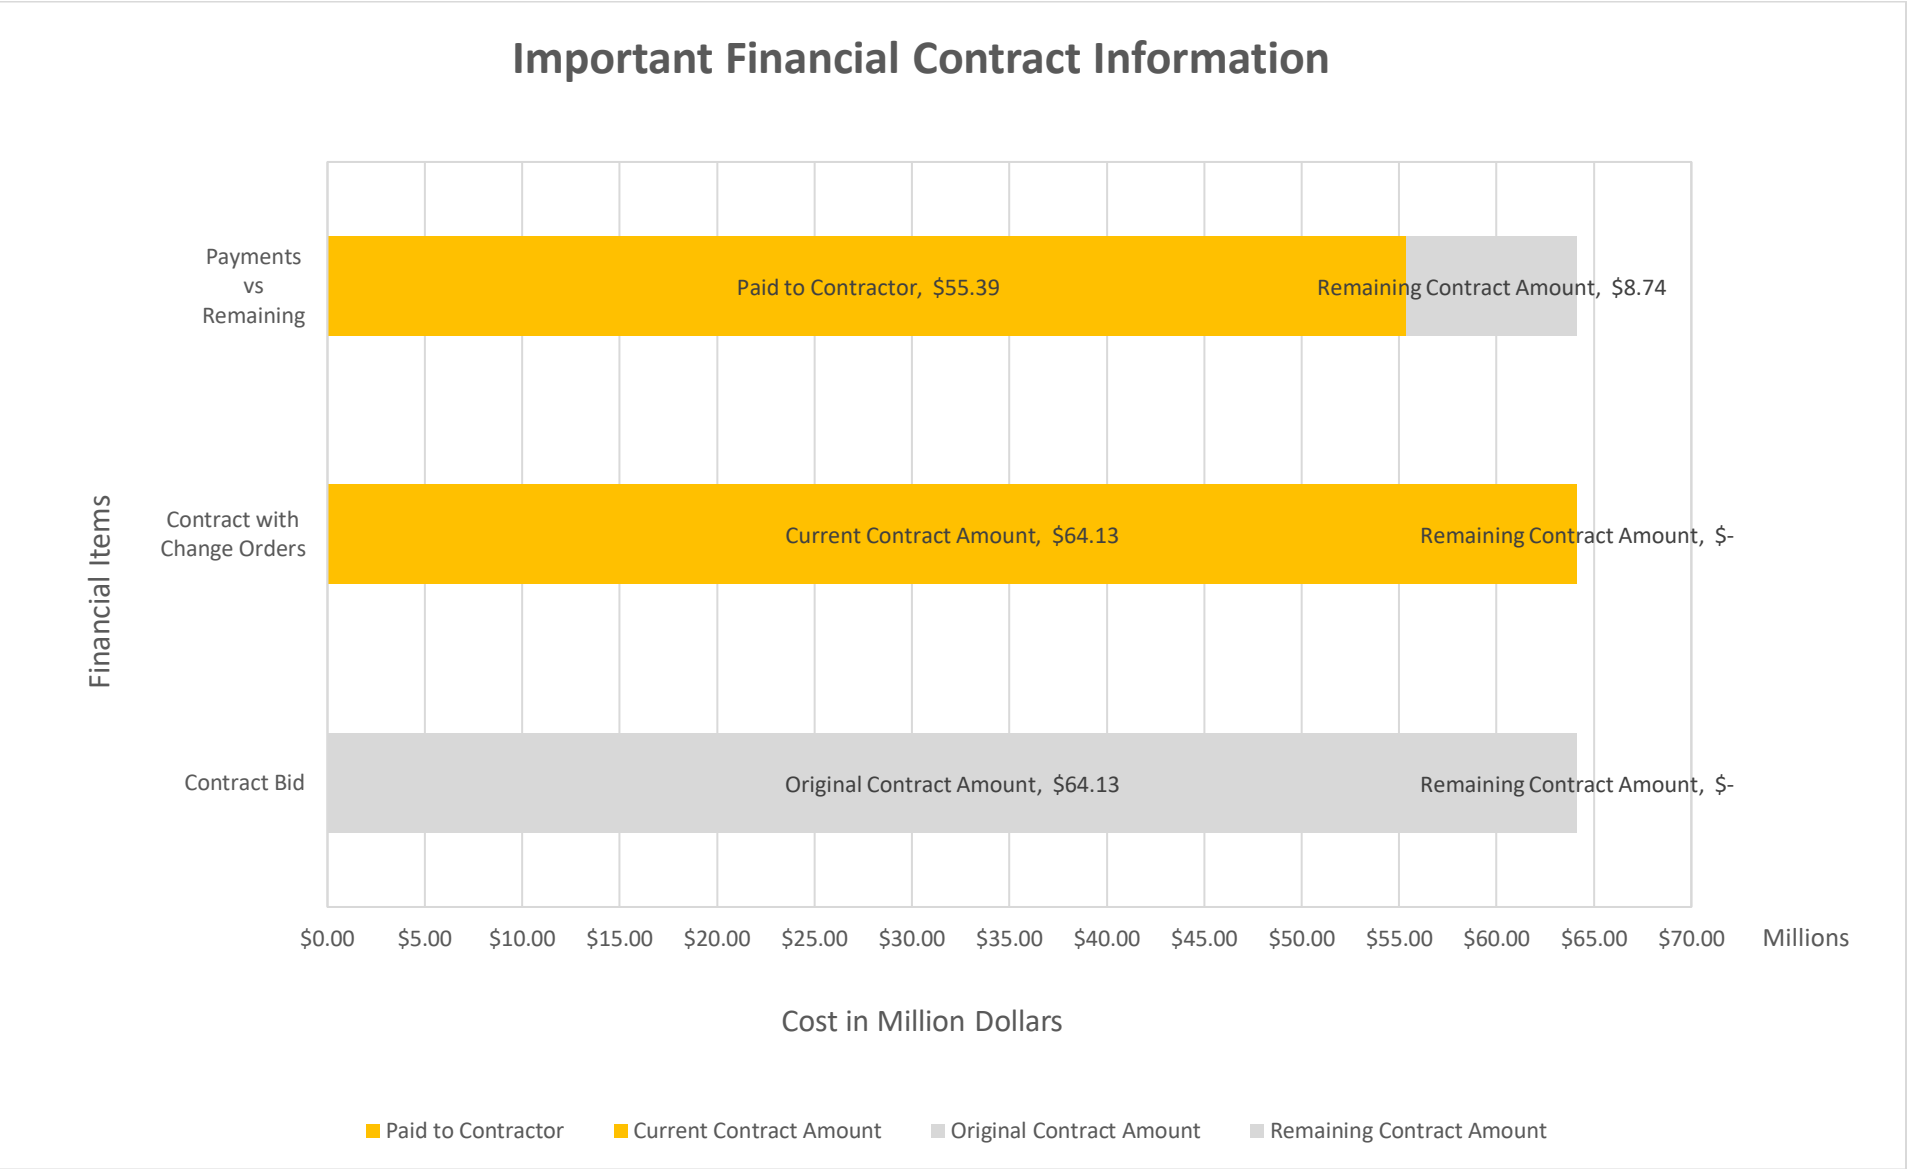

Initial Contract Value: \$64.13 Million


Payments to date: \$55.39 Million, Payments remaining \$8.74 Million

Current Contract Value: \$64.13 Million, Total Change Orders to Date: \$0

Project Name: I-70 Floyd Hill East Section
Project Number: 25174
Date: July 2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

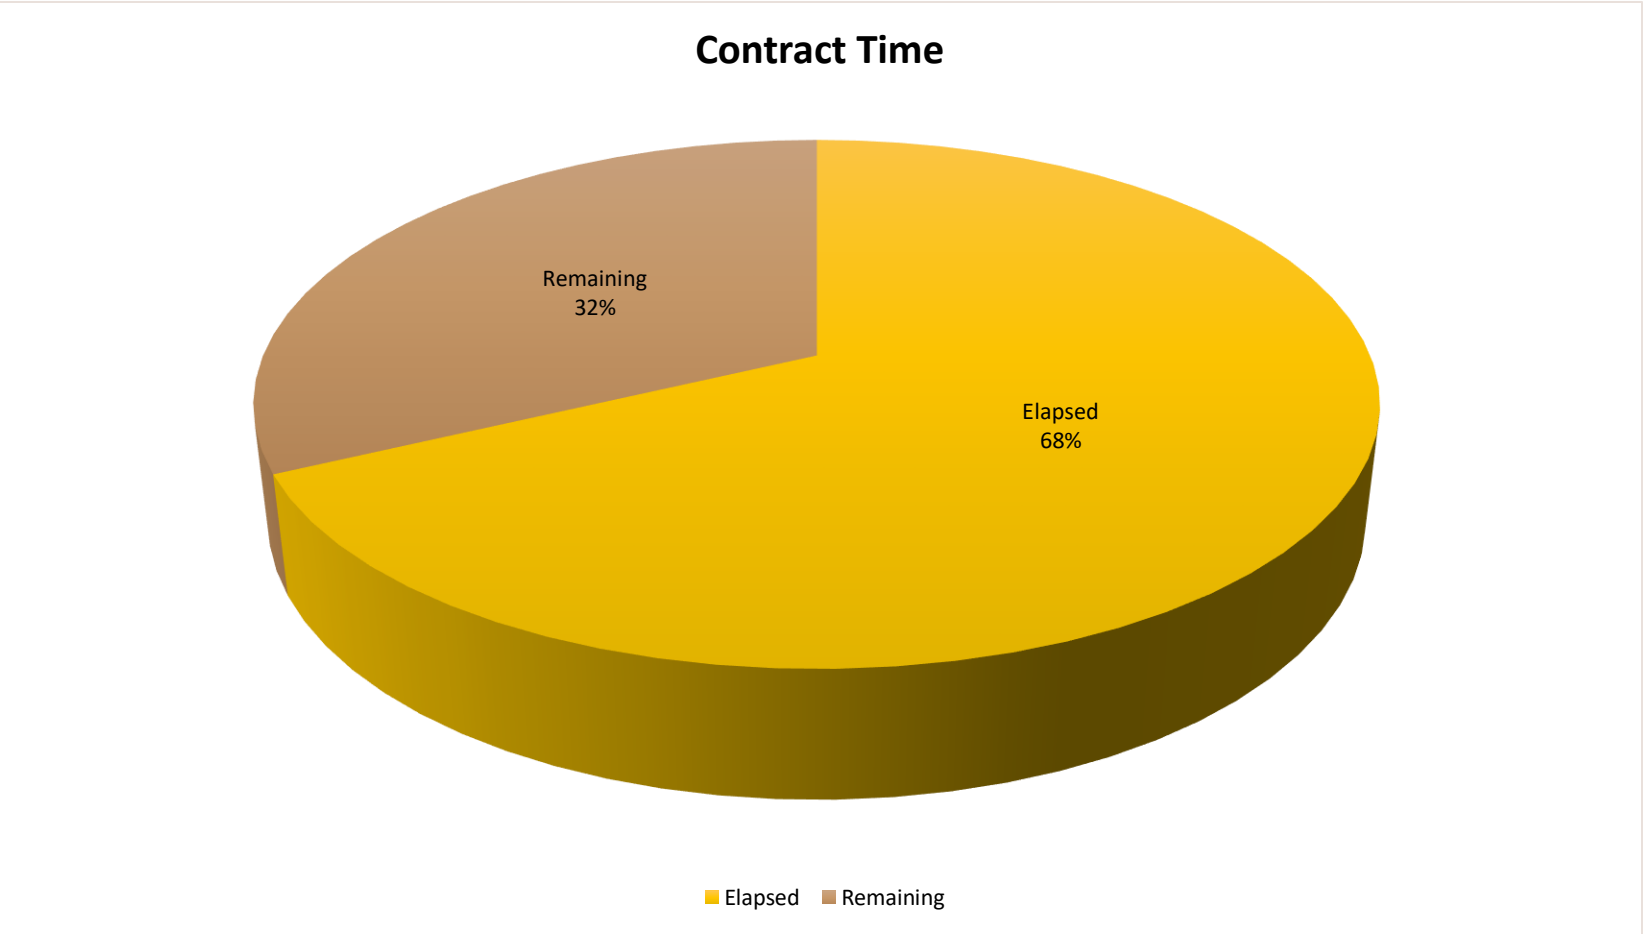

Total Contract time: 1136 Calendar Days

Elapsed Contact time: 772 days, 68%

Contract Time Remaining: 364 days, 32%
