


Project Name: I-70 Floyd Hill West Section  
Project Number: 25175  
Date: October 2023 Update

## I-70 Floyd Hill West Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

### Key Dates

The following image shows the progression of the key project dates.

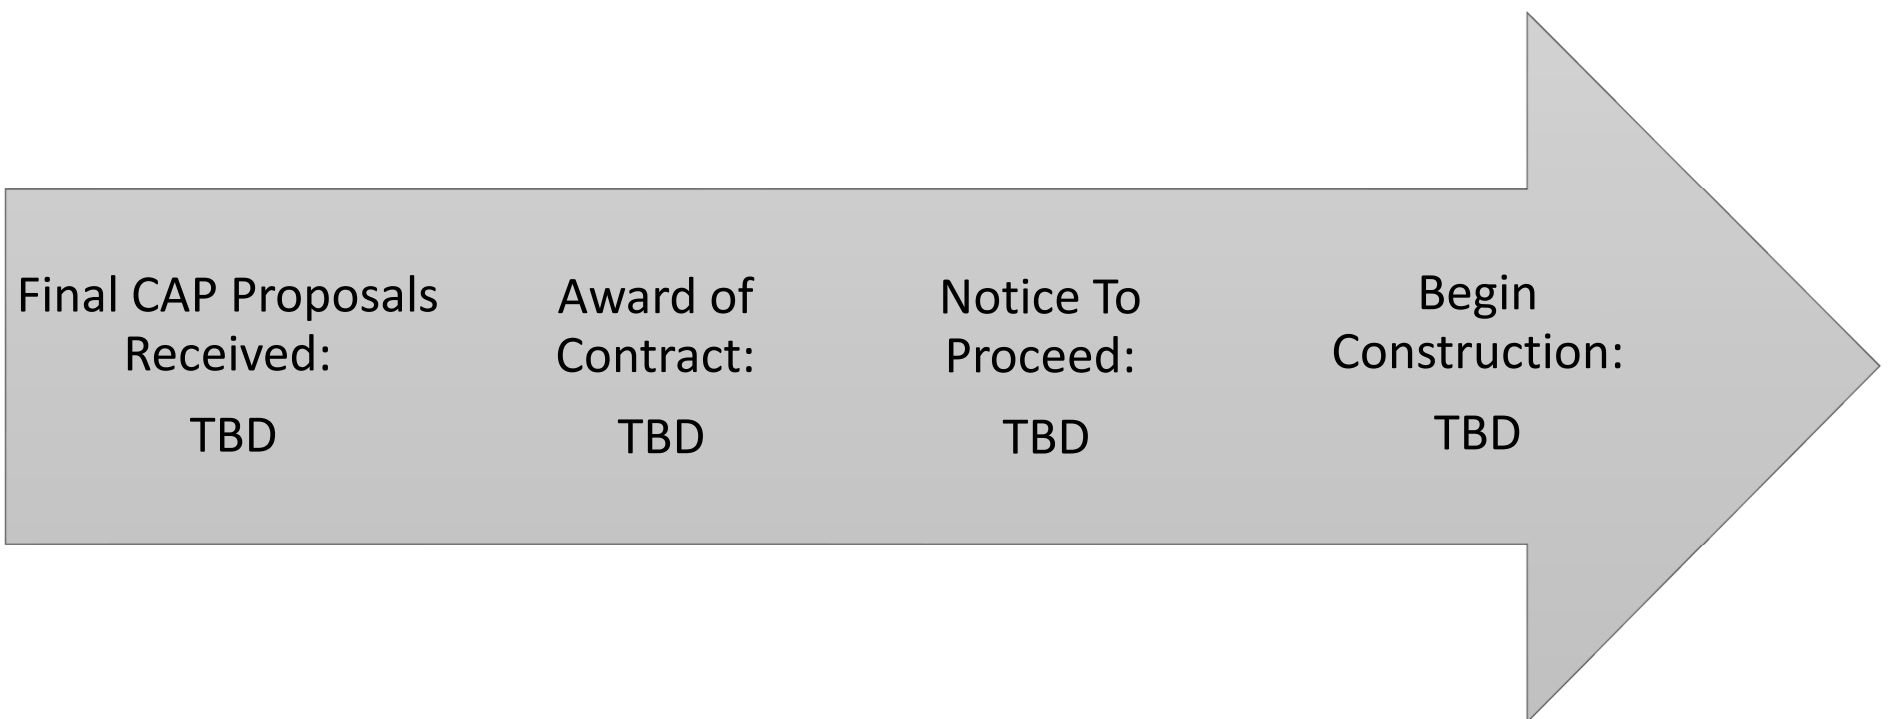

Final CAP Proposals Received: TBD

Award of Contract: TBD


Notice To Proceed: TBD

Begin Construction: TBD

Project Name: I-70 Floyd Hill West Section  
 Project Number: 25175  
 Date: October 2023 Update

### Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

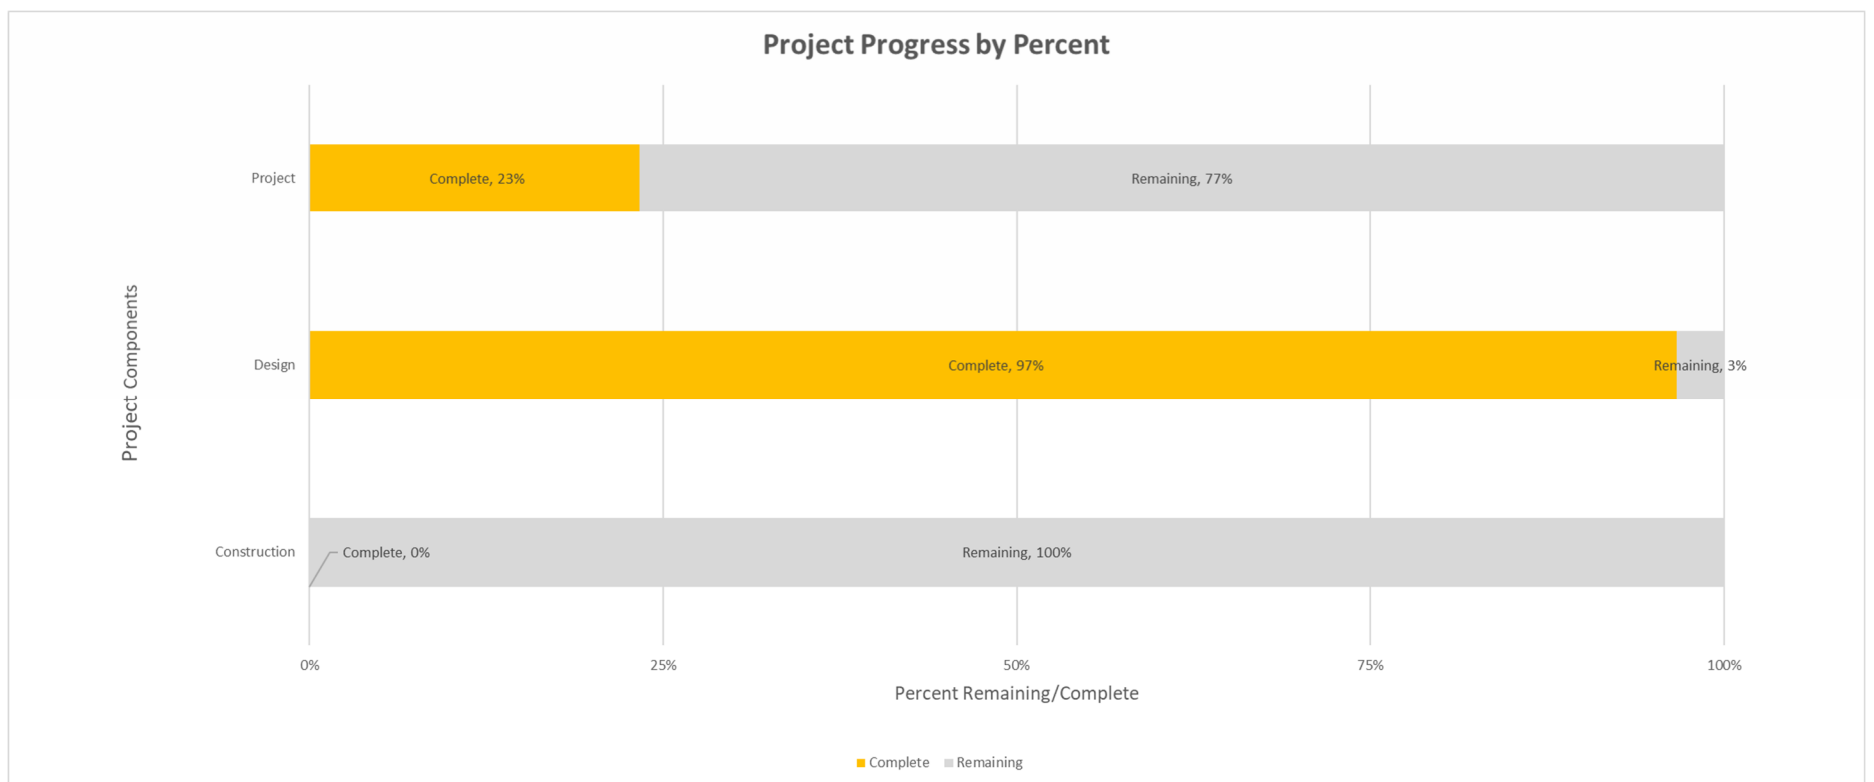

Overall Project: 23% Complete, 77% Remaining

Design: 97% Complete, 3% Remaining

Construction: 0% Complete, 100% Remaining




Project Name: I-70 Floyd Hill West Section

Project Number: 25175

Date: October 2023 Update

**Important Financial Contract Information**

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

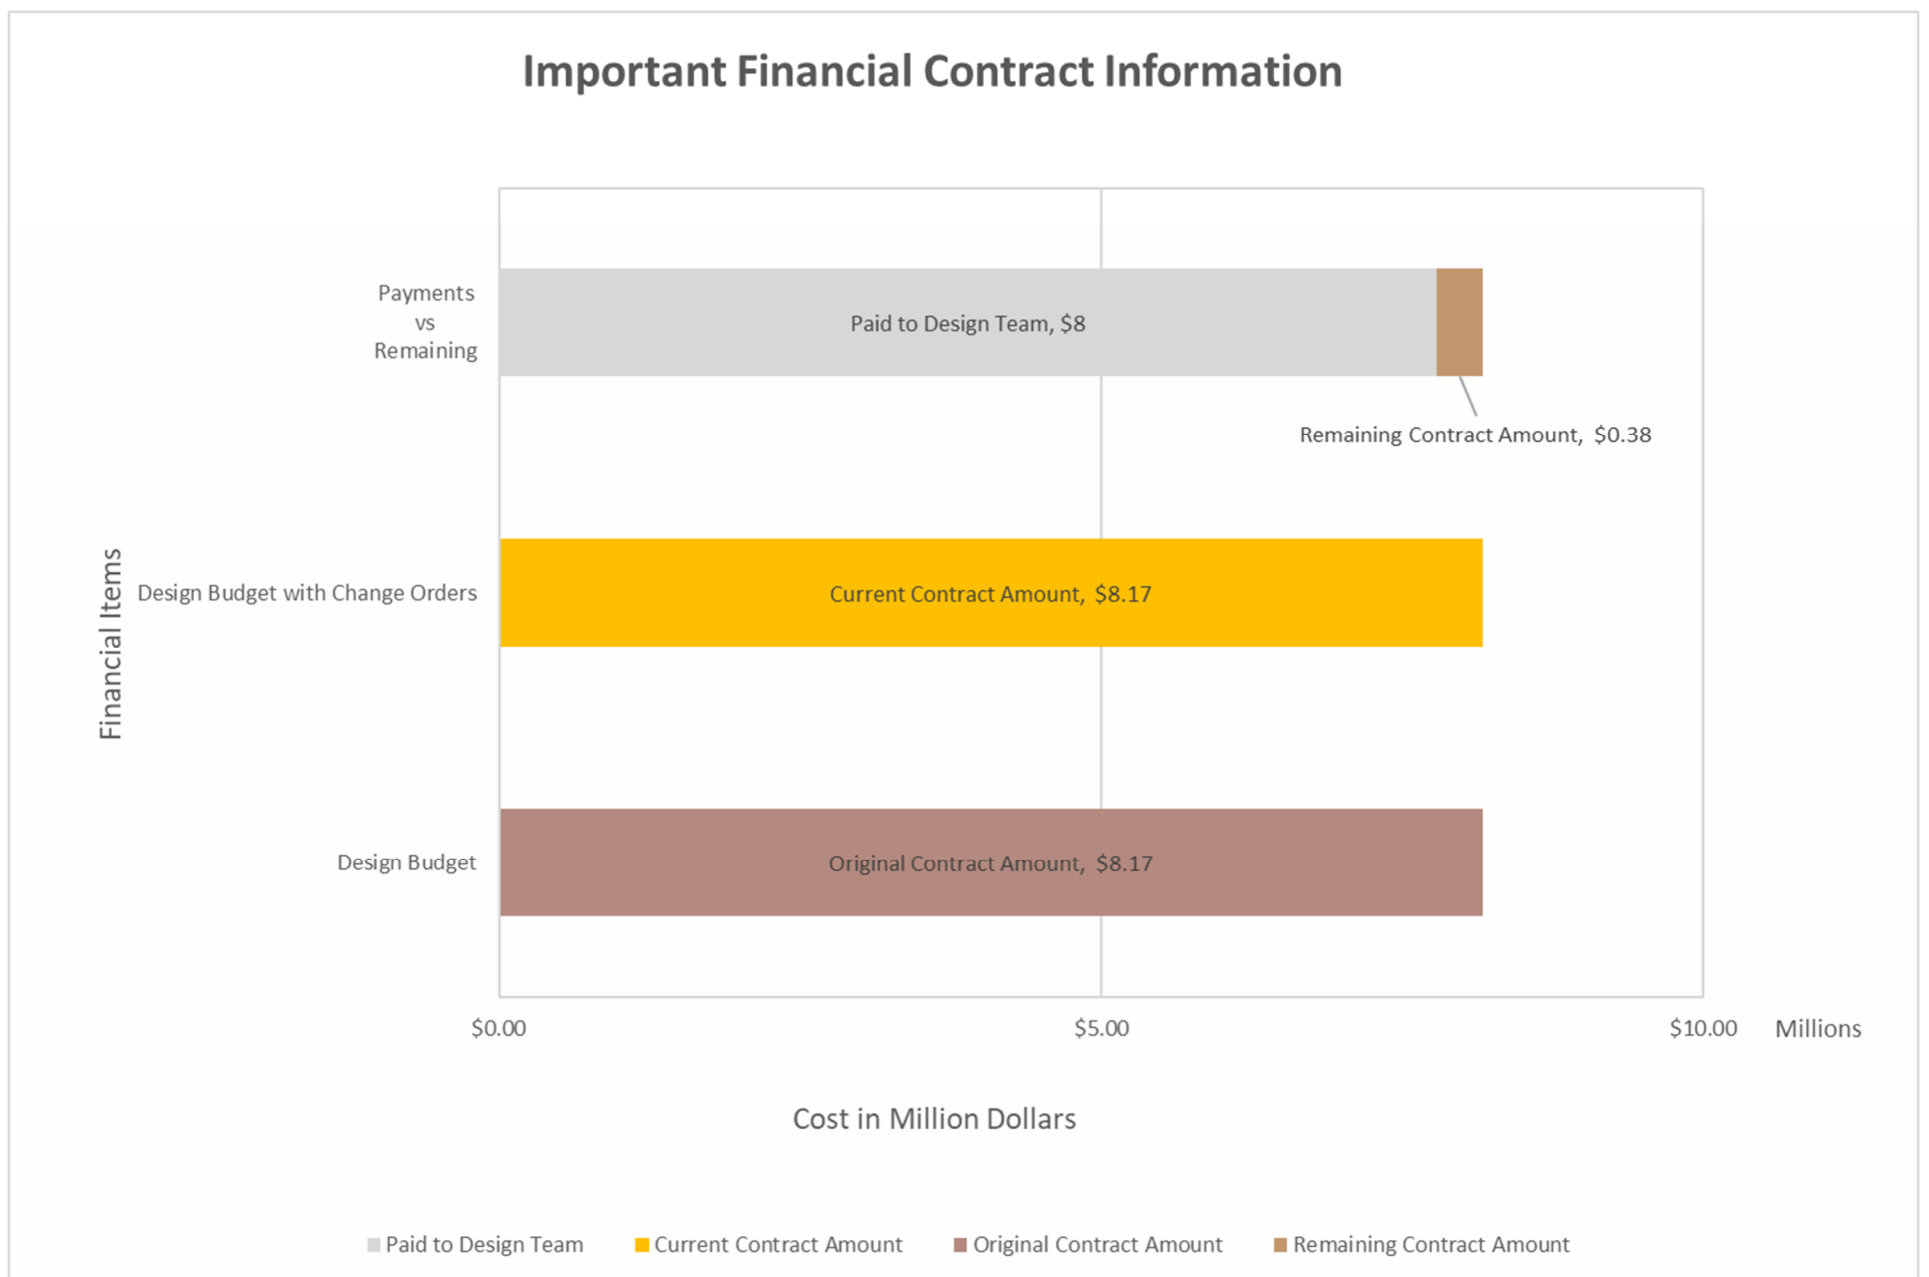

Initial Design Contract Value: \$8.17 Million

Design Payments to date: \$7.79 Million, Design Payments remaining: \$0.38 Million

Current Contract Value: \$8.17 Million, Total Change Orders to Date: \$0


Project Name: I-70 Floyd Hill West Section

Project Number: 25175

Date: October 2023 Update

### Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

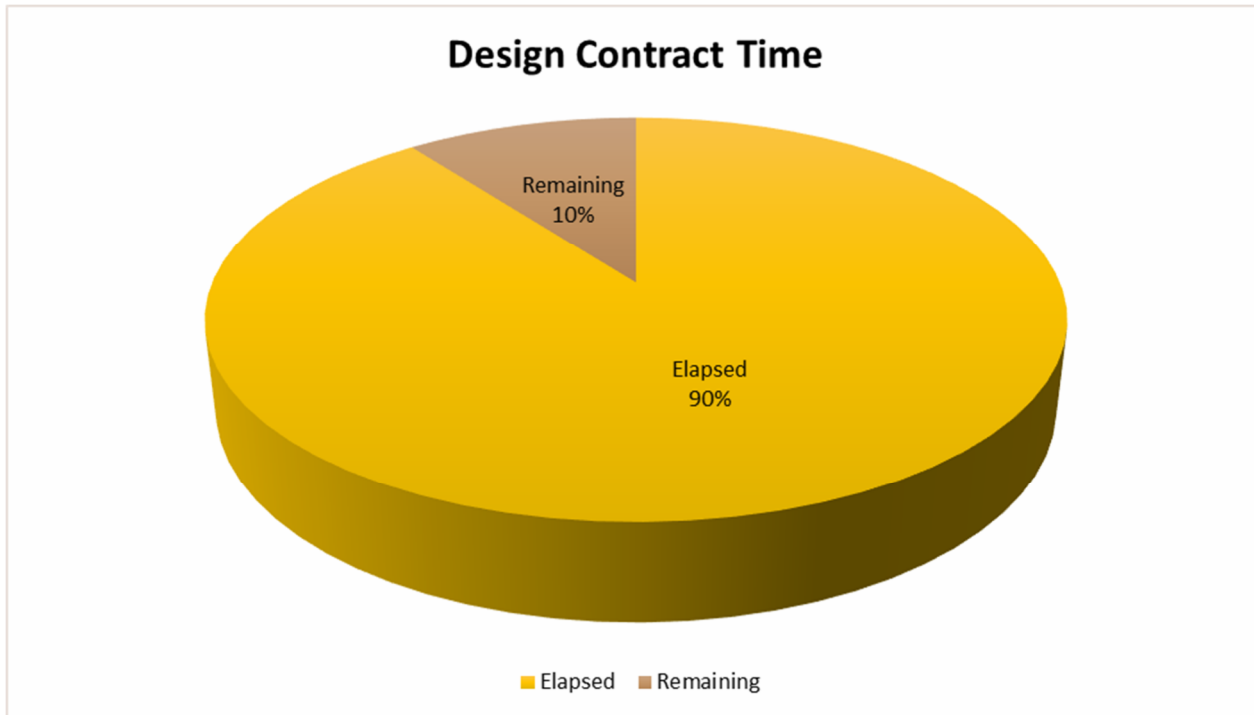

Total Design Contract time: 414 days

Elapsed Contact time: 369 days, 93%

Contract Time Remaining: 45 days ,7%
