


Project Name: I-70 Floyd Hill Central Section
Project Number: 25177
Date: February 2025 Update

I-70 Floyd Hill Central Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.



Final CAP Proposals Received: TBD
Award of Contract: TBD
Notice To Proceed: TBD
Begin Construction: TBD


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: February 2025 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

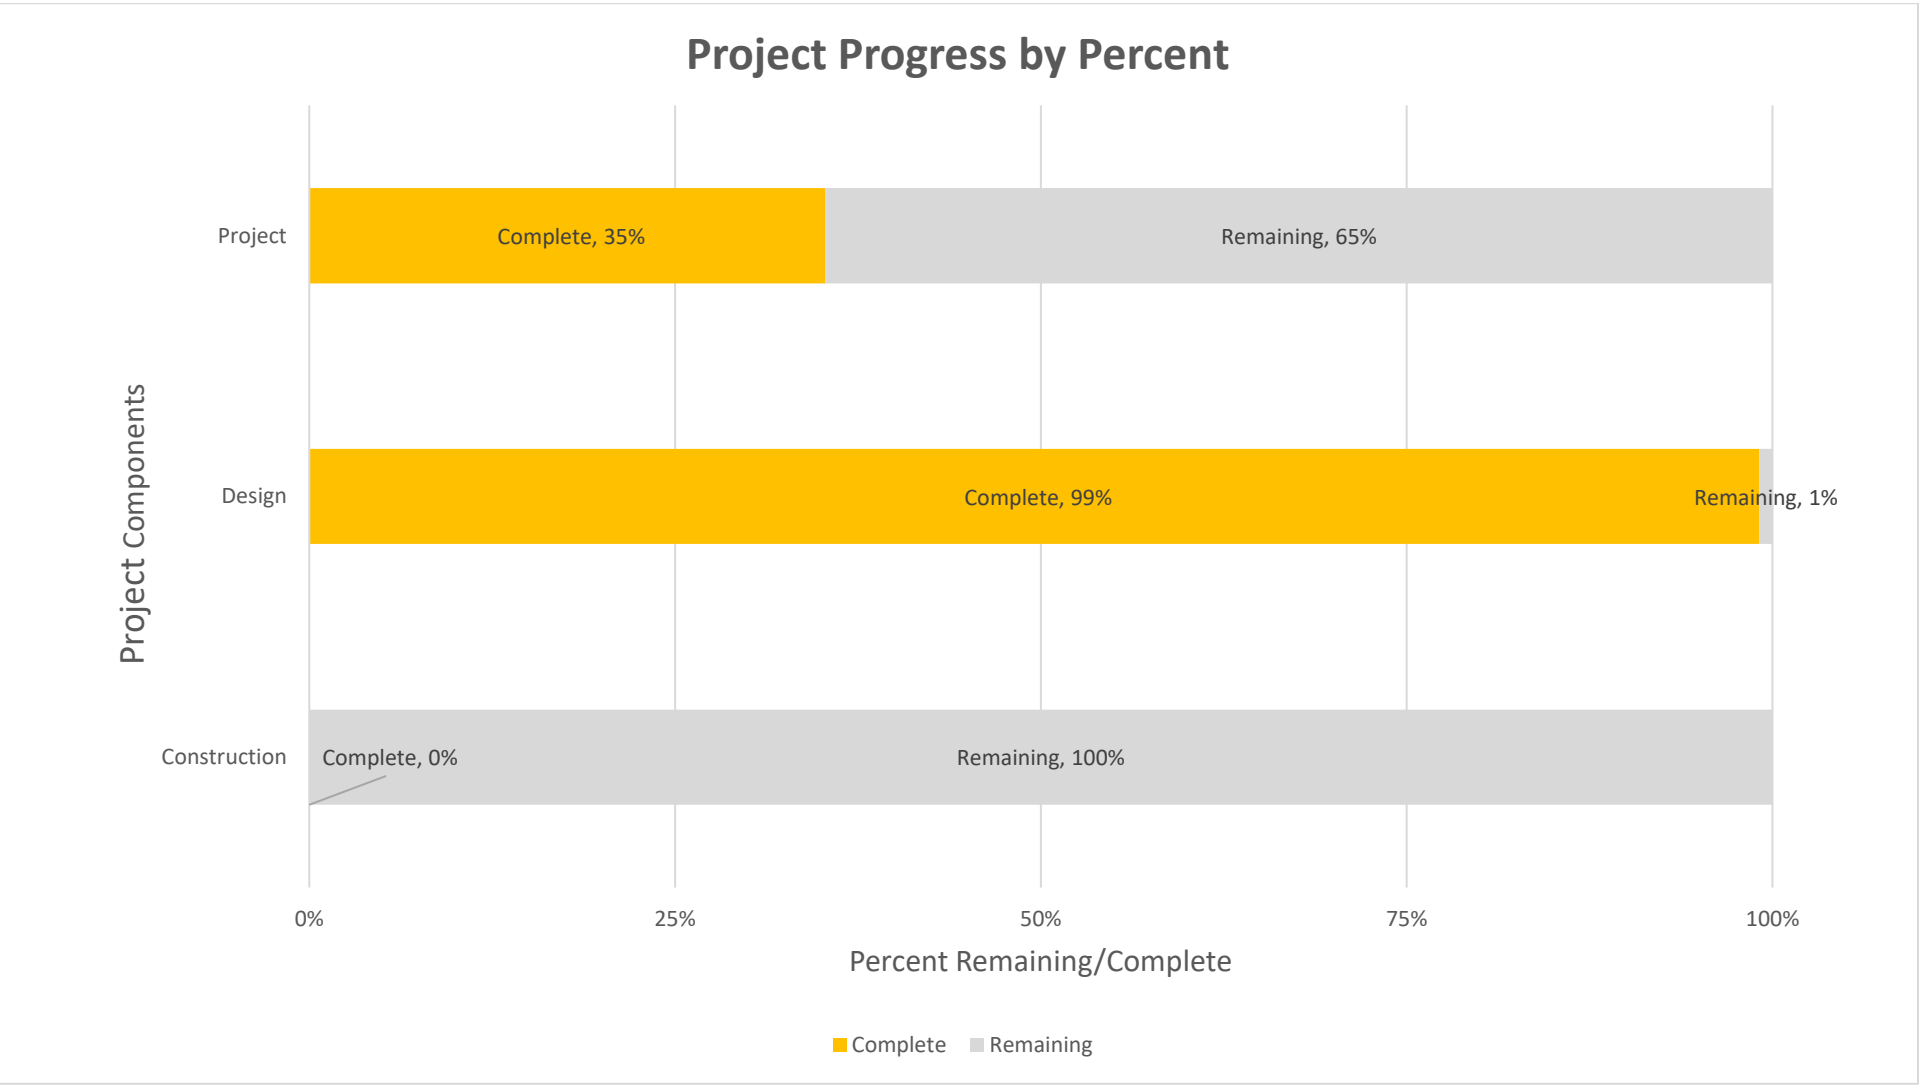

Overall Project: 29% Complete, 71% Remaining

Design: 85% Complete, 15% Remaining

Construction: 0% Complete, 100% Remaining


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: February 2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

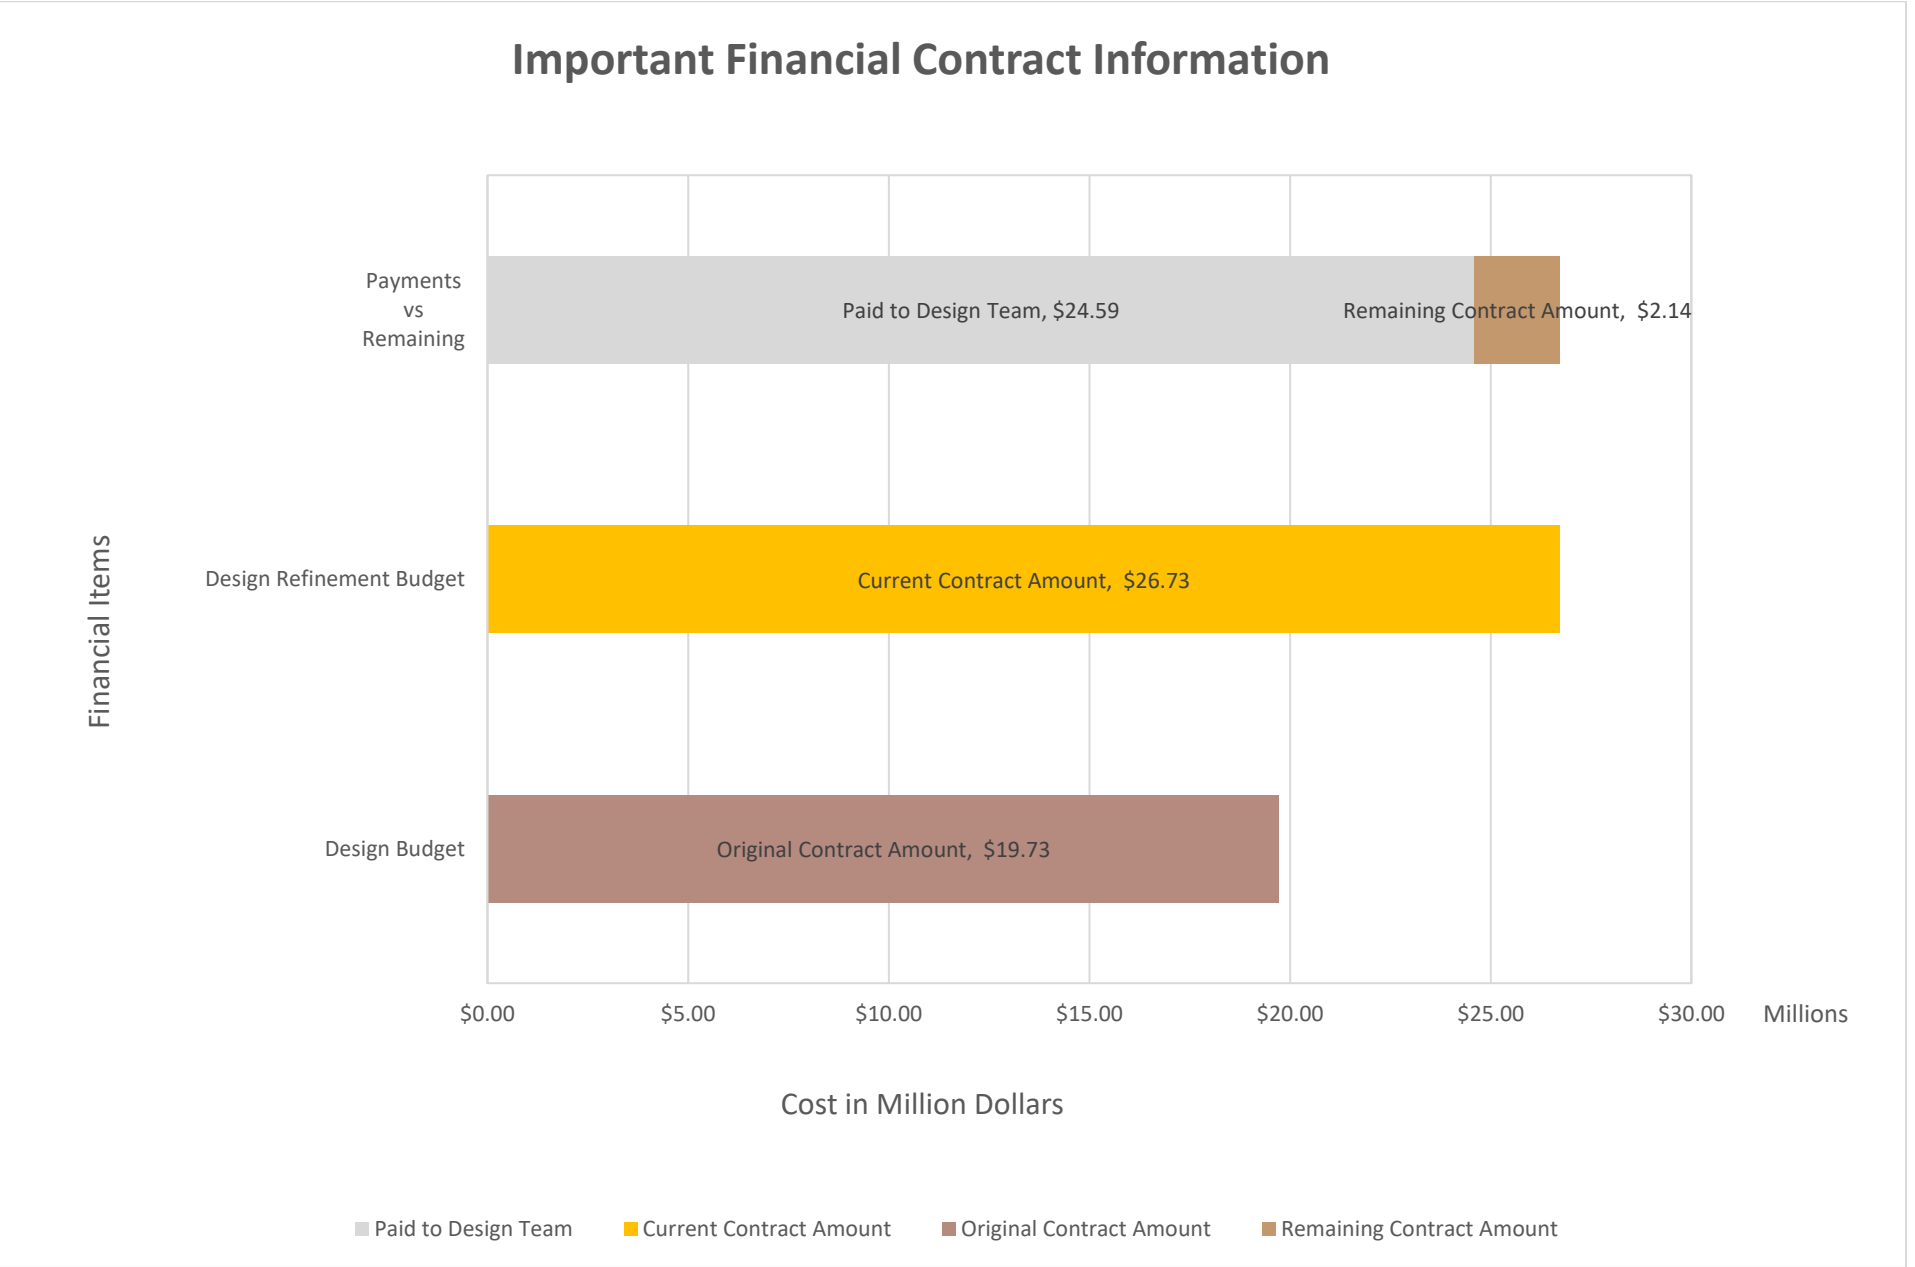

Initial Design Contract Value: \$19.73 Million


Design Payments to date: \$24.59 Million, Payments remaining \$2.14 Million

Current Design Contract Value: \$26.73 Million, Total Change Orders to Date: \$7 Million

Project Name: I-70 Floyd Hill Central Section
Project Number: 25177
Date: February 2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

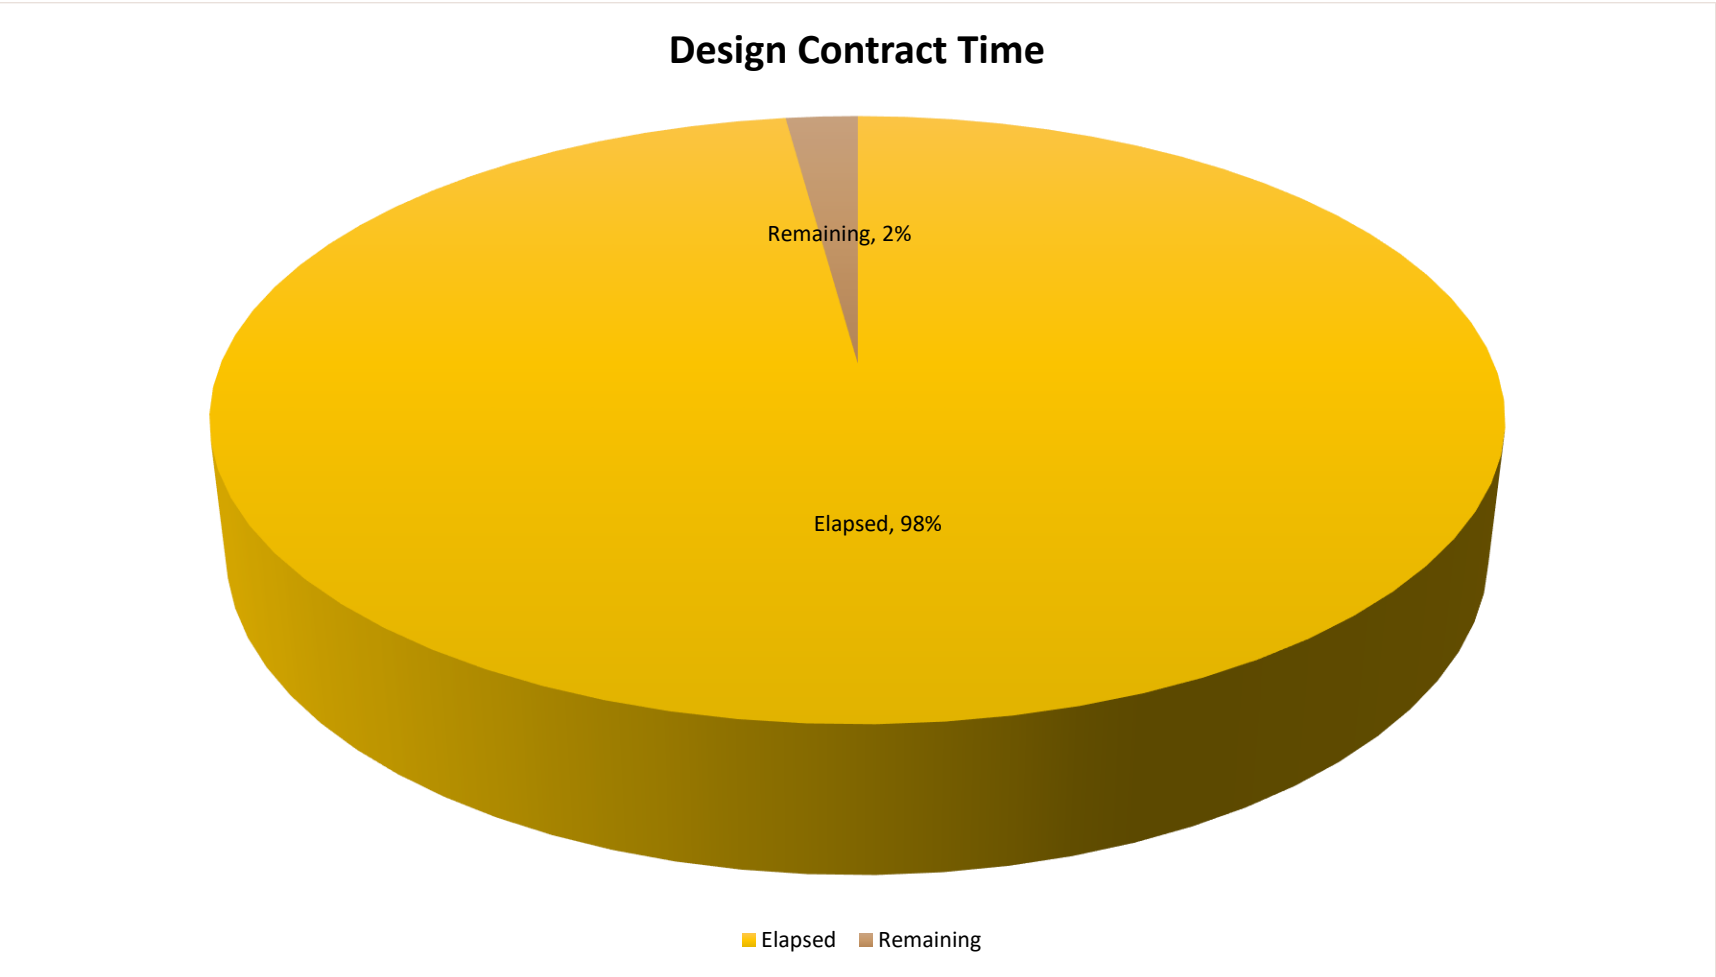

Total Design Contract time: 653 days
Elapsed Design Contact time: 639 days, 98%
Design Contract Time Remaining: 14 days, 2%
