


Project Name: I-70 Floyd Hill Central Section  
Project Number: 25177  
Date: October 2023 Update

## I-70 Floyd Hill Central Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

### Key Dates

The following image shows the progression of the key project dates.

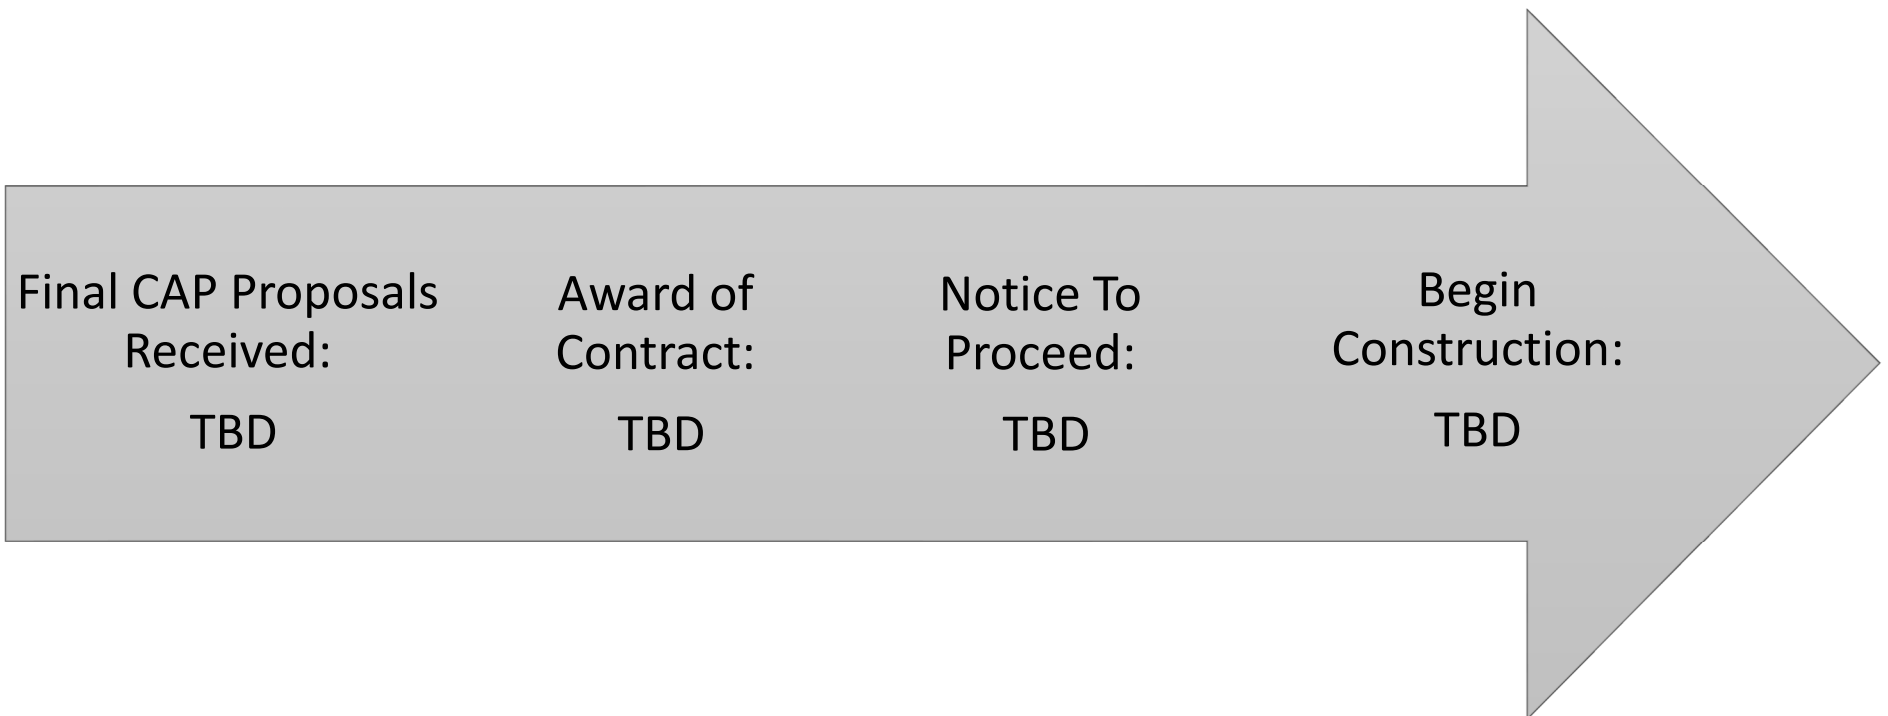

Final CAP Proposals Received: TBD

Award of Contract: TBD

Notice To Proceed: TBD

Begin Construction: TBD




Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: October 2023 Update

## Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

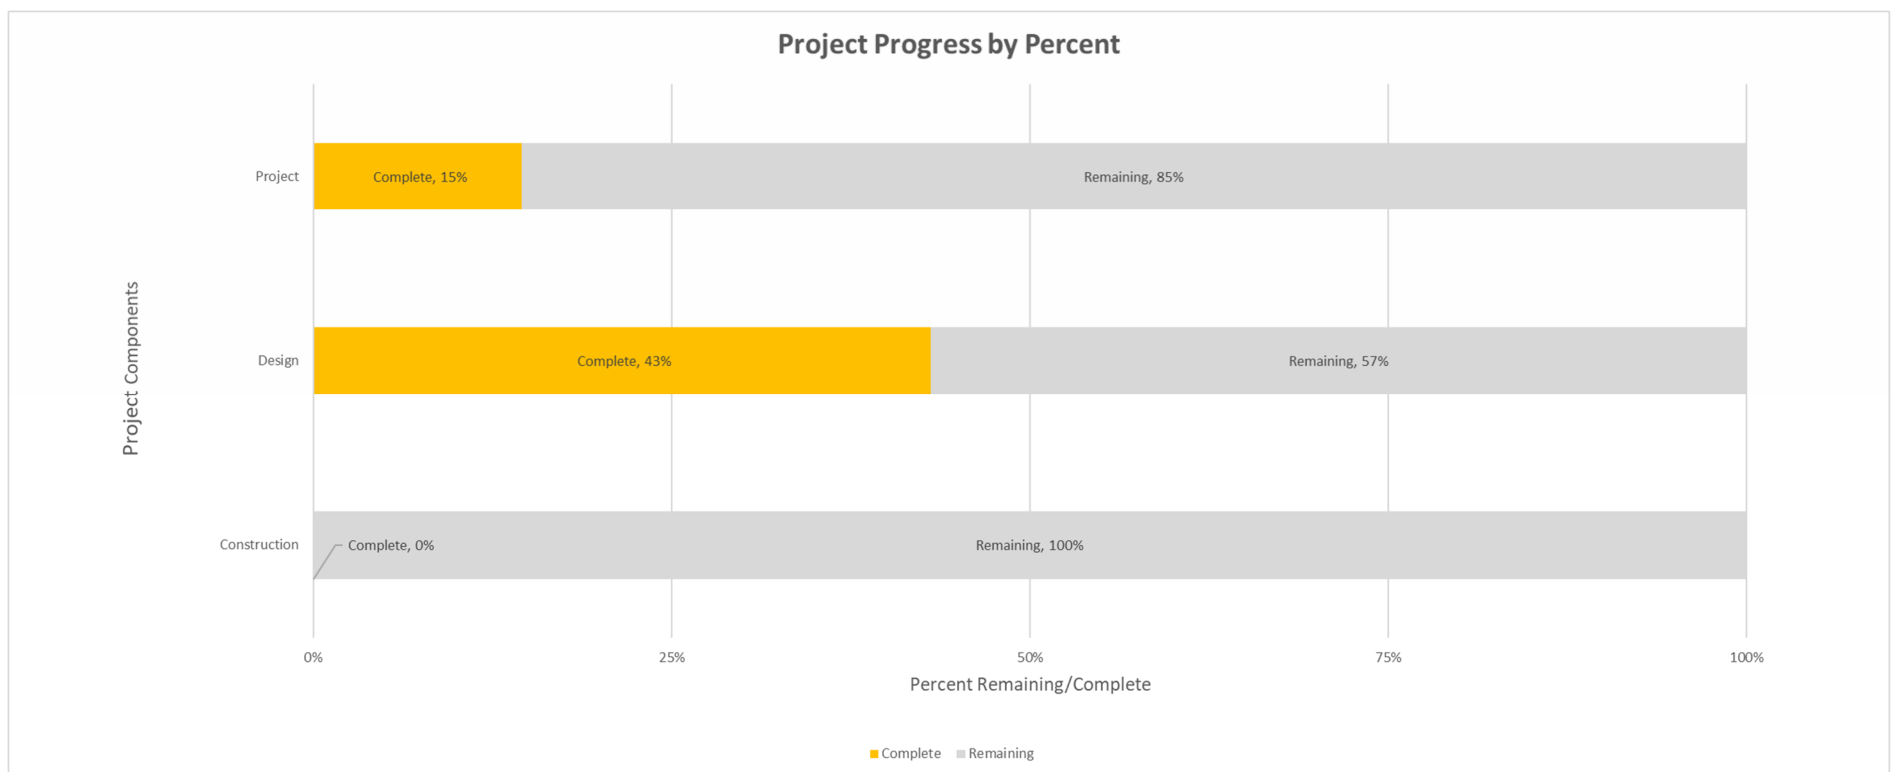

Overall Project: 15% Complete, 85% Remaining

Design: 43% Complete, 57% Remaining

Construction: 0% Complete, 100% Remaining




Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: October 2023 Update

### Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

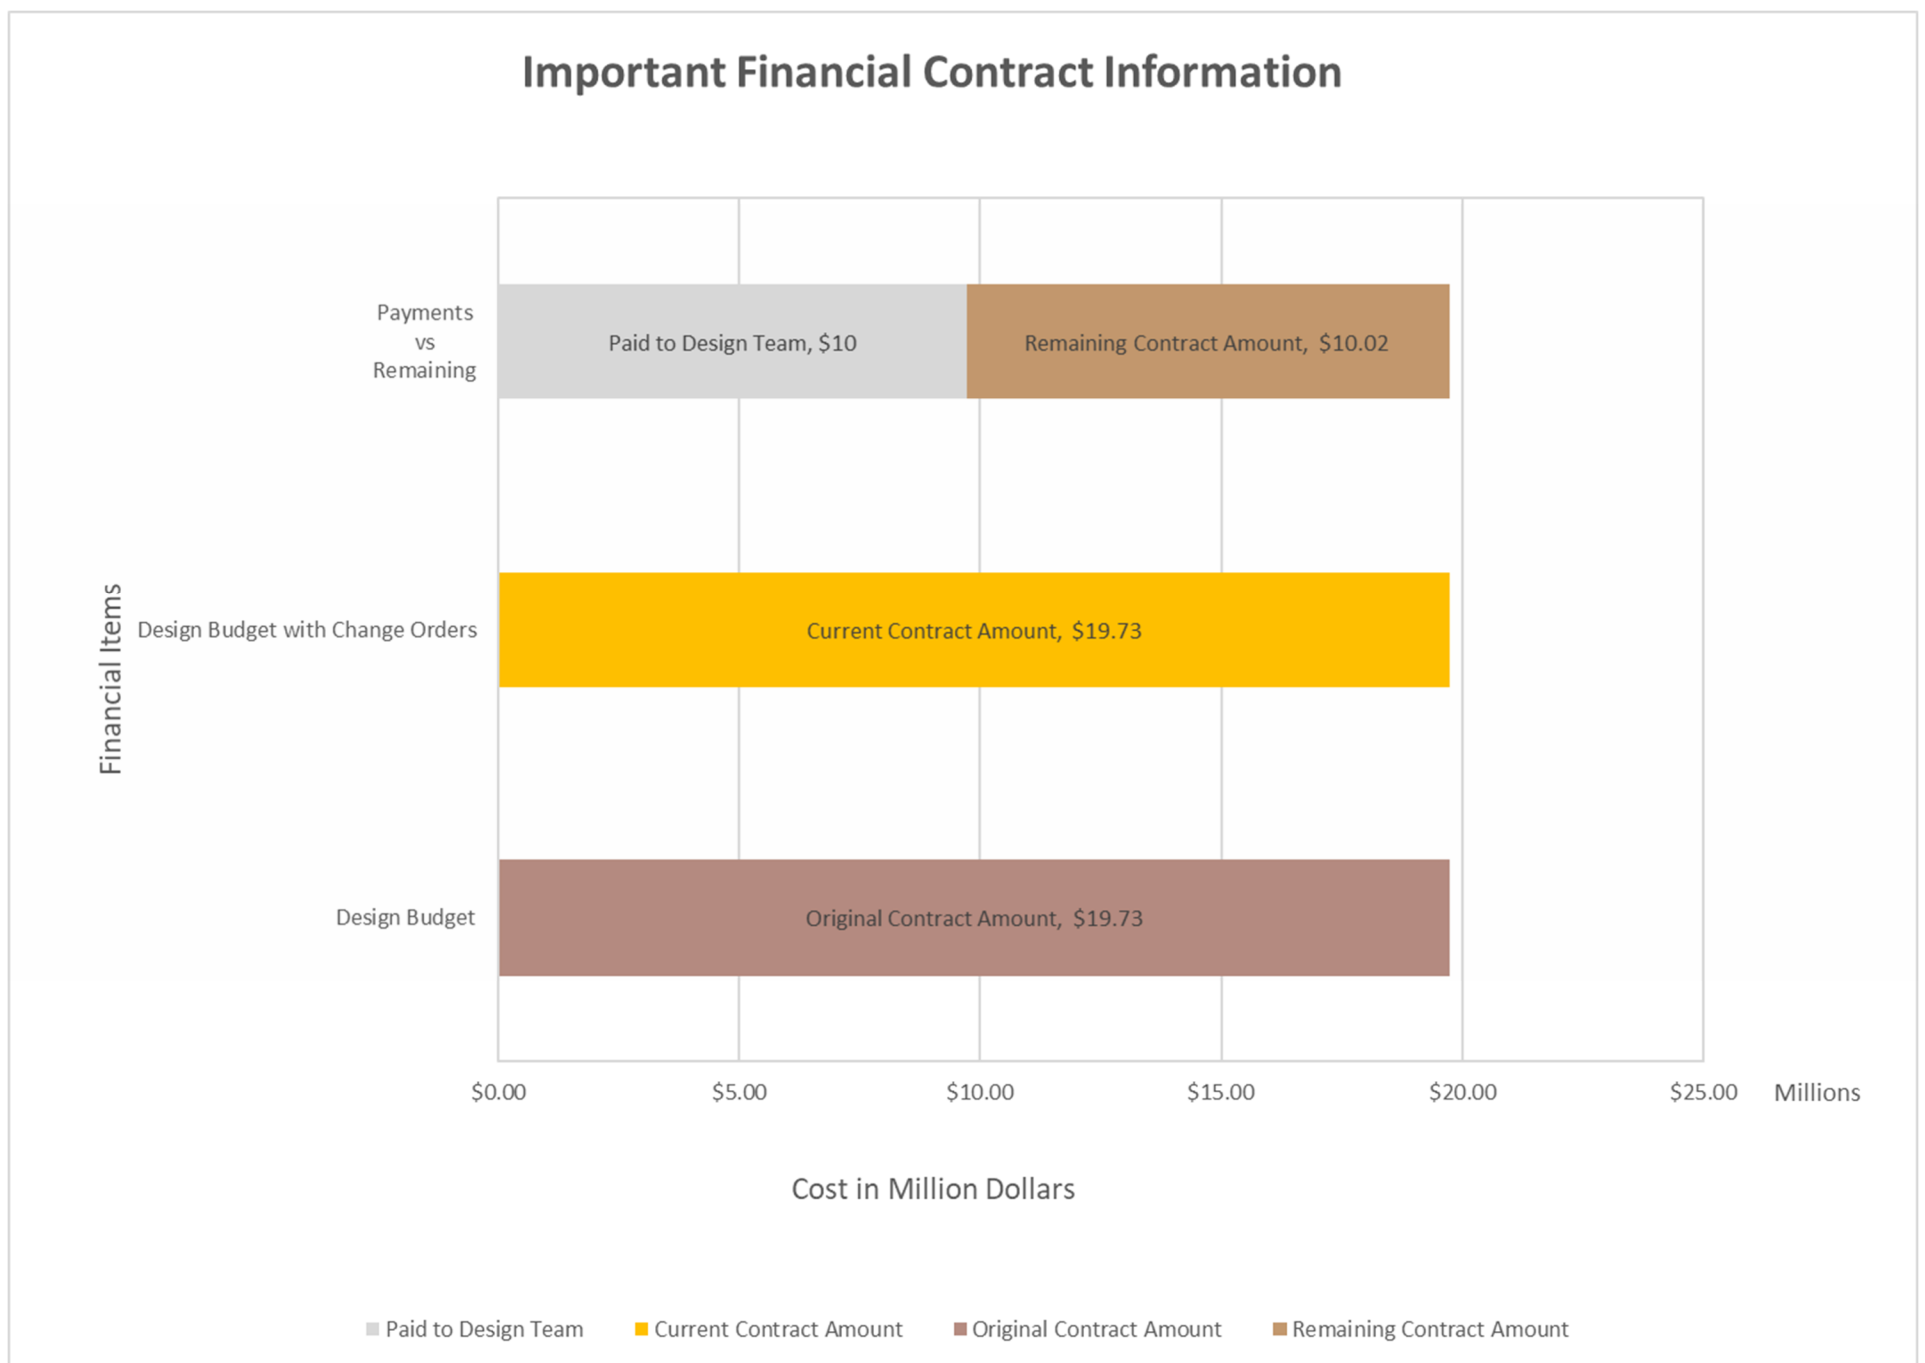

Initial Design Contract Value: \$19.73 Million

Design Payments to date: \$9.71 Million, Payments remaining \$10.02 Million

Current Design Contract Value: \$19.73 Million, Total Change Orders to Date: \$0


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: October 2023 Update

## Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

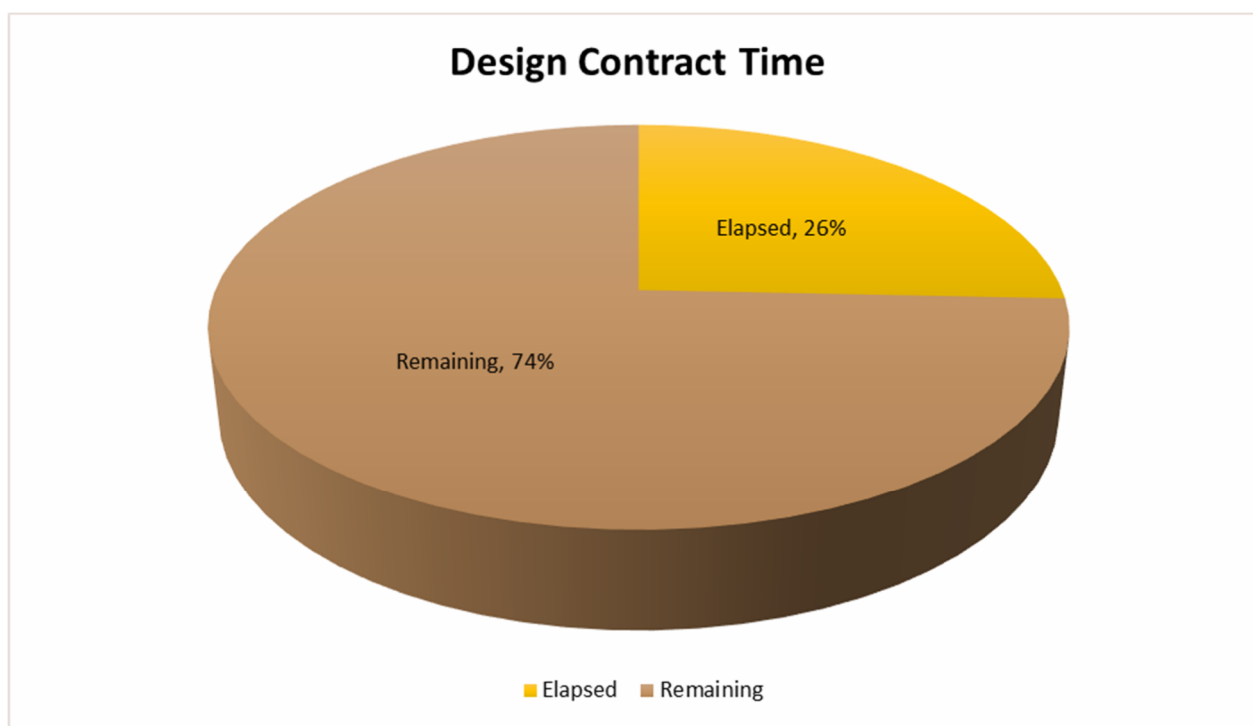

Total Design Contract time: 596 days

Elapsed Design Contract time: 153 days, 26%

Design Contract Time Remaining: 443 days, 74%
