


Project Name: I-70 Floyd Hill Central Section  
 Project Number: 25177  
 Date: December 2023 Update

### I-70 Floyd Hill Central Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

#### Key Dates

The following image shows the progression of the key project dates.



Final CAP Proposals Received: TBD

Award of Contract: TBD


Notice To Proceed: TBD

Begin Construction: TBD

Project Name: I-70 Floyd Hill Central Section  
 Project Number: 25177  
 Date: December 2023 Update

### Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

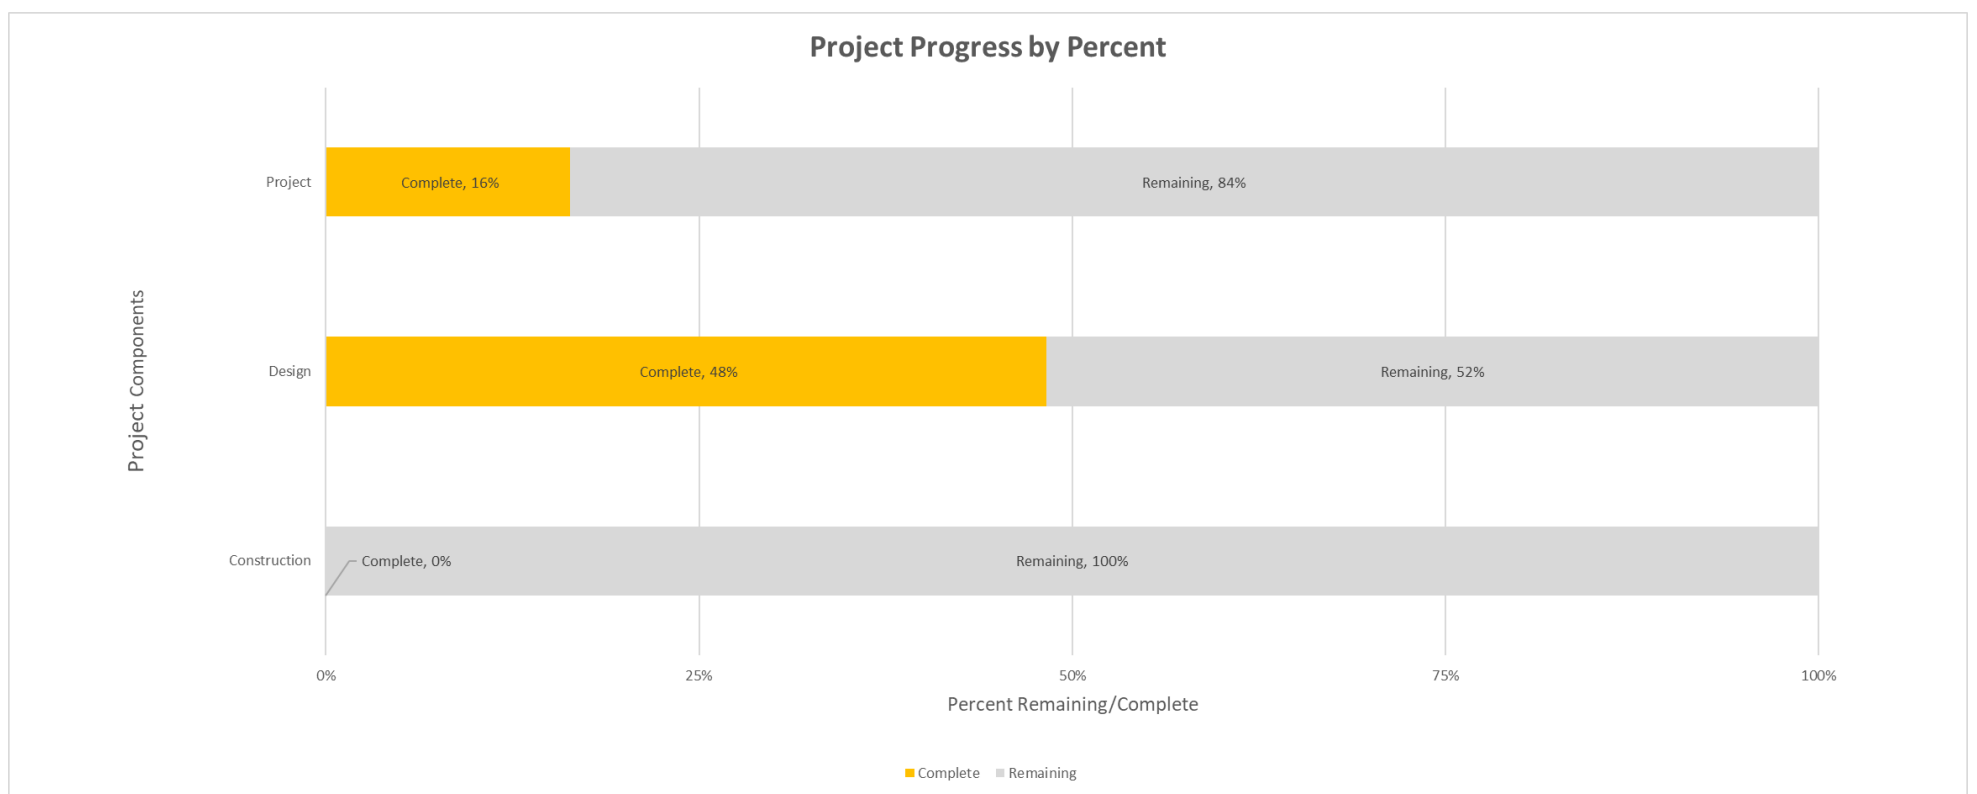

Overall Project: 16% Complete, 84% Remaining

Design: 48% Complete, 52% Remaining

Construction: 0% Complete, 100% Remaining




Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: December 2023 Update

**Important Financial Contract Information**

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

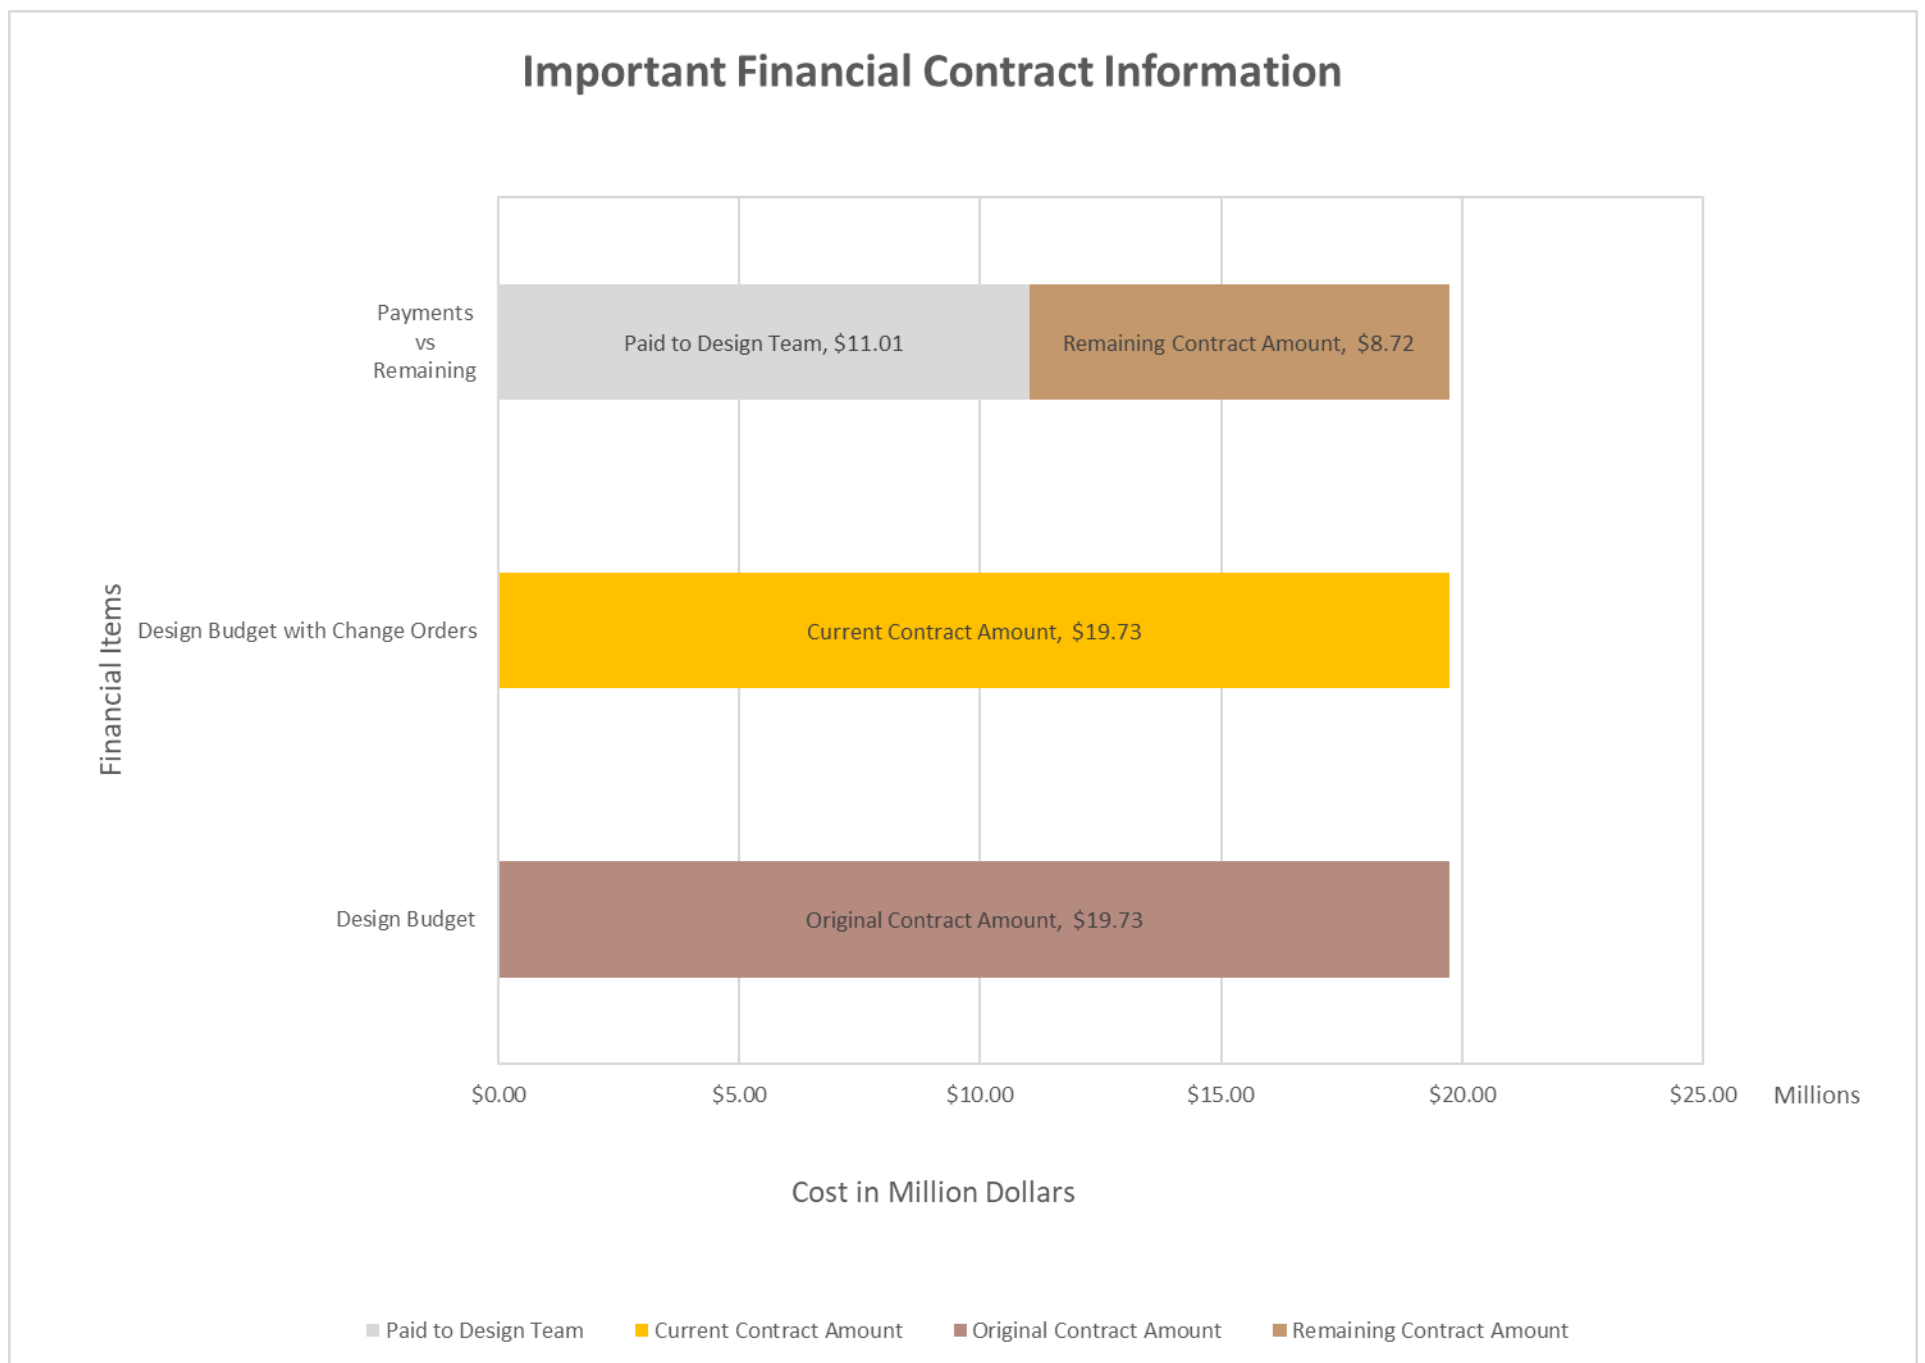

Initial Design Contract Value: \$19.73 Million

Design Payments to date: \$11.01 Million, Payments remaining \$8.72 Million

Current Design Contract Value: \$19.73 Million, Total Change Orders to Date: \$0


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: December 2023 Update

## Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

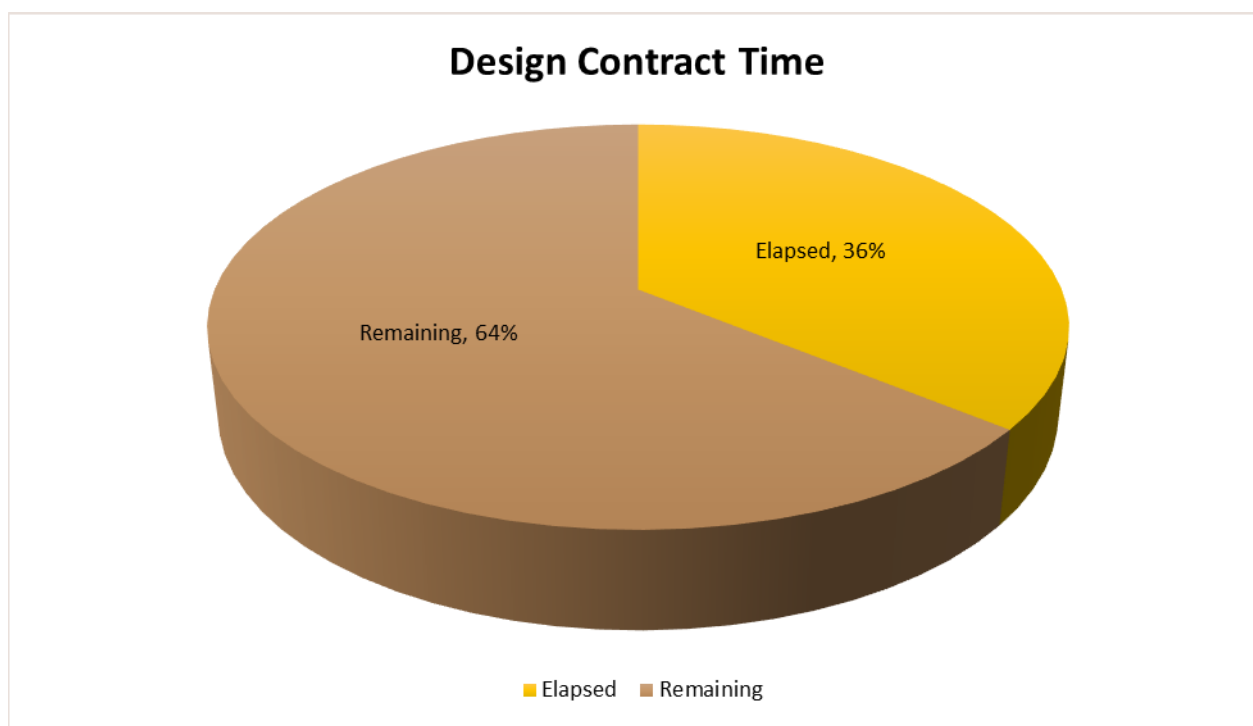

Total Design Contract time: 596 days

Elapsed Design Contract time: 214 days, 36%

Design Contract Time Remaining: 382 days, 64%
