


Project Name: I-70 Floyd Hill Central Section
Project Number: 25177
Date: December 2024 Update

I-70 Floyd Hill Central Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

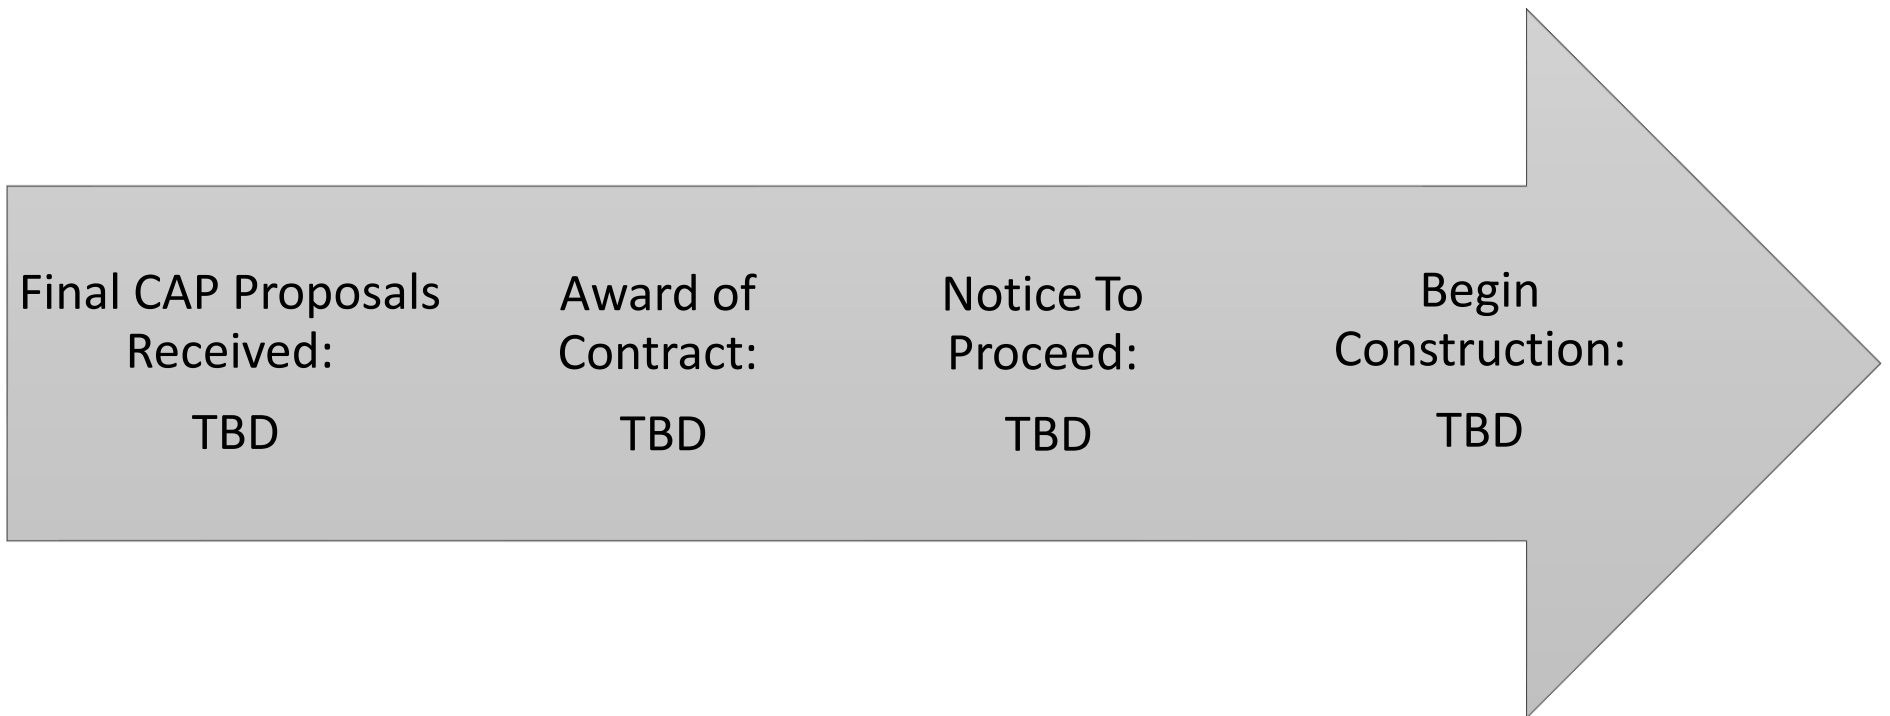

Final CAP Proposals Received: TBD

Award of Contract: TBD

Notice To Proceed: TBD

Begin Construction: TBD




Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: December 2024 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

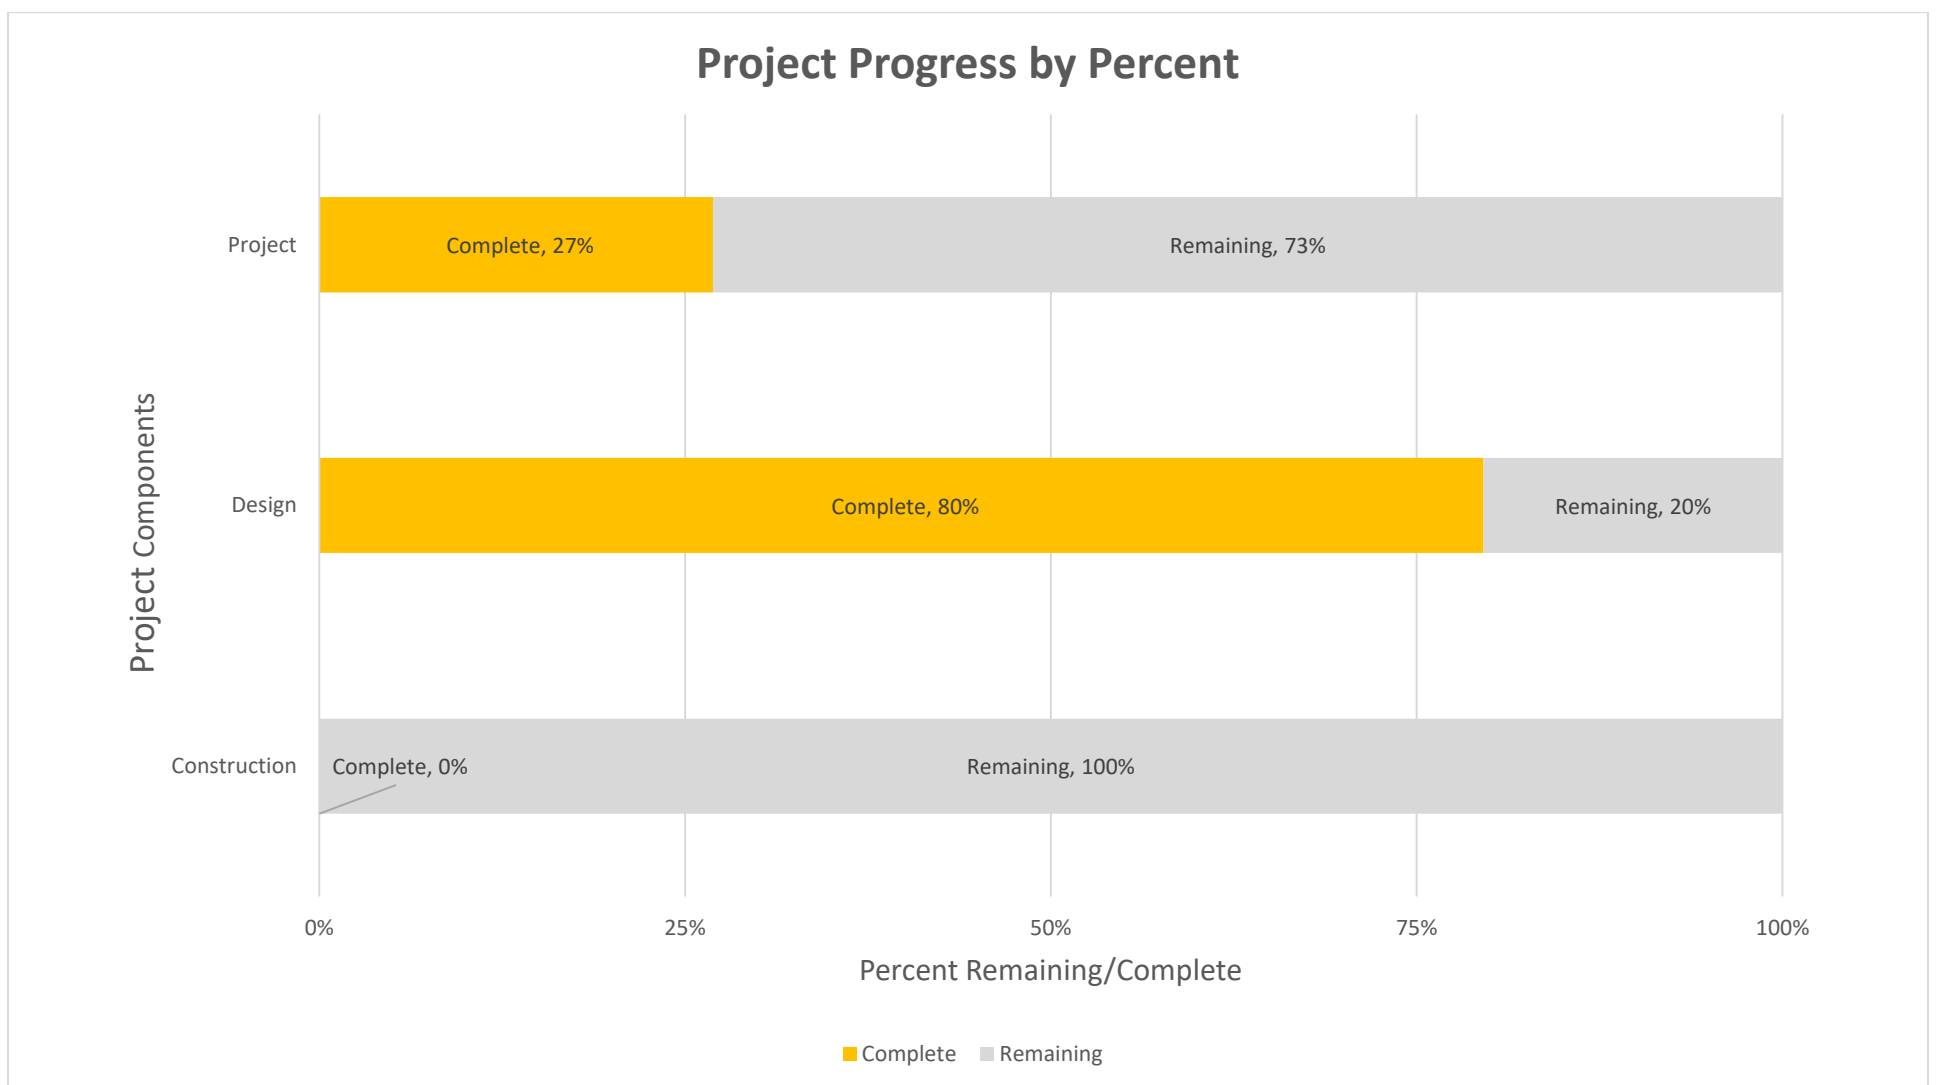

Overall Project: 27% Complete, 73% Remaining

Design: 80% Complete, 20% Remaining


Construction: 0% Complete, 100% Remaining



Project Name: I-70 Floyd Hill Central Section
Project Number: 25177
Date: December 2024 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

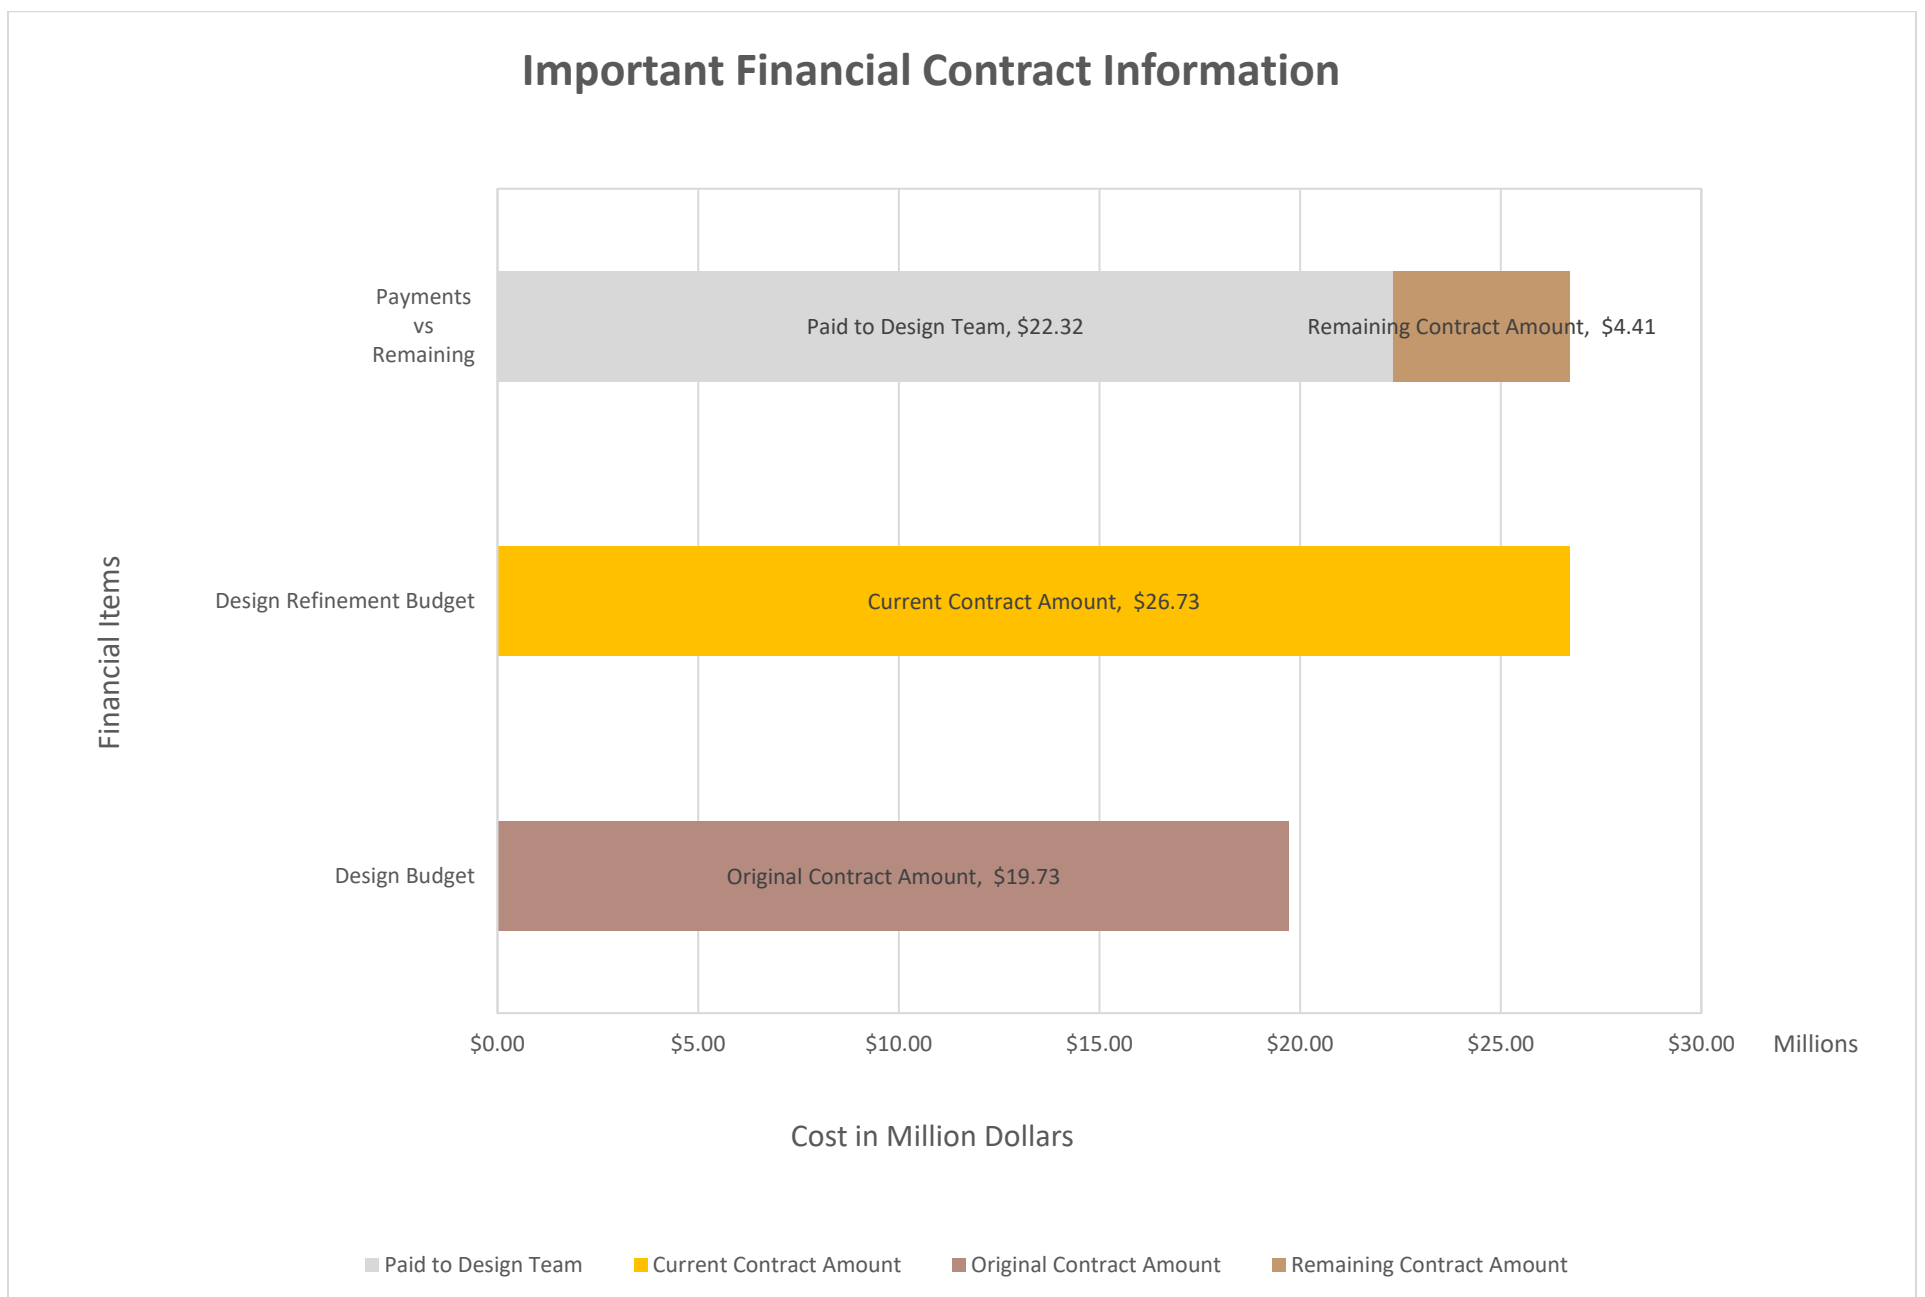

Initial Design Contract Value: \$19.73 Million

Design Payments to date: \$22.32 Million, Payments remaining \$4.41 Million

Current Design Contract Value: \$26.73 Million, Total Change Orders to Date: \$7 Million


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: December 2024 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

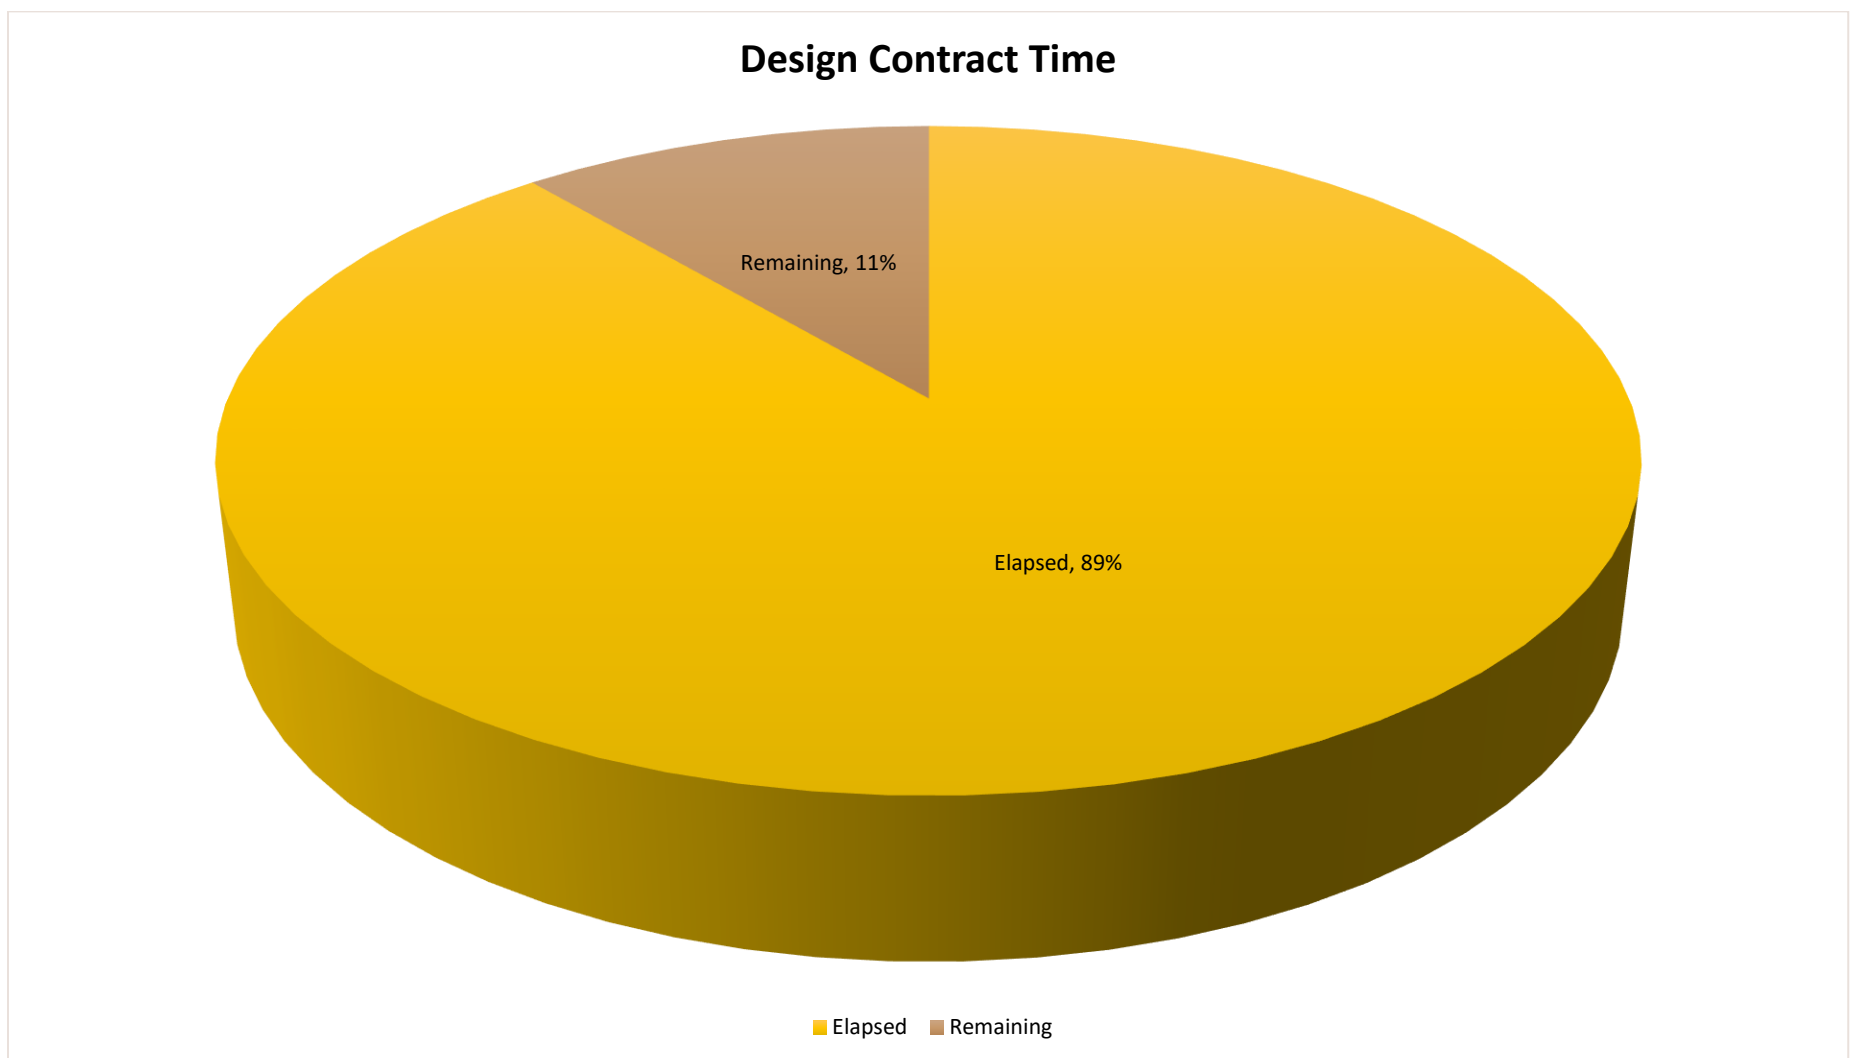

Total Design Contract time: 653 days

Elapsed Design Contract time: 580 days, 89%

Design Contract Time Remaining: 73 days, 11%
