


Project Name: I-70 Floyd Hill Central Section  
Project Number: 25177  
Date: May 2025 Update

**I-70 Floyd Hill Central Section Project Dashboard**

This document provides monthly progress and financial updates on current CDOT projects.

**Key Dates**

The following image shows the progression of the key project dates.

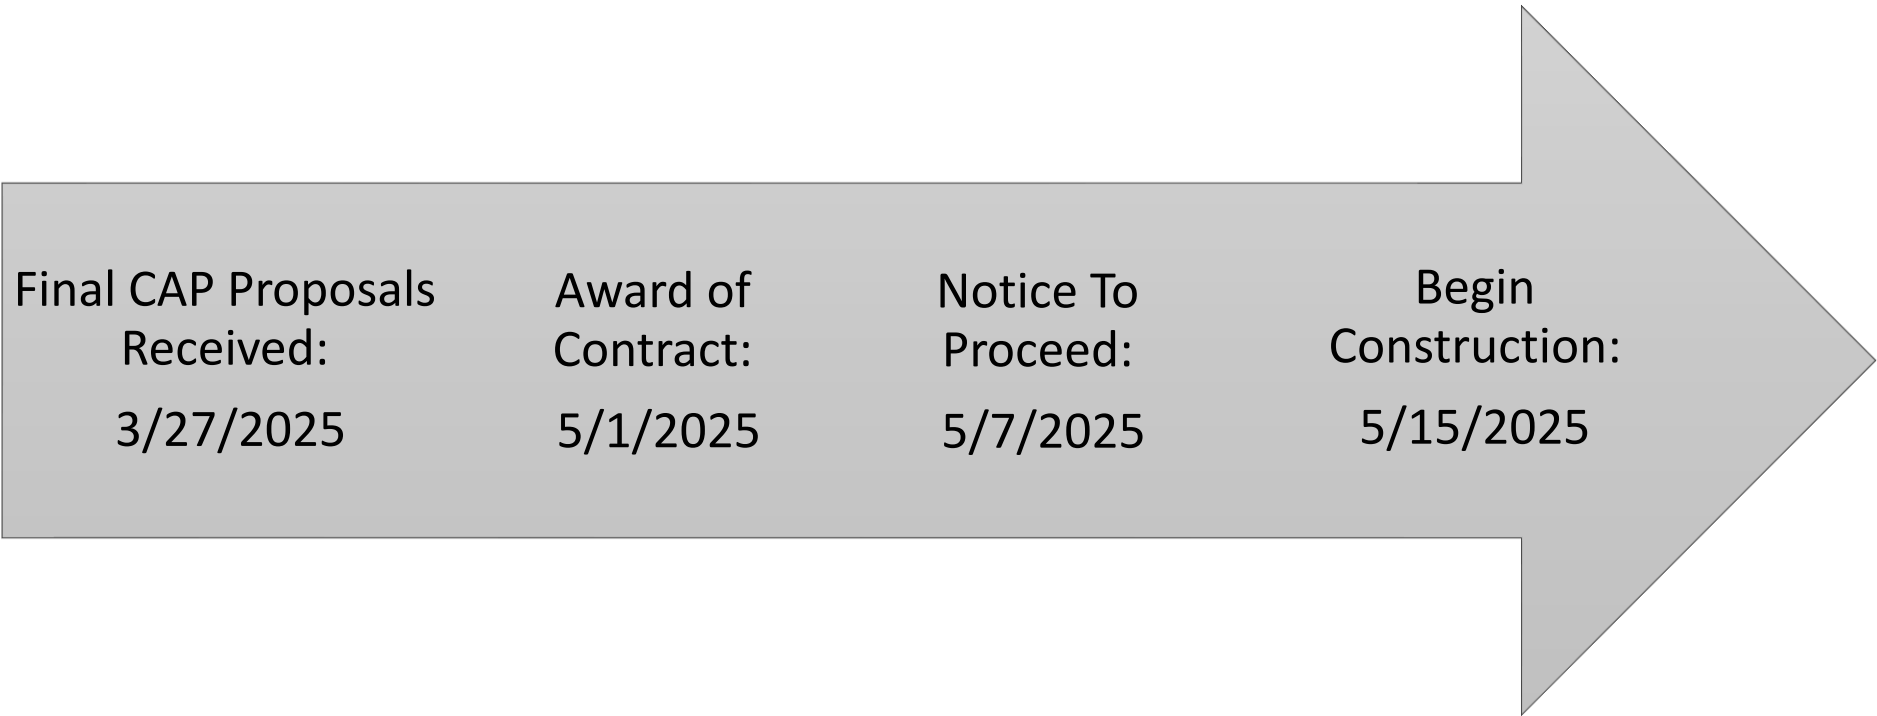


Final CAP Proposals Received: 3/27/2025  
Award of Contract: 5/1/2025  
Notice To Proceed: 5/7/2025  
Begin Construction: 5/15/2025

Project Name: I-70 Floyd Hill Central Section  
Project Number: 25177  
Date: May 2025 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

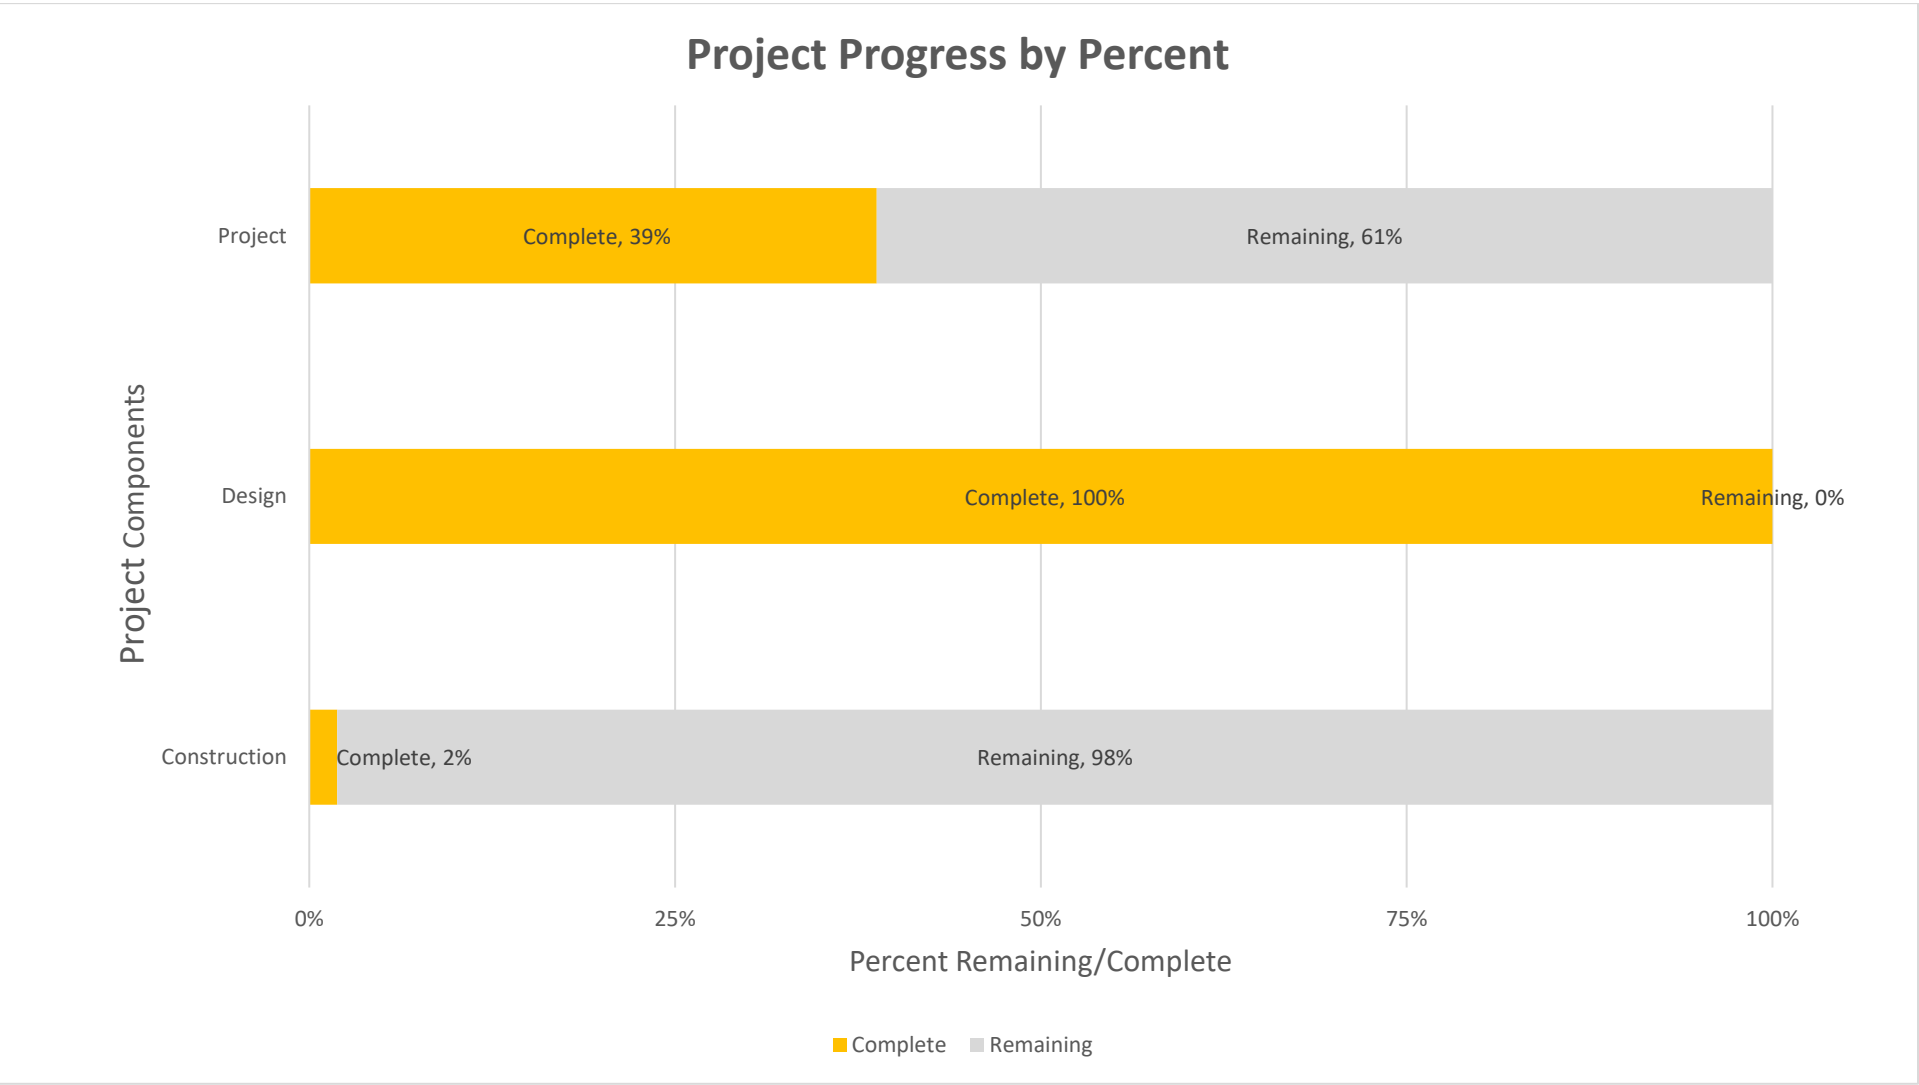

Overall Project: 39% Complete, 61% Remaining  
Design: 100% Complete, 0% Remaining  
Construction: 2% Complete, 98% Remaining


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: May 2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

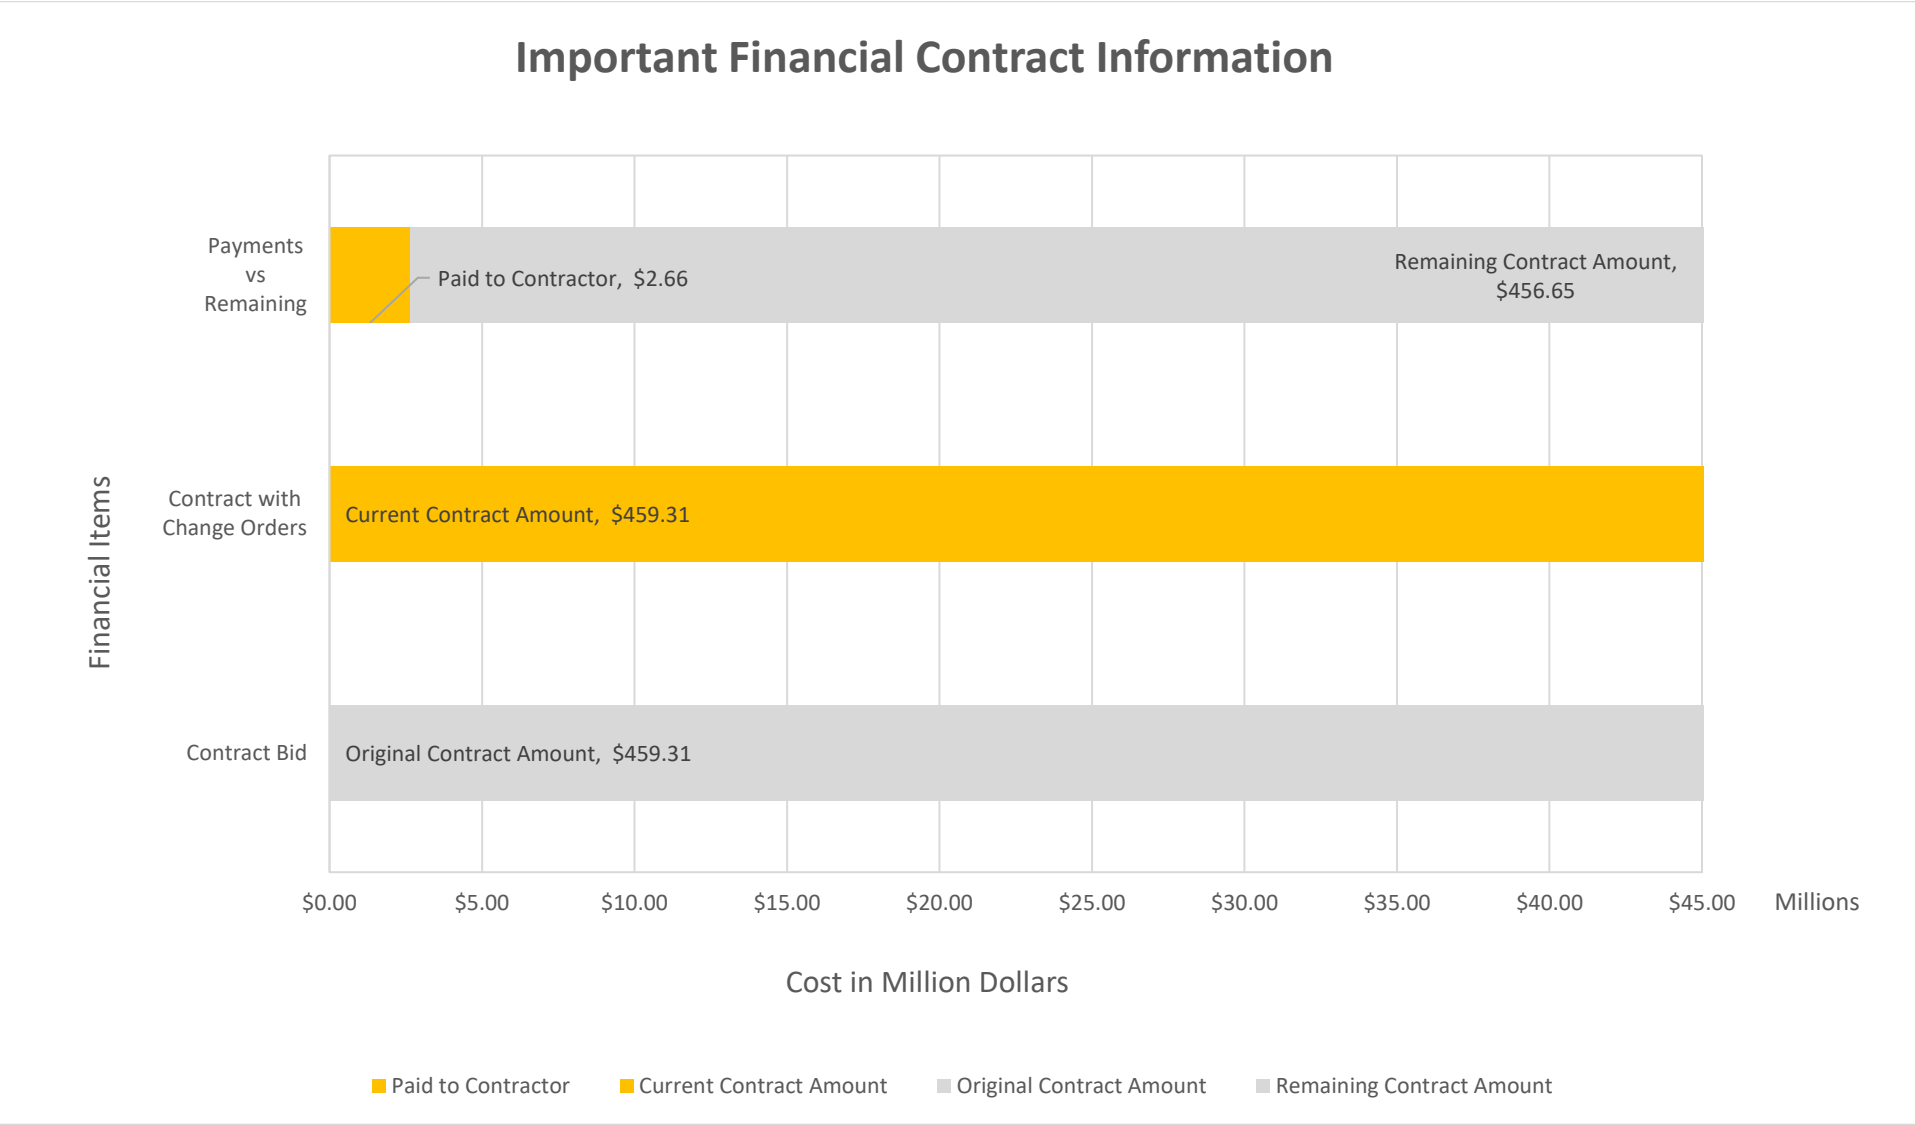

Initial Contract Value: \$459.31 Million


Design Payments to date: \$2.66 Million, Payments remaining: \$456.65 Million

Current Contract Value: \$459.31 Million, Total Change Orders to Date: \$0

Project Name: I-70 Floyd Hill Central Section  
Project Number: 25177  
Date: May 2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

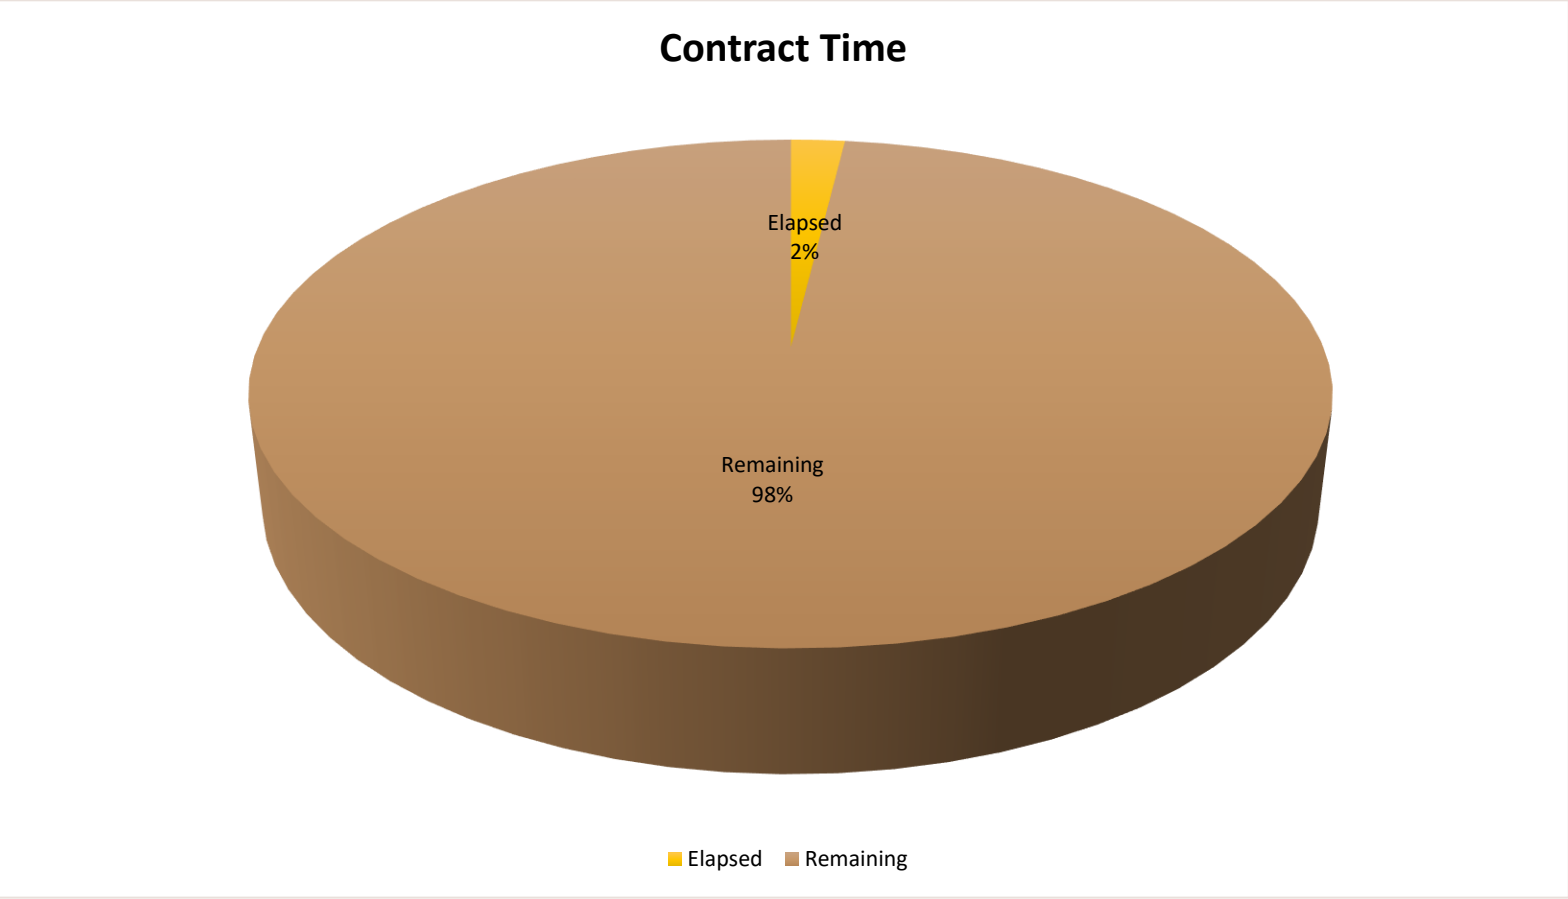

Total Contract time: 1251 days  
Elapsed Contact time: 24 days, 2%  
Design Time Remaining: 1227 days, 98%
