


Project Name: I-70 Floyd Hill Central Section
Project Number: 25177
Date: August 2025 Update

I-70 Floyd Hill Central Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

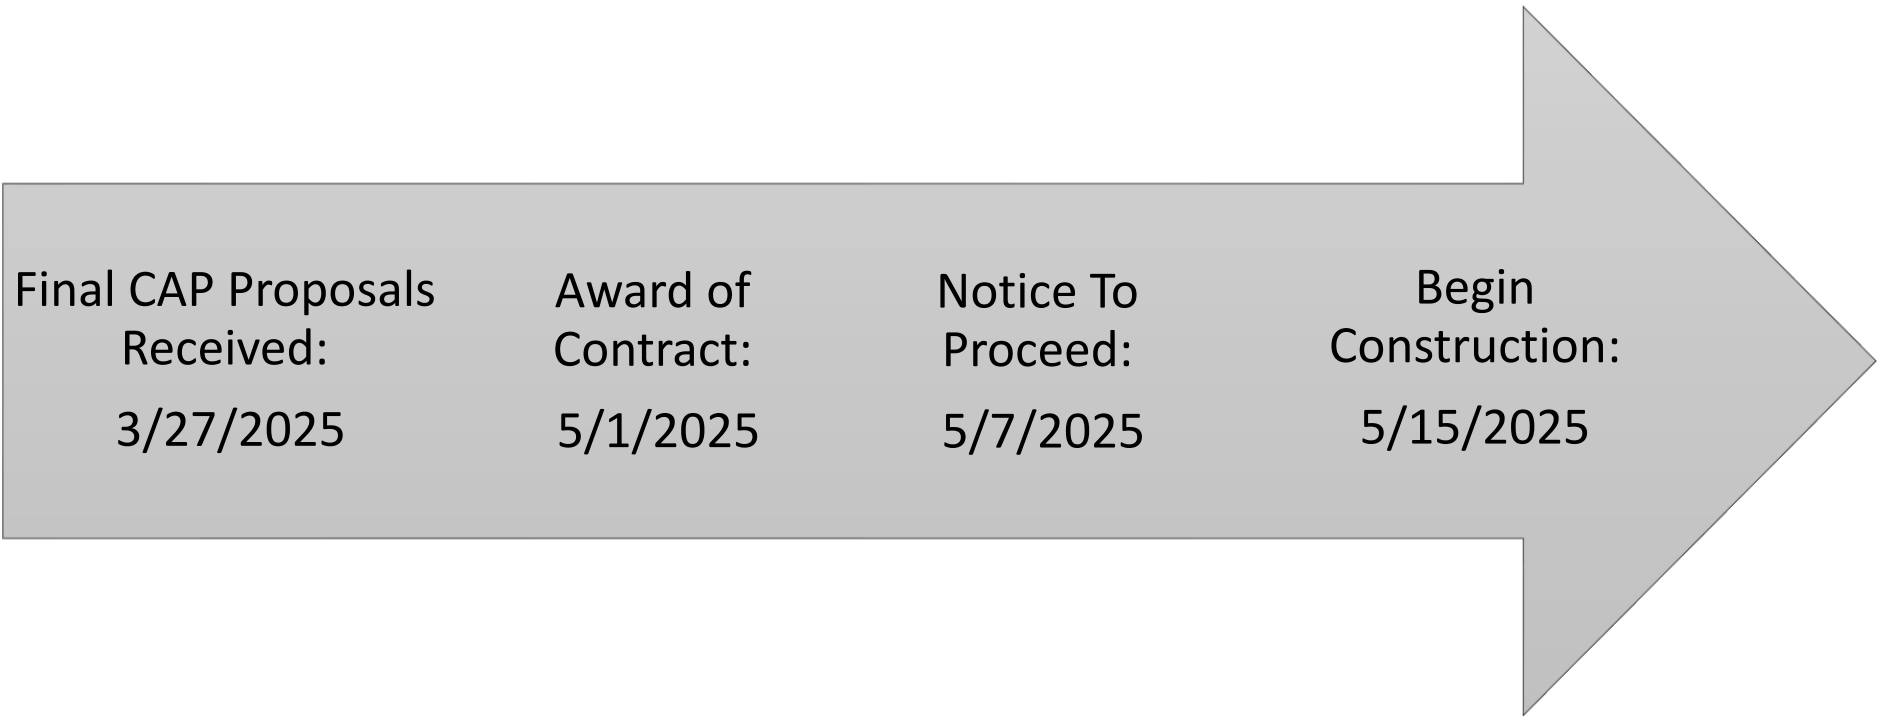

Final CAP Proposals Received: 3/27/2025
Award of Contract: 5/1/2025
Notice To Proceed: 5/7/2025
Begin Construction: 5/15/2025


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: August 2025 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

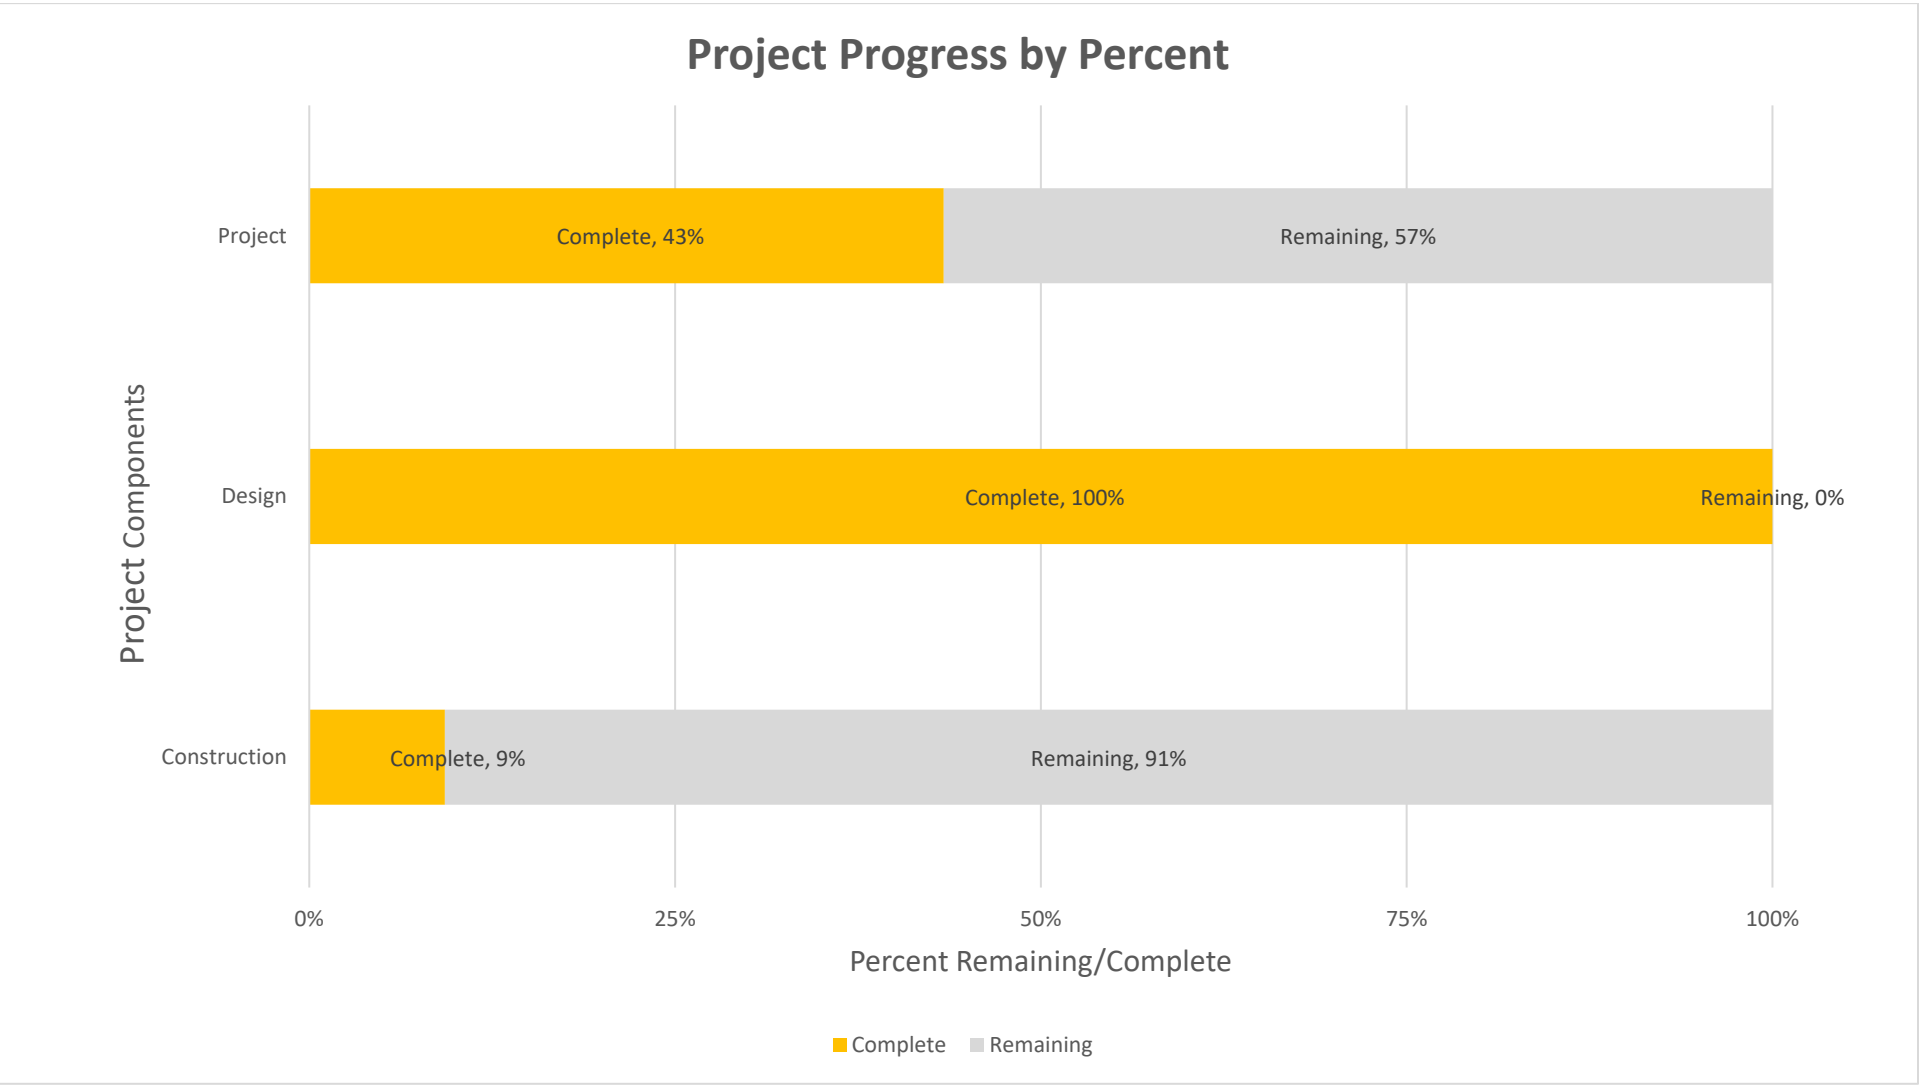

Overall Project: 43% Complete, 57% Remaining

Design: 100% Complete, 0% Remaining

Construction: 9% Complete, 91% Remaining


Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: August 2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

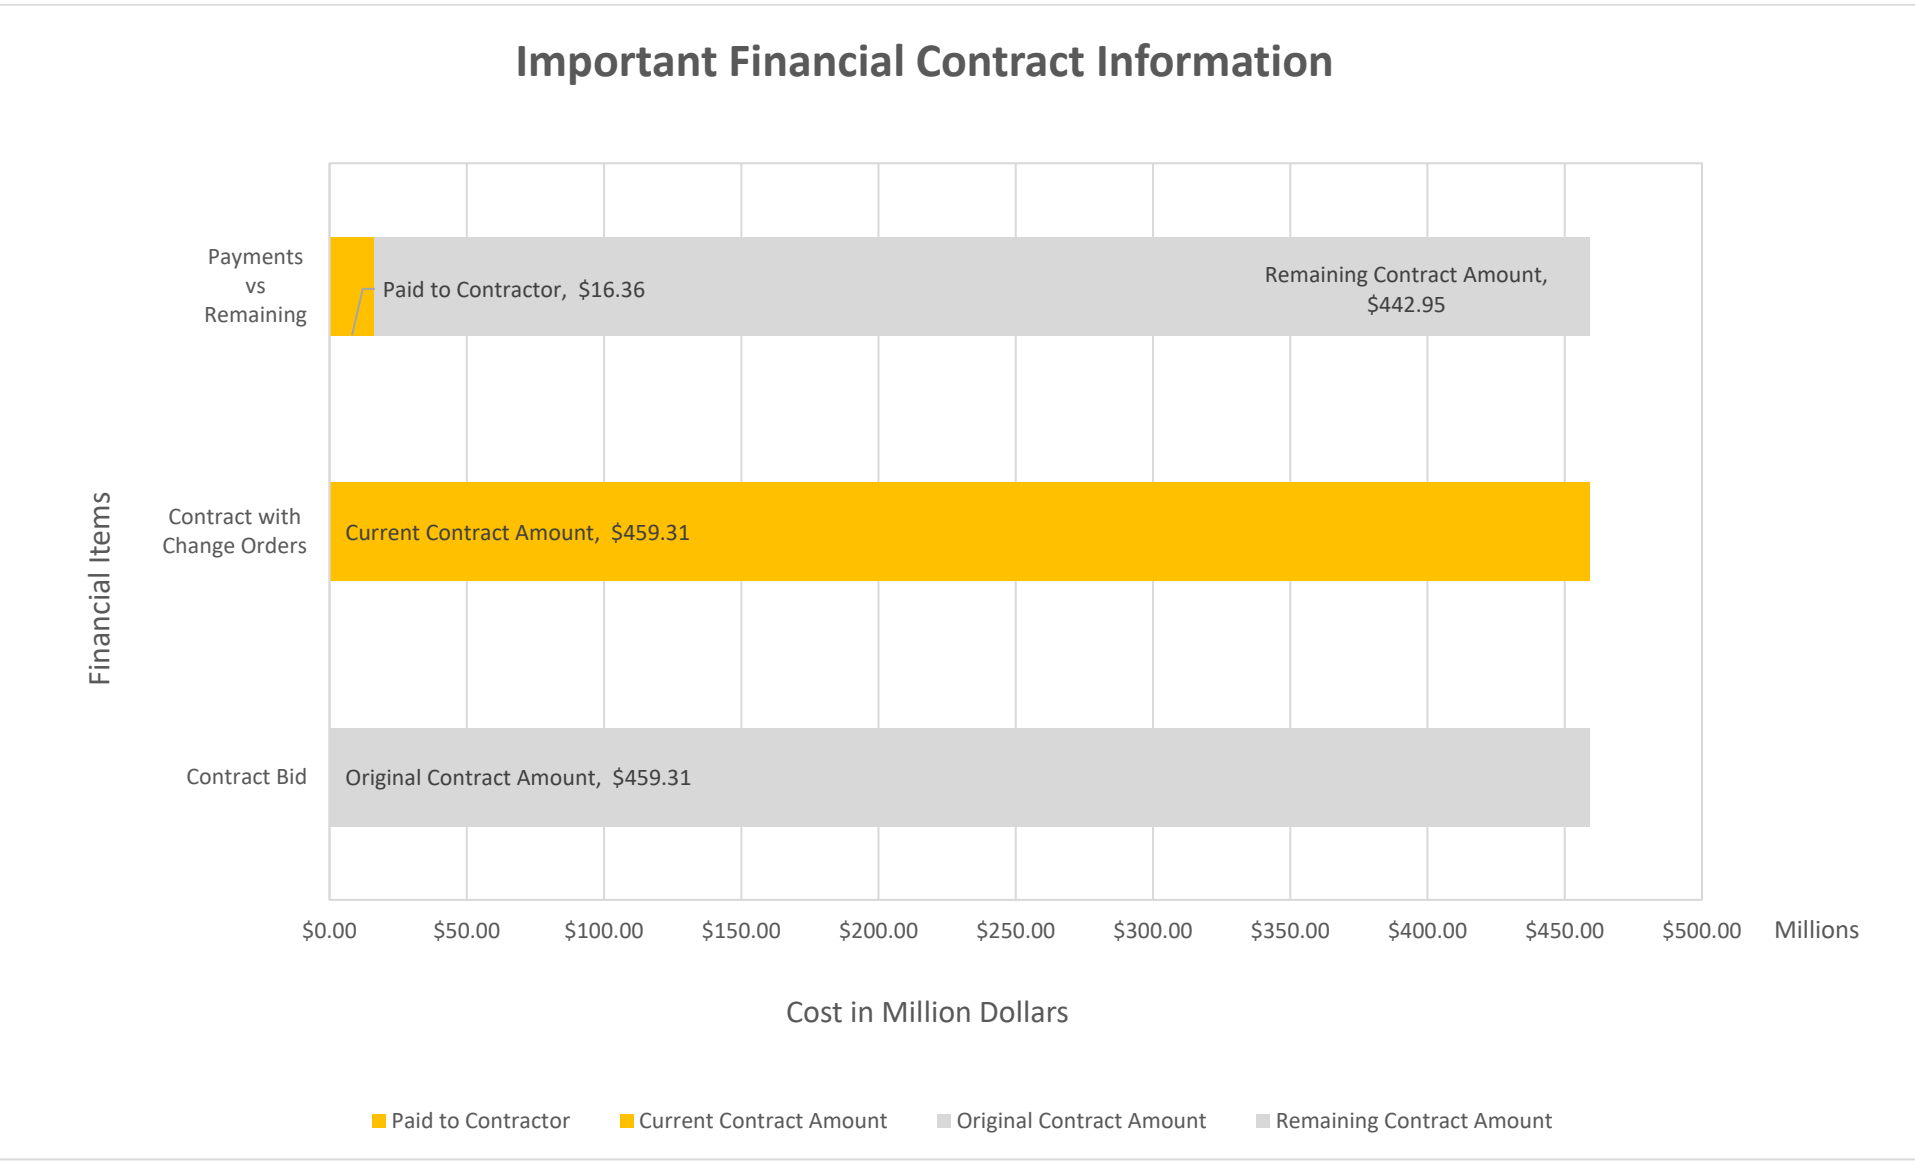

Initial Contract Value: \$459.31 Million


Payments to date: \$16.36 Million, Payments remaining: \$442.95 Million

Current Design Value: \$459.31 Million, Total Change Orders to Date: \$0

Project Name: I-70 Floyd Hill Central Section
Project Number: 25177
Date: August 2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

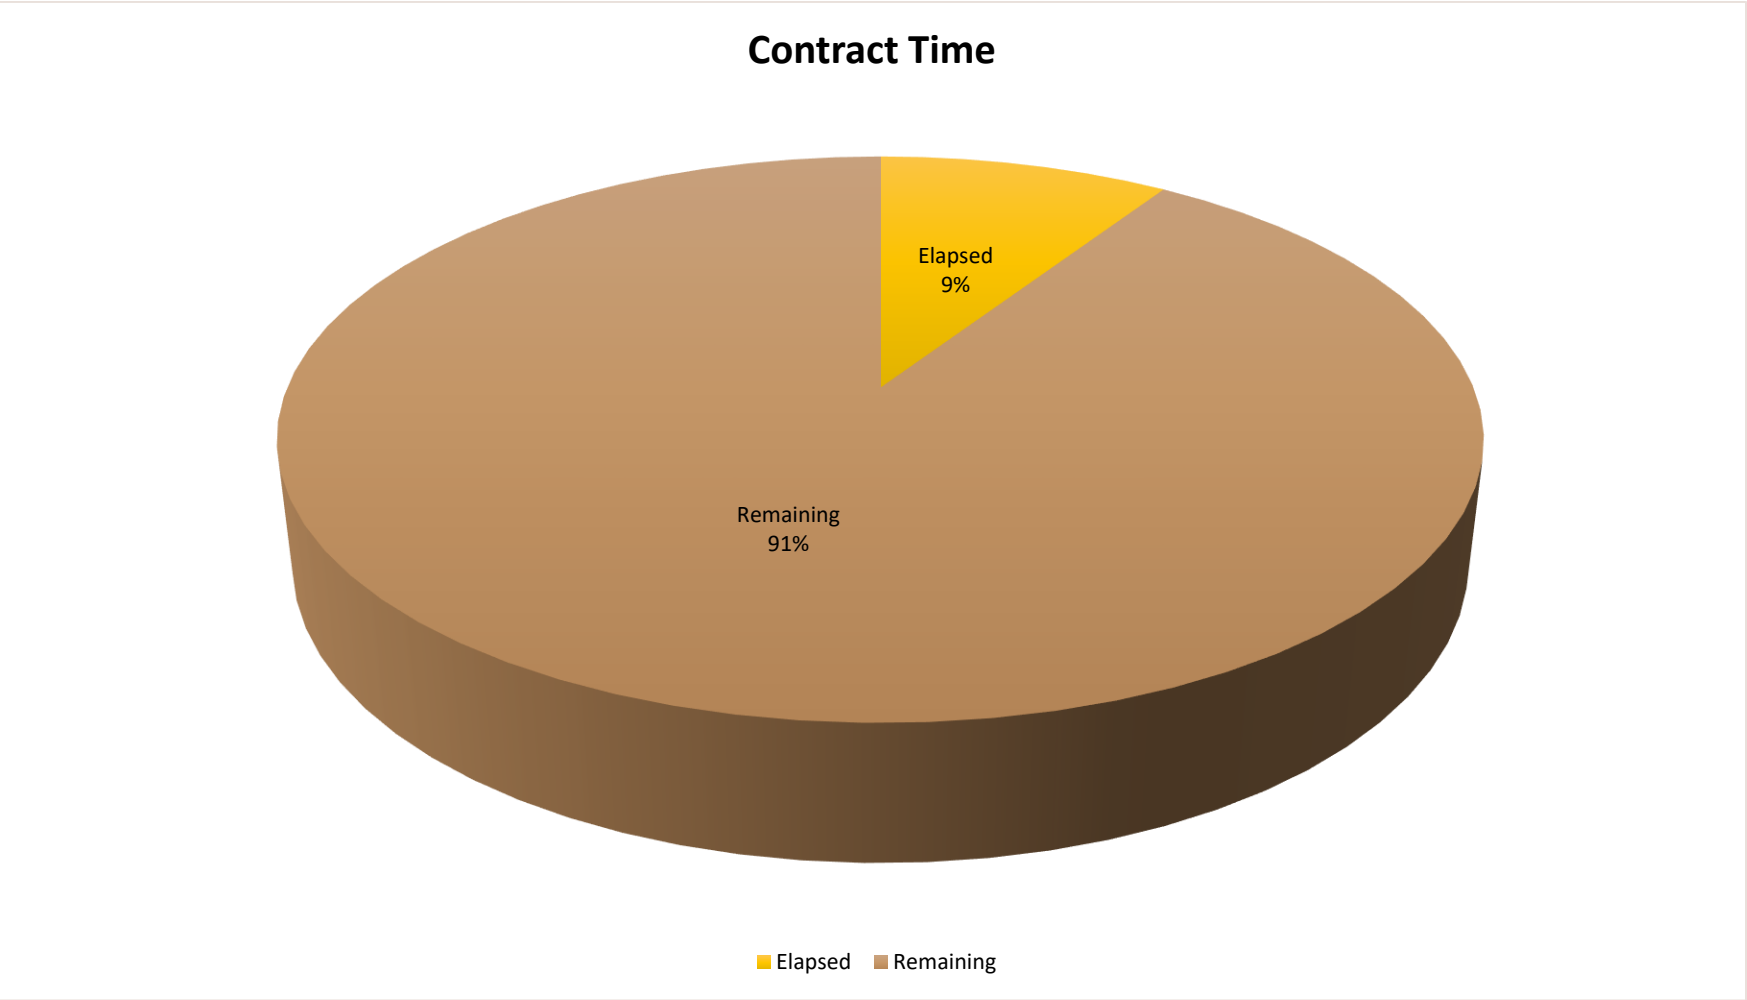

Total Contract time: 1251 days
Elapsed Contact time: 116 days, 9%
Contract Time Remaining: 1135 days, 91%
