


Project Name: I-70 Floyd Hill Early Access
Project Number: 25176
Date: July 2025 Update

I-70 Floyd Hill Central Section Project Dashboard July 2025
This document provides monthly progress and financial updates on current CDOT projects.

Key Dates
The following image shows the progression of the key project dates.

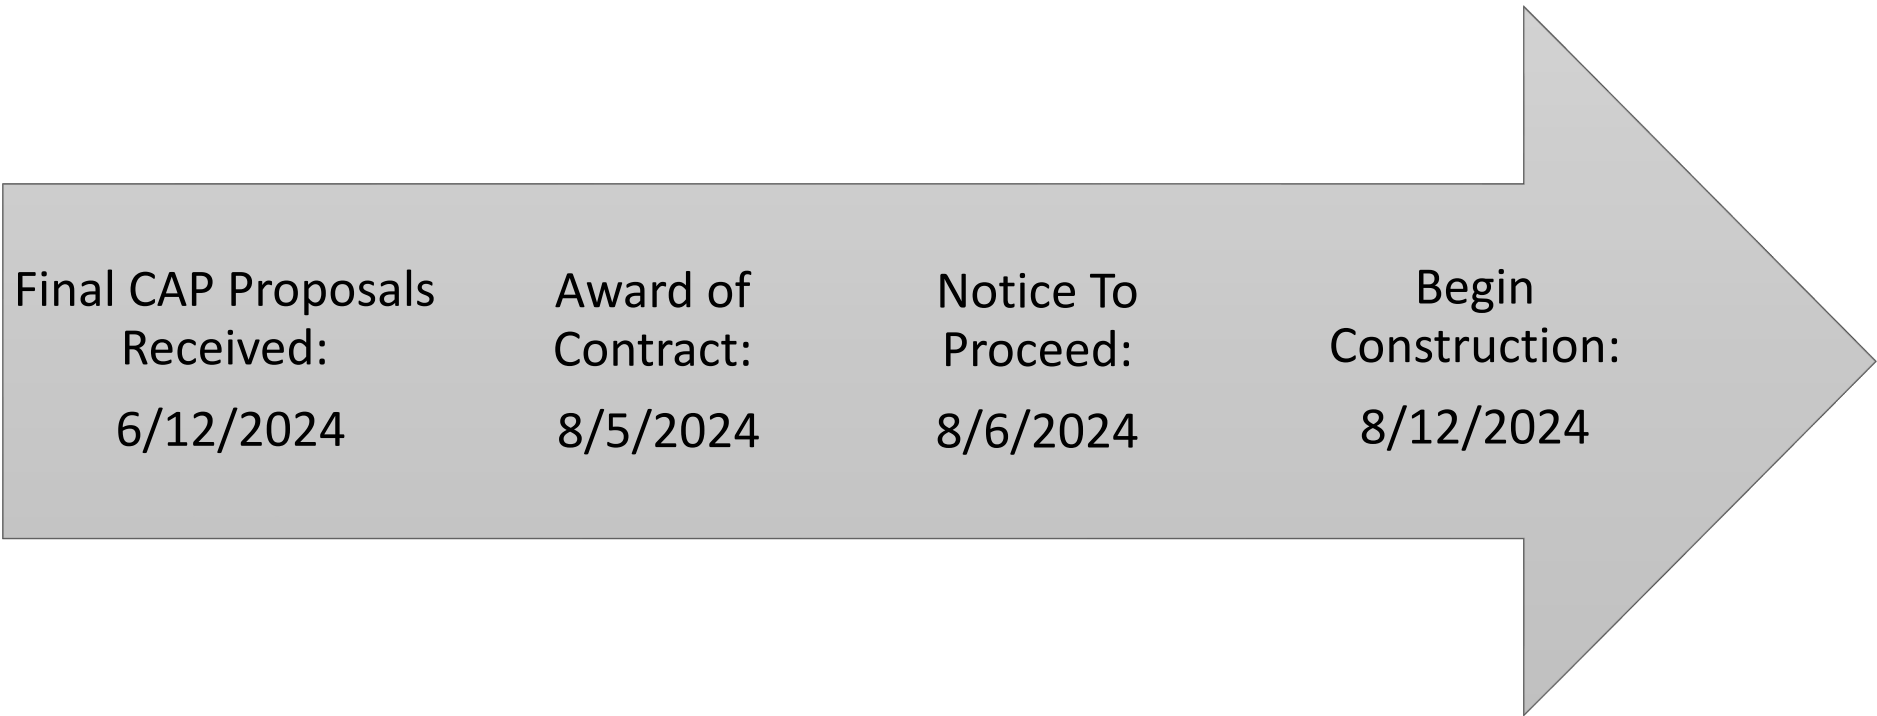


Final CAP Proposals Received: 6/12/2024
Award of Contract: 8/5/2024
Notice To Proceed: 8/6/2024
Begin Construction: 8/12/2024

Project Name: I-70 Floyd Hill Early Access
Project Number: 25176
Date: July 2025 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

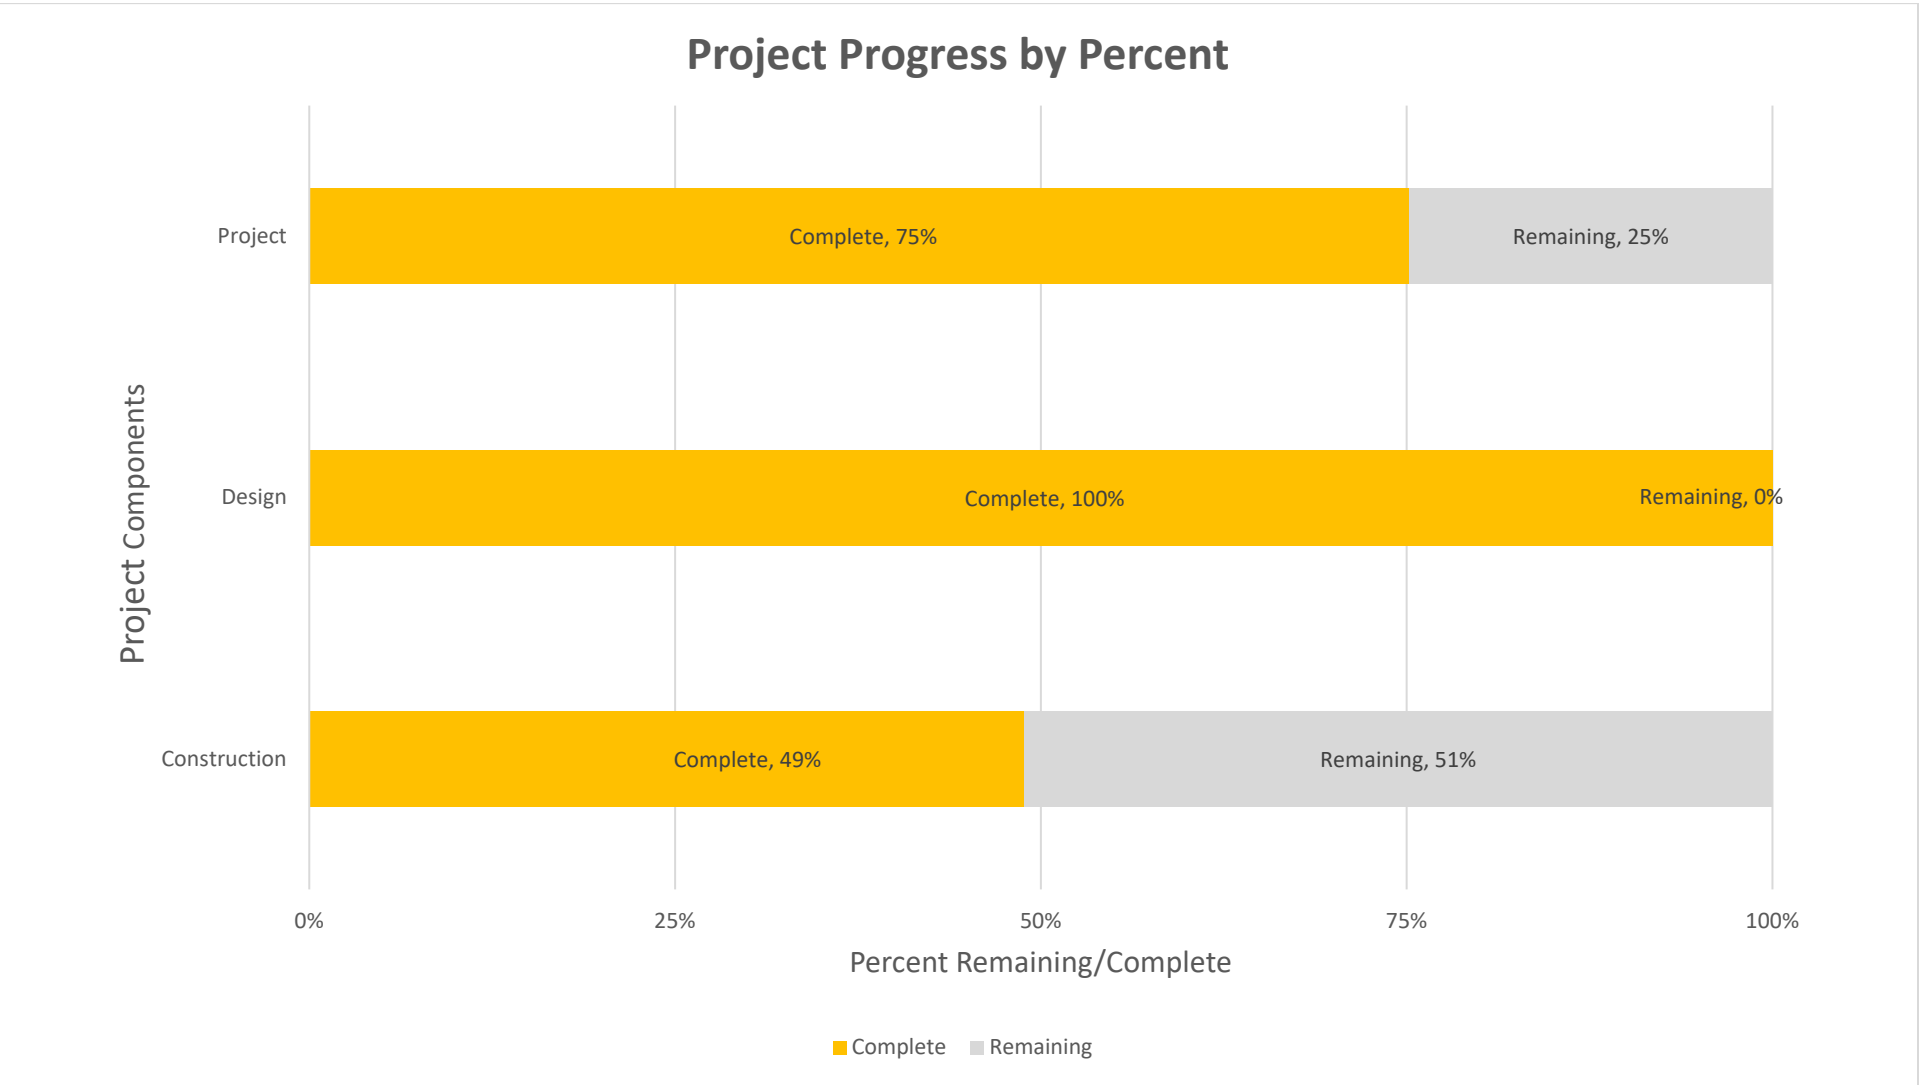


Overall Project: 75% Complete, 25% Remaining
Design: 100% Complete, 0% Remaining
Construction: 49% Complete, 51% Remaining

Project Name: I-70 Floyd Hill Early Access
Project Number: 25176
Date: July 2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

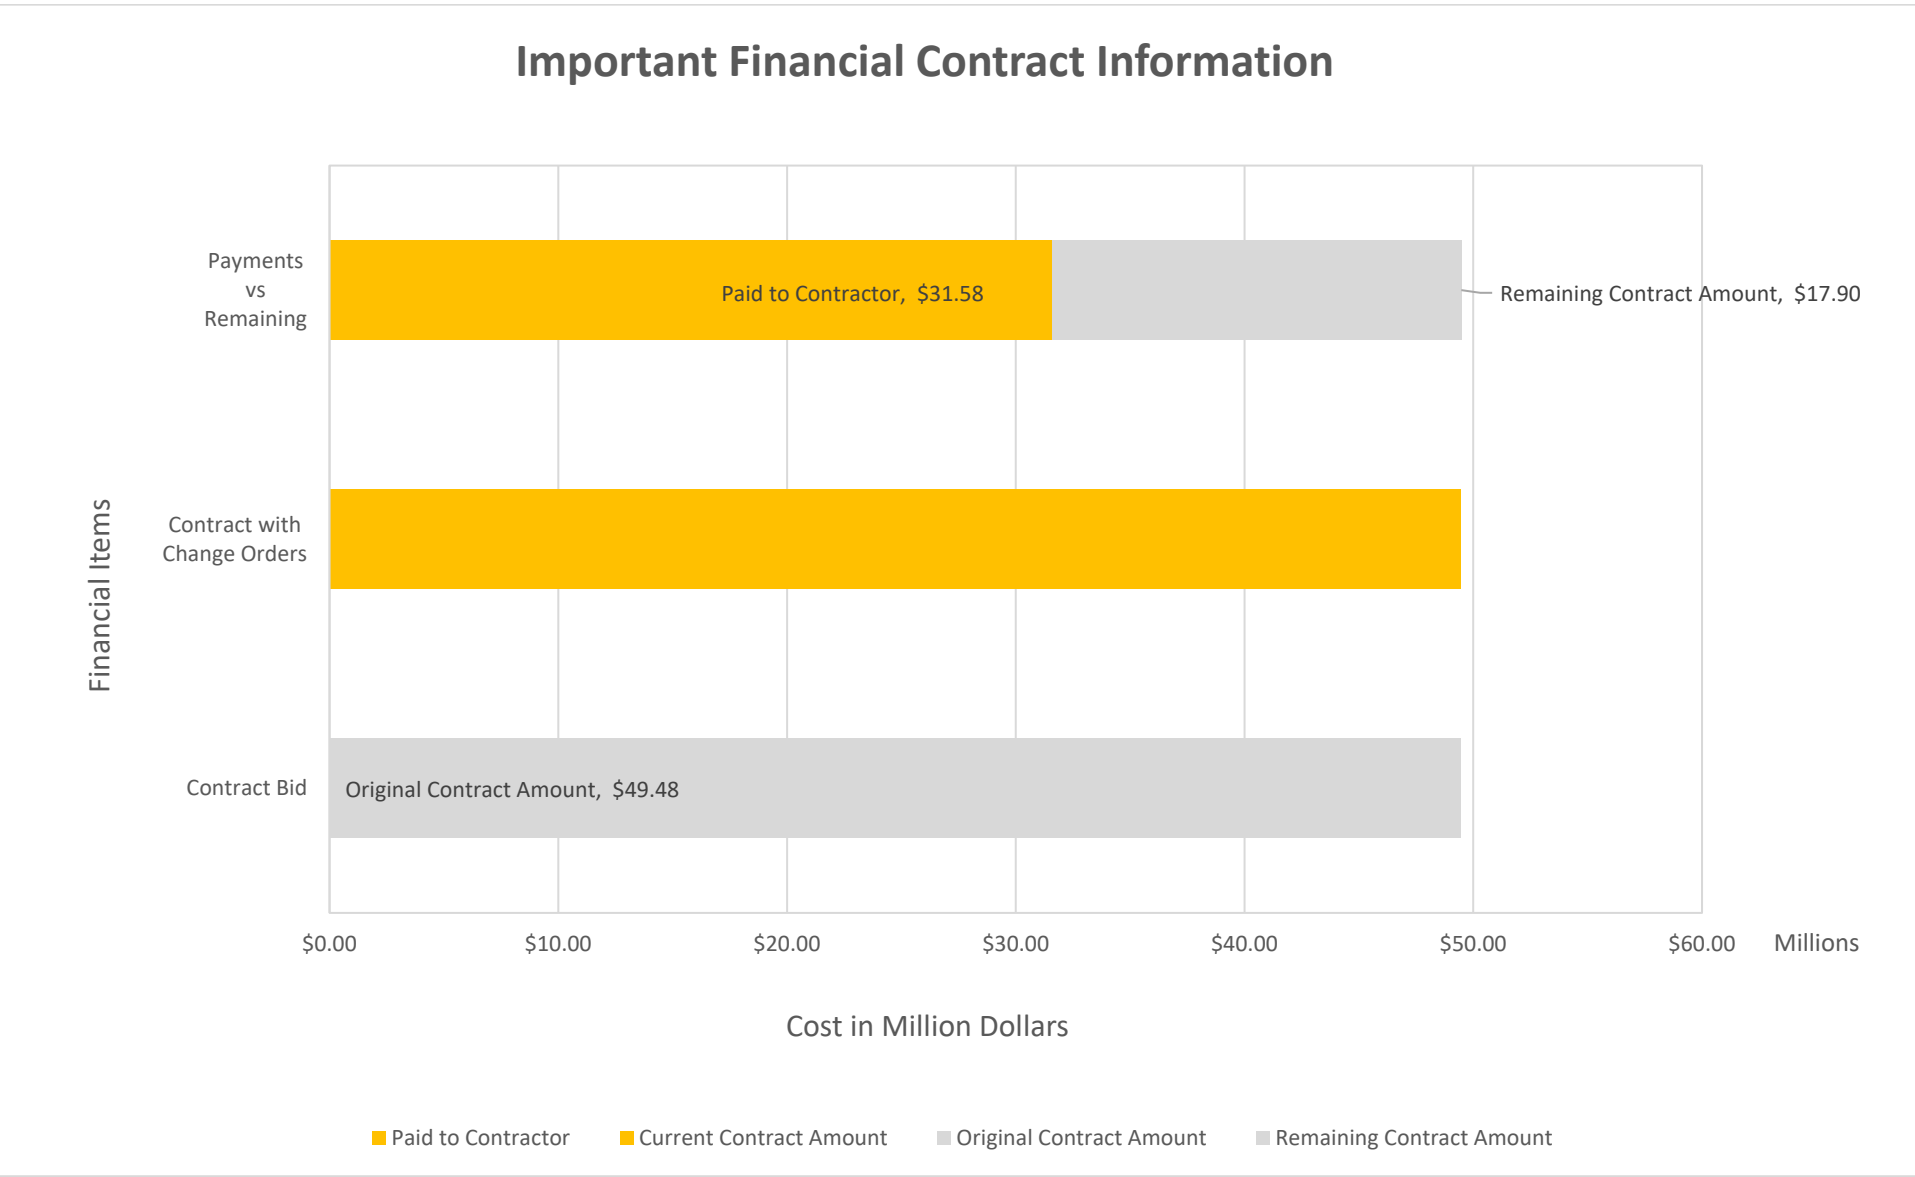


Total Contract Value: \$49.48 Million
Payments to date: \$31.58 Million, Payments remaining: \$17.90 Million
Current Contract Value: \$49.48 Million, Total Change Orders to Date: \$0

Project Name: I-70 Floyd Hill Early Access
Project Number: 25176
Date: July 2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

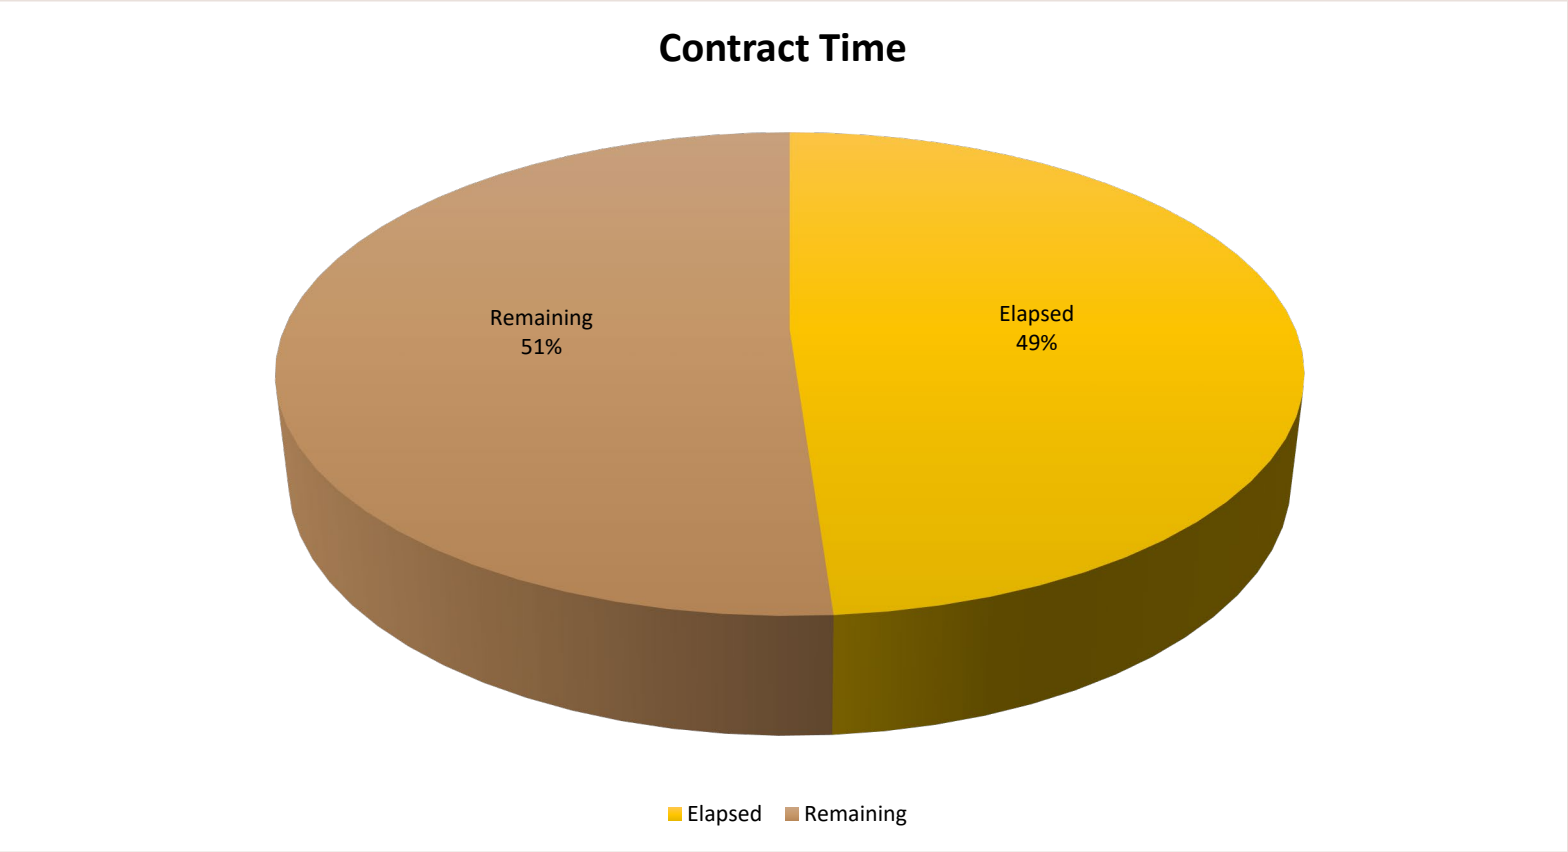

Total Contract time: 710 days
Elapsed Contact time: 347 days, 49%
Contract Time Remaining: 363 days, 51%
