


Project Name: I-70 Floyd Hill West Section
Project Number: 25175
Date: April 2026 Update

I-70 Floyd Hill West Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

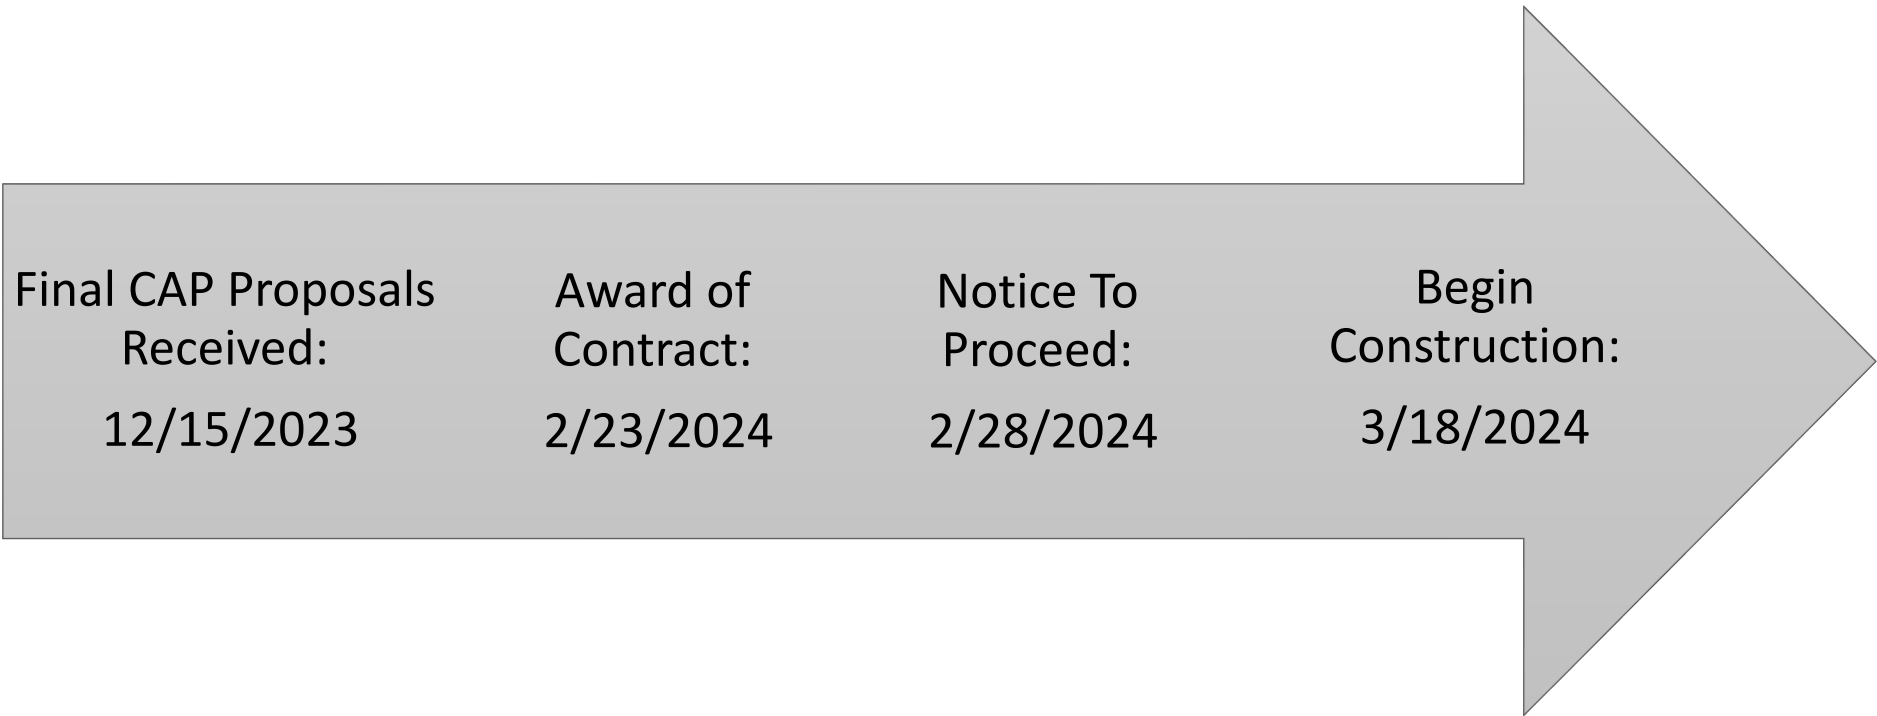

Final CAP Proposals Received: 12/15/2023
Award of Contract: 2/23/2024
Notice To Proceed: 2/28/2024
Begin Construction: 3/18/2024


Project Name: I-70 Floyd Hill West Section

Project Number: 25175

Date: April 2026 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

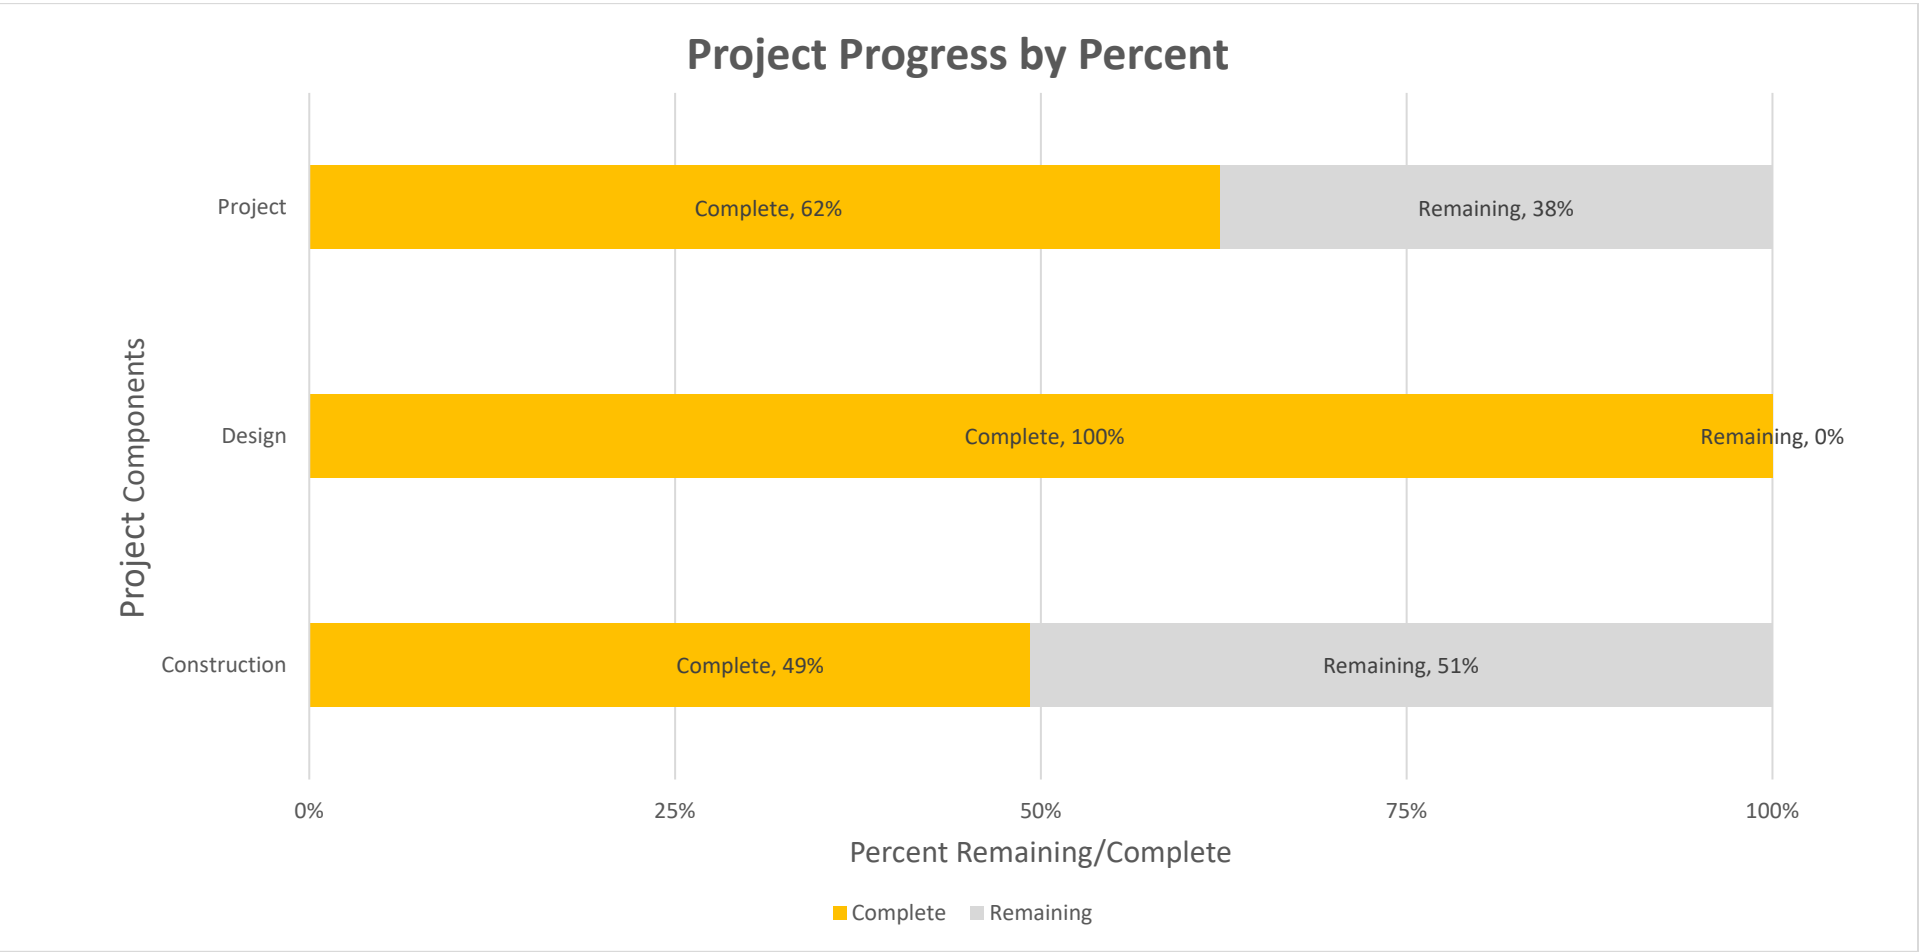

Overall Project: 62% Complete, 38% Remaining

Design: 100% Complete, 0% Remaining

Construction: 49% Complete, 51% Remaining


Project Name: I-70 Floyd Hill West Section

Project Number: 25175

Date: April 2026 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

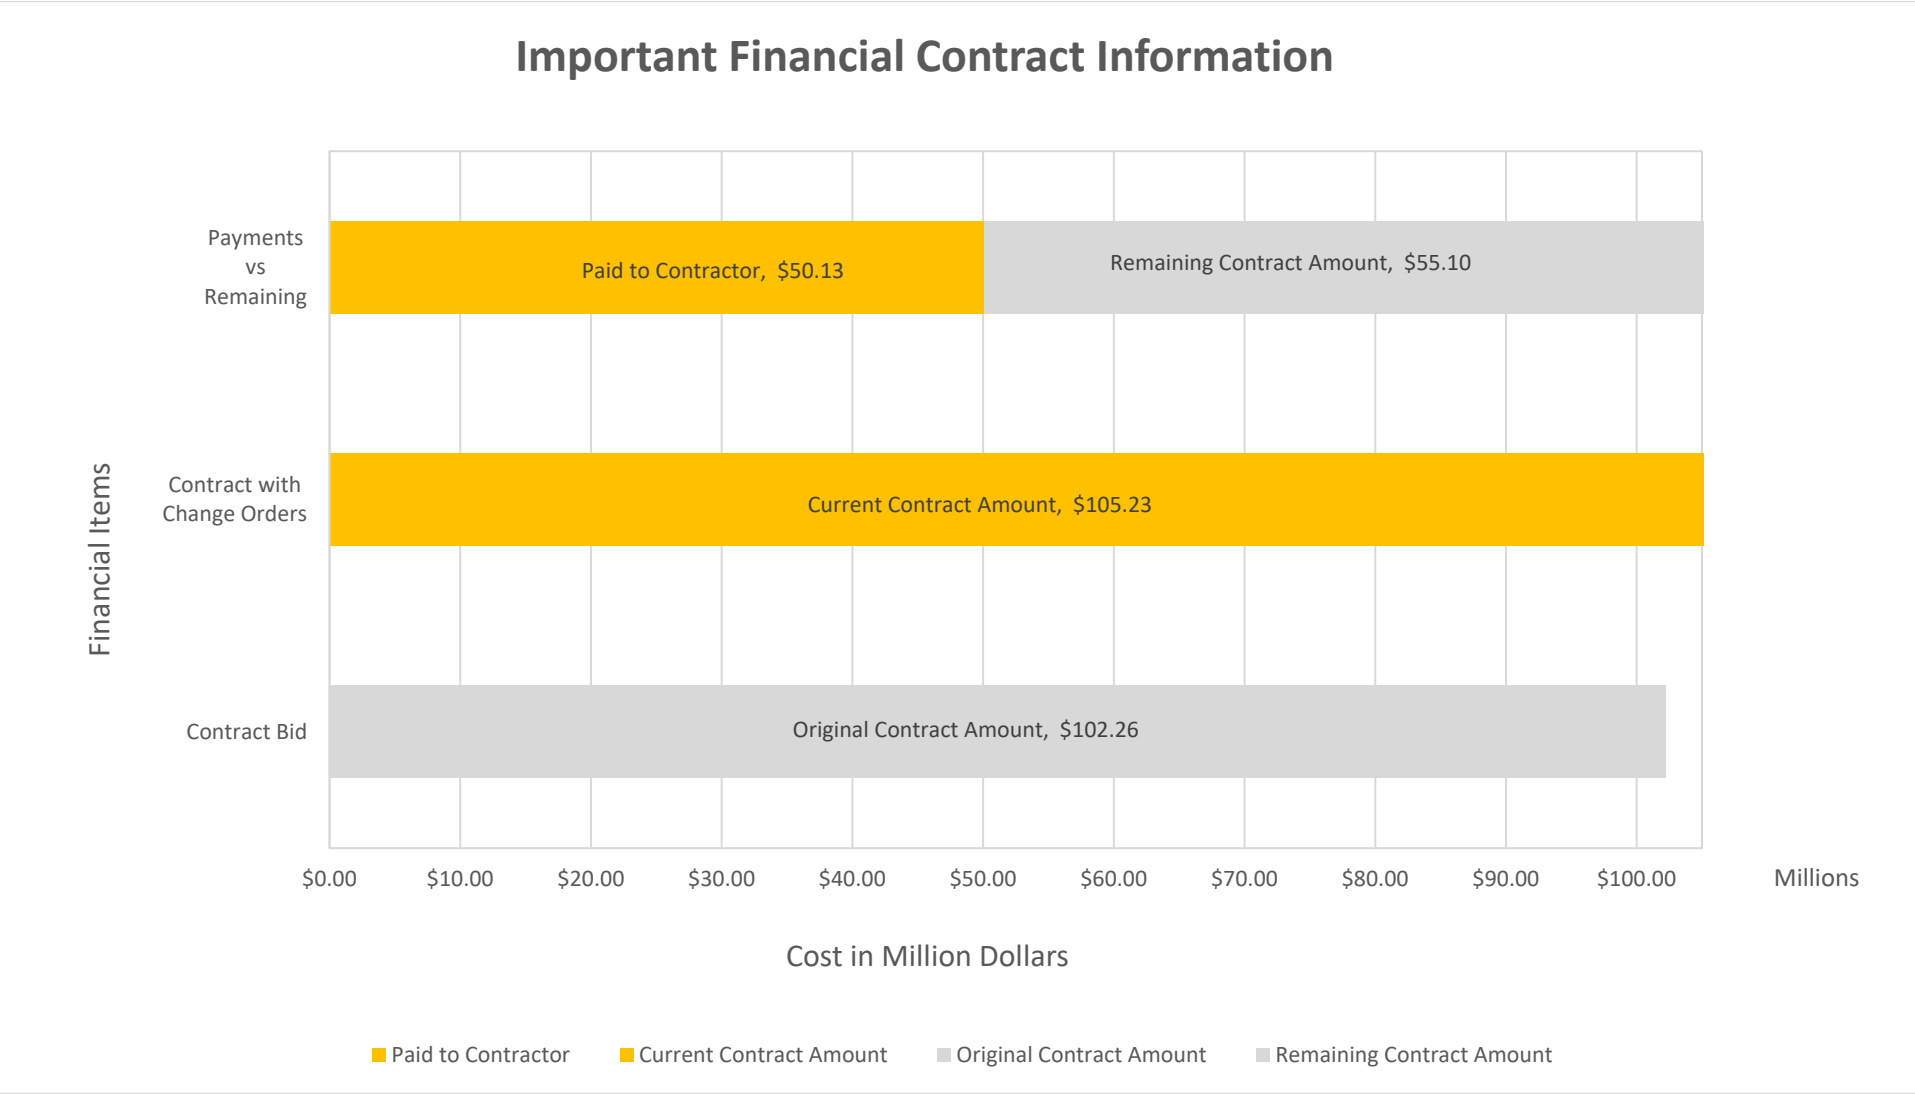

Initial Contract Value: \$105.23 Million


Payments to date: \$50.13 Million, Construction Payments remaining: \$55.10 Million

Current Contract Value: 105.23 Million, Total Change Orders to Date: \$0

Project Name: I-70 Floyd Hill West Section
Project Number: 25175
Date: April 2026 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

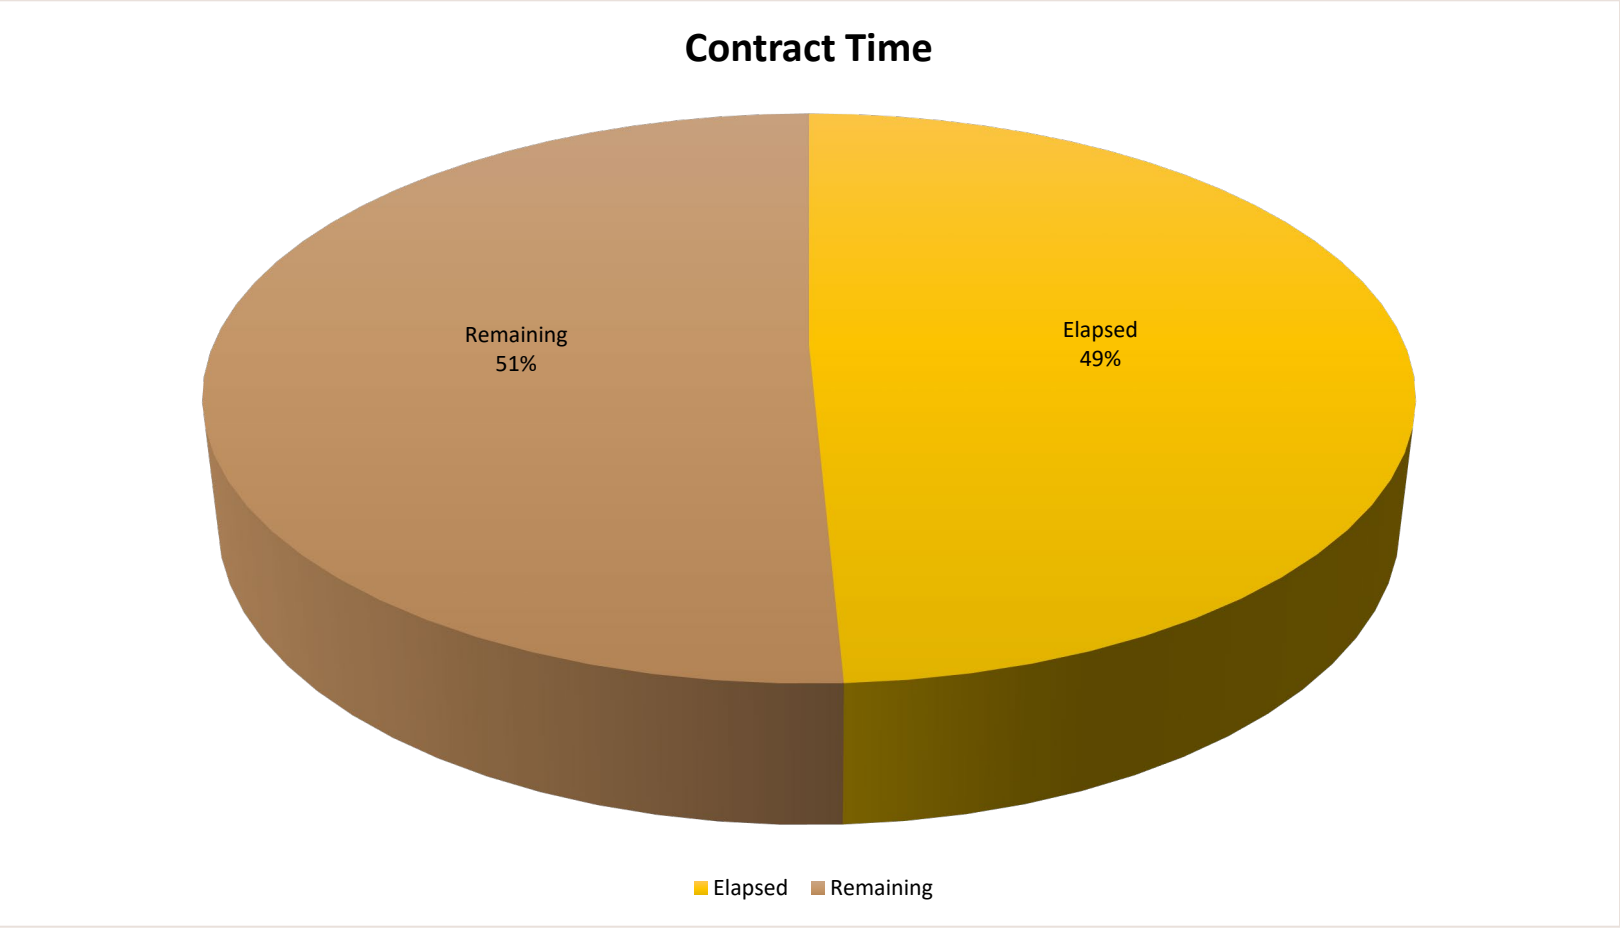

Total Construction Contract time: 1584 days
Elapsed Contact time: 780 days, 49%
Contract Time Remaining: 804 days, 51%
