


Project Name: I-70 Floyd Hill Central Section  
 Project Number: 25177  
 Date: June 2025 Update

### I-70 Floyd Hill Central Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

#### Key Dates

The following image shows the progression of the key project dates.

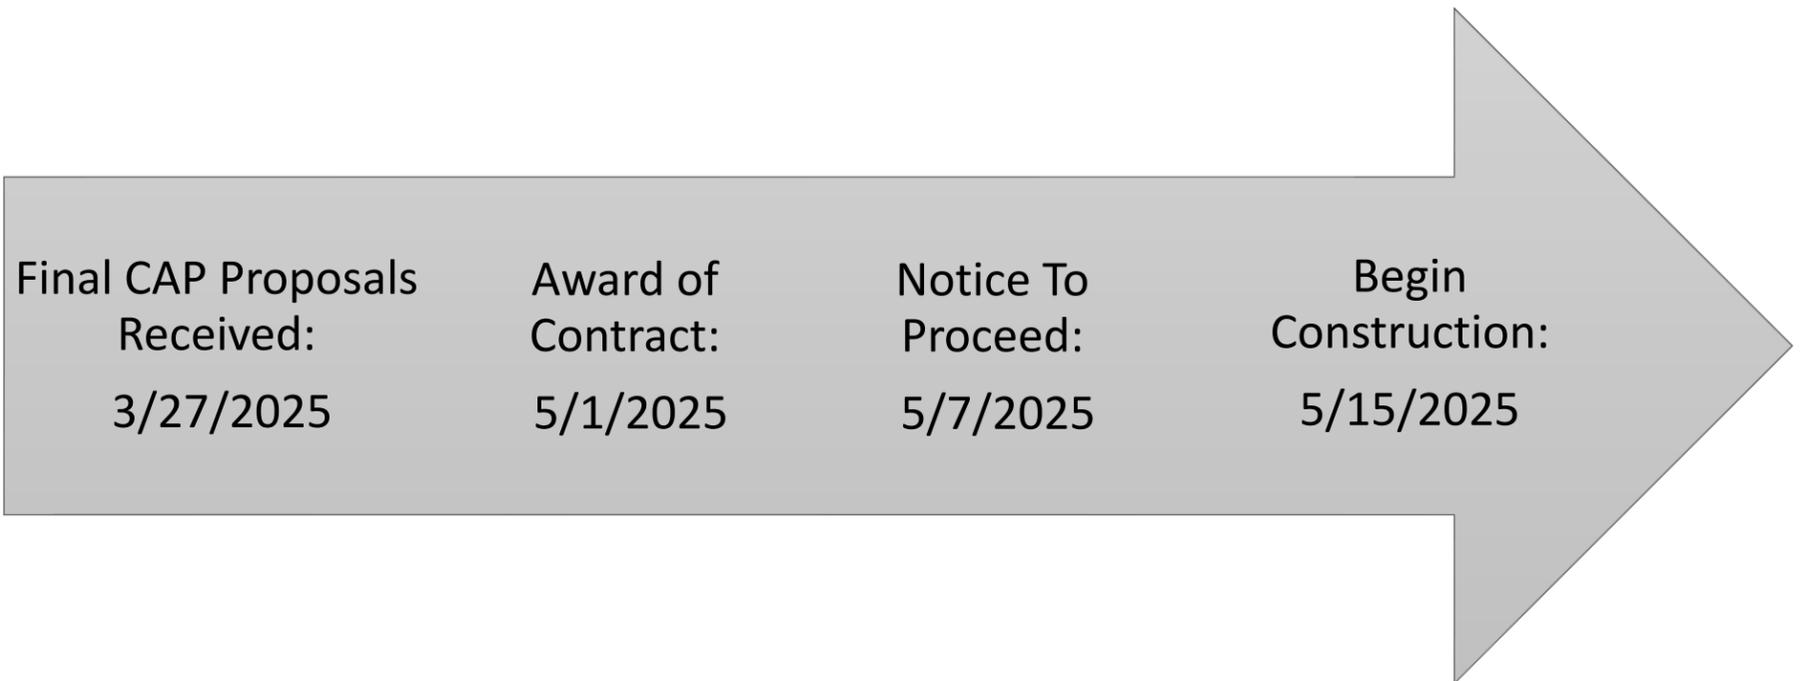

Final CAP Proposals Received: 3/27/2025

Award of Contract: 5/1/2025


Notice To Proceed: 5/7/2025

Begin Construction: 5/15/2025

Project Name: I-70 Floyd Hill Central Section  
 Project Number: 25177  
 Date: June 2025 Update

### Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

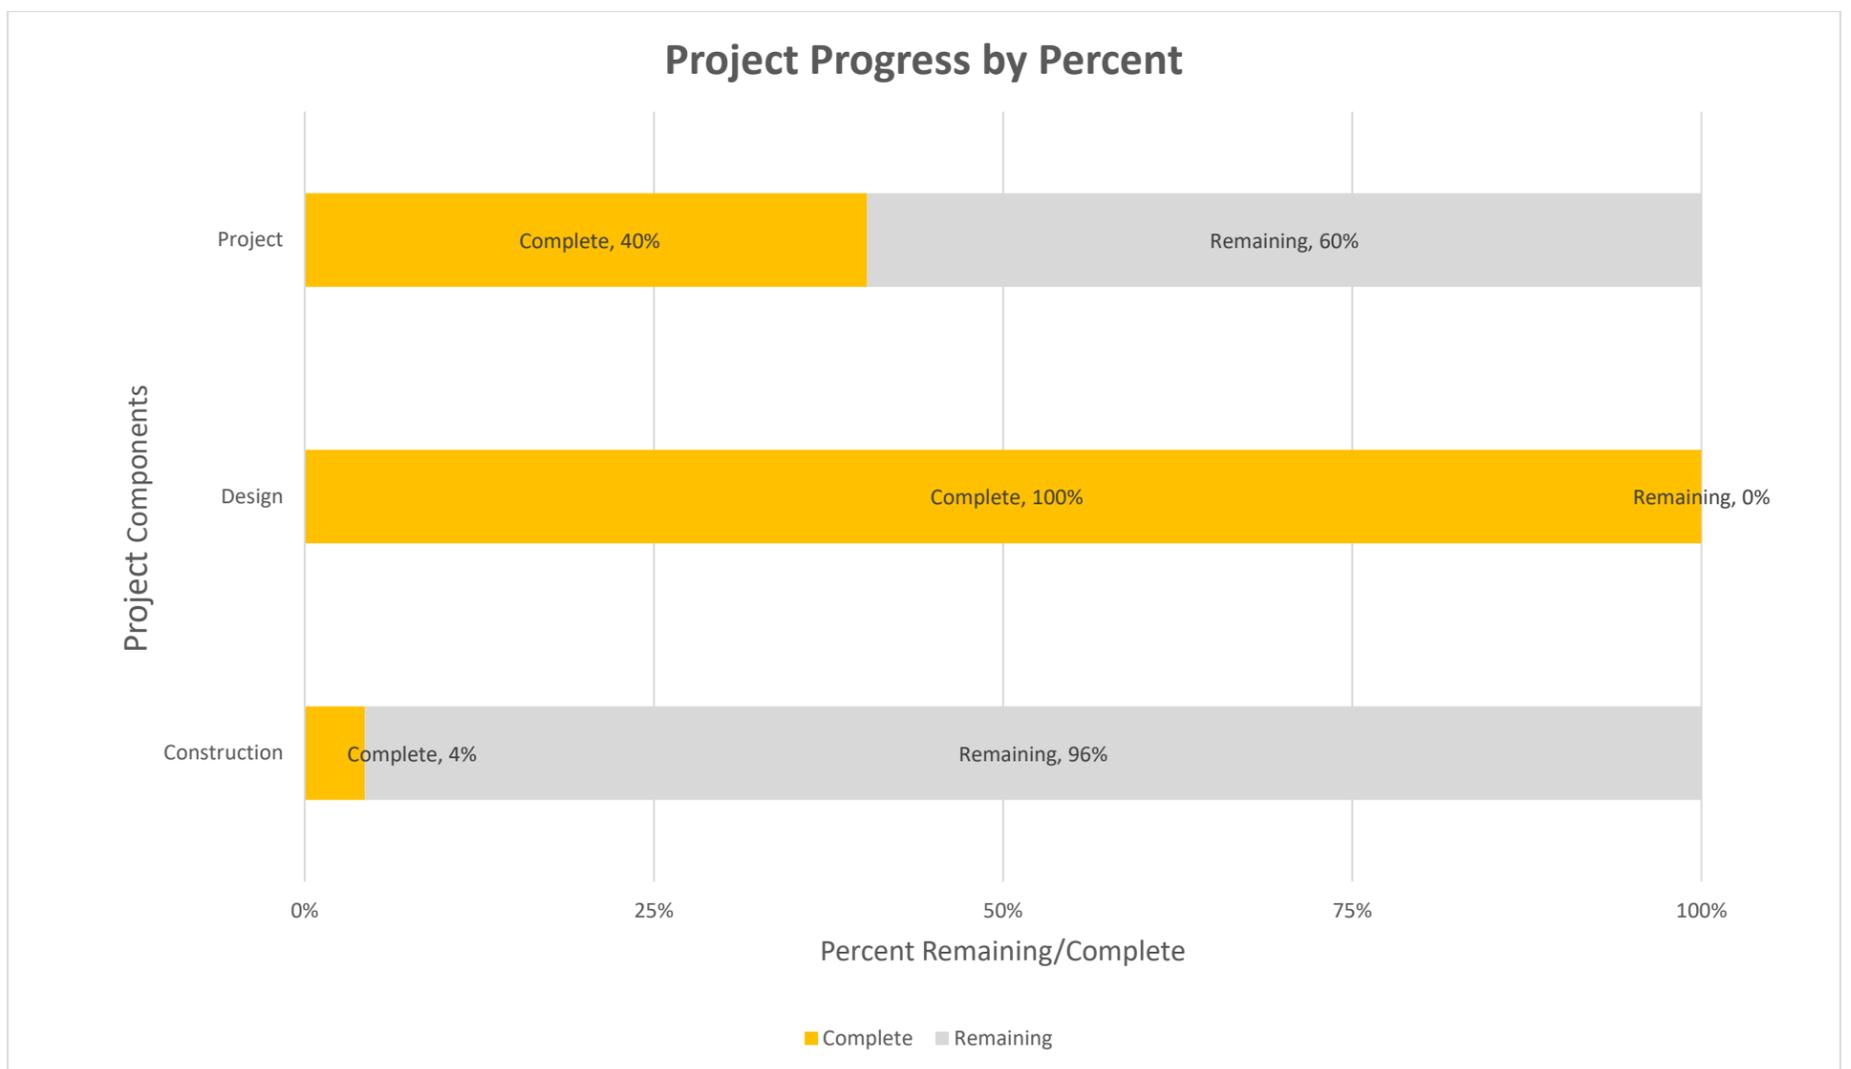

Overall Project: 40% Complete, 60% Remaining

Design: 100% Complete, 0% Remaining


Construction: 4% Complete, 96% Remaining



Project Name: I-70 Floyd Hill Central Section  
 Project Number: 25177  
 Date: June 2025 Update

### Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

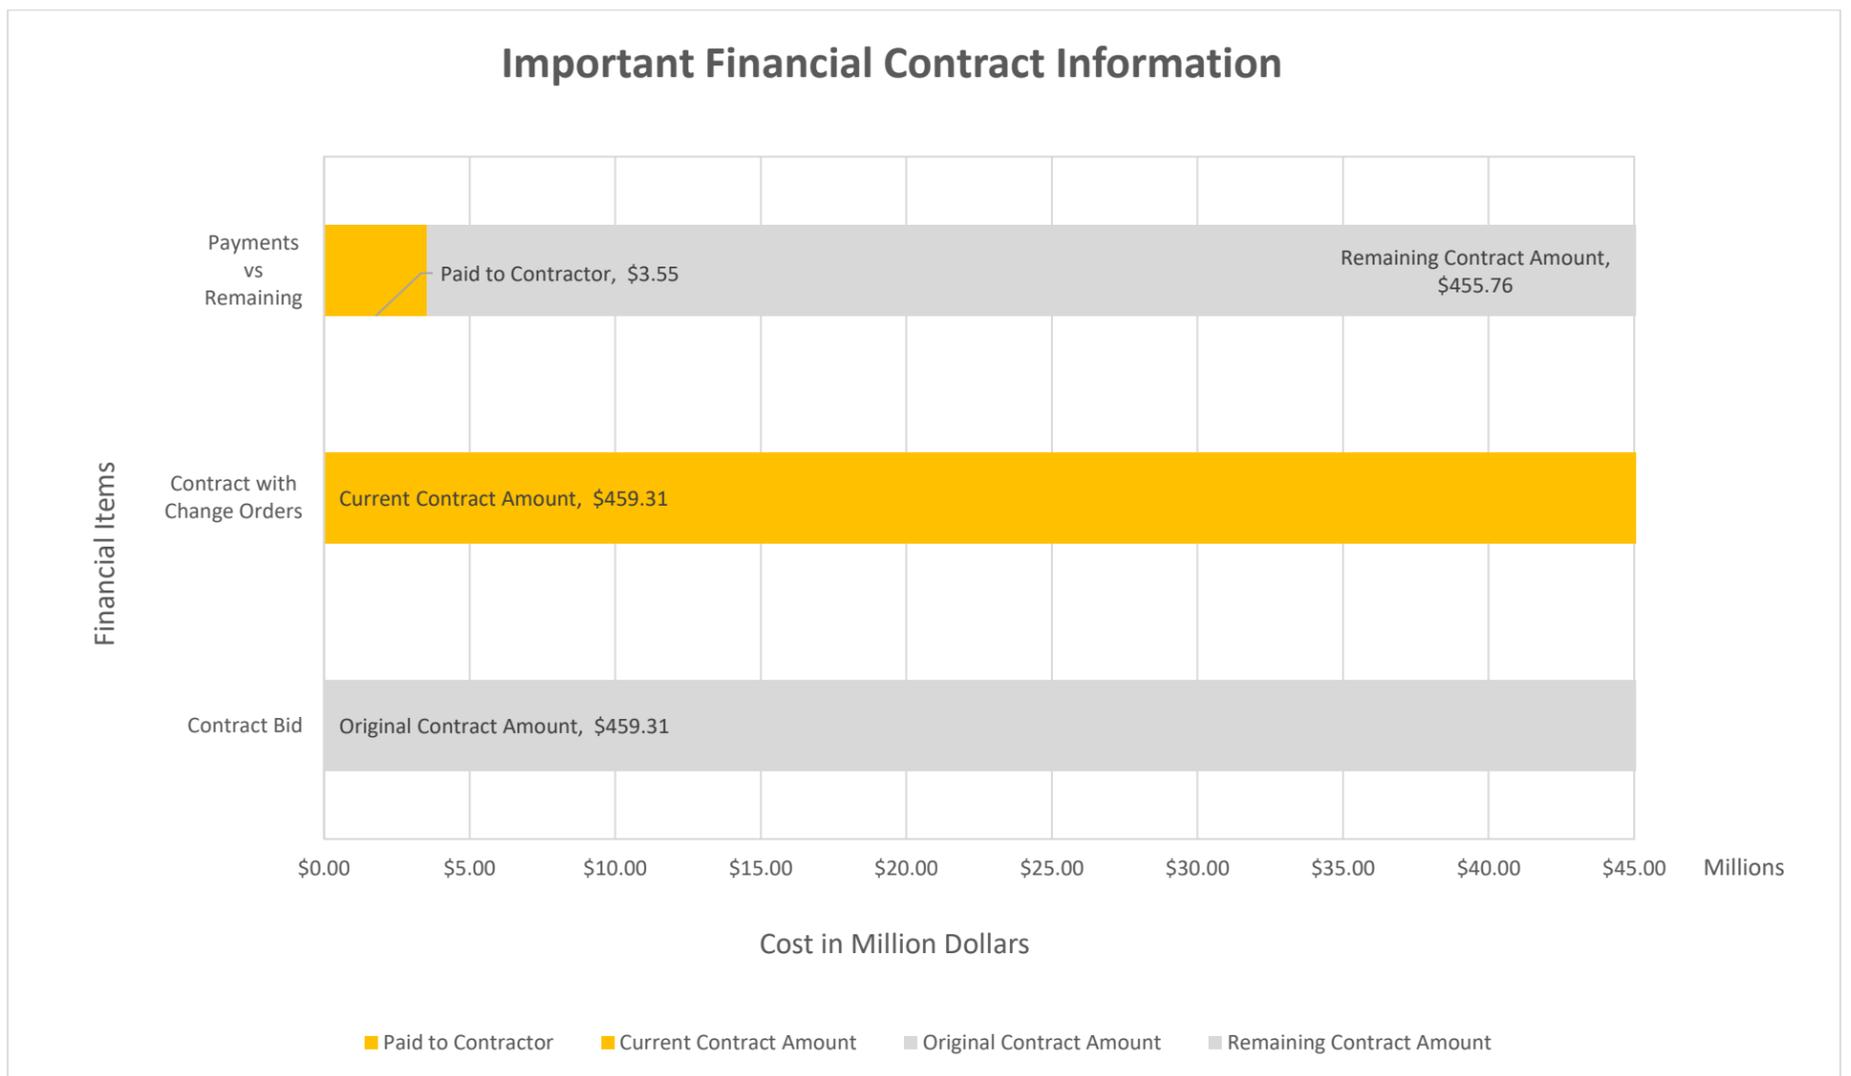

Initial Contract Value: \$459.31 Million

Payments to date: \$3.55 Million, Payments remaining: \$455.76 Million

Current Design Value: \$459.31 Million, Total Change Orders to Date: \$0




Project Name: I-70 Floyd Hill Central Section

Project Number: 25177

Date: June 2025 Update

## Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

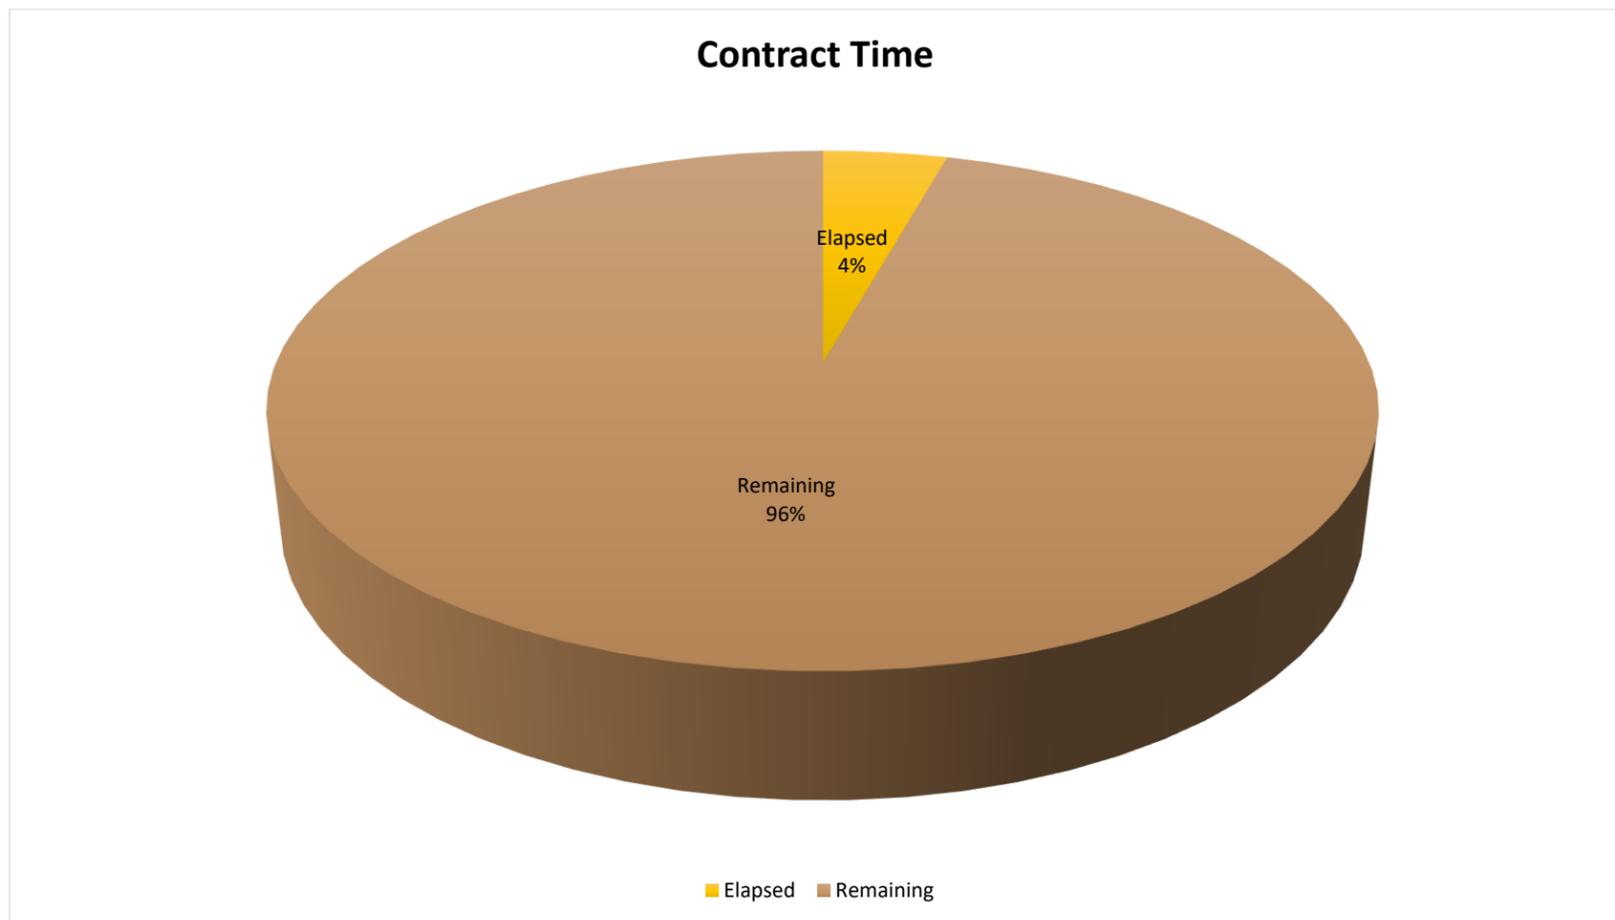

Total Contract time: 1251 days

Elapsed Contact time: 54 days, 4%

Contract Time Remaining: 1197 days, 96%
