



## North I-25 Segment 5: Mead to Berthoud (CO 66 to CO 56) Delivery: CMGC

### I. Project Dashboard

The purpose of this document is to provide a progress and financial update pertaining to the design and construction of the North I-25 Segment 5 Project and the following associated project numbers:

- **Design:** Project Number 24309
- **Construction Package 1:** Project Number 25986
- **Construction Package 2:** Project Number 25987


### II. Milestone Dates

#### Design







## Construction Package 1

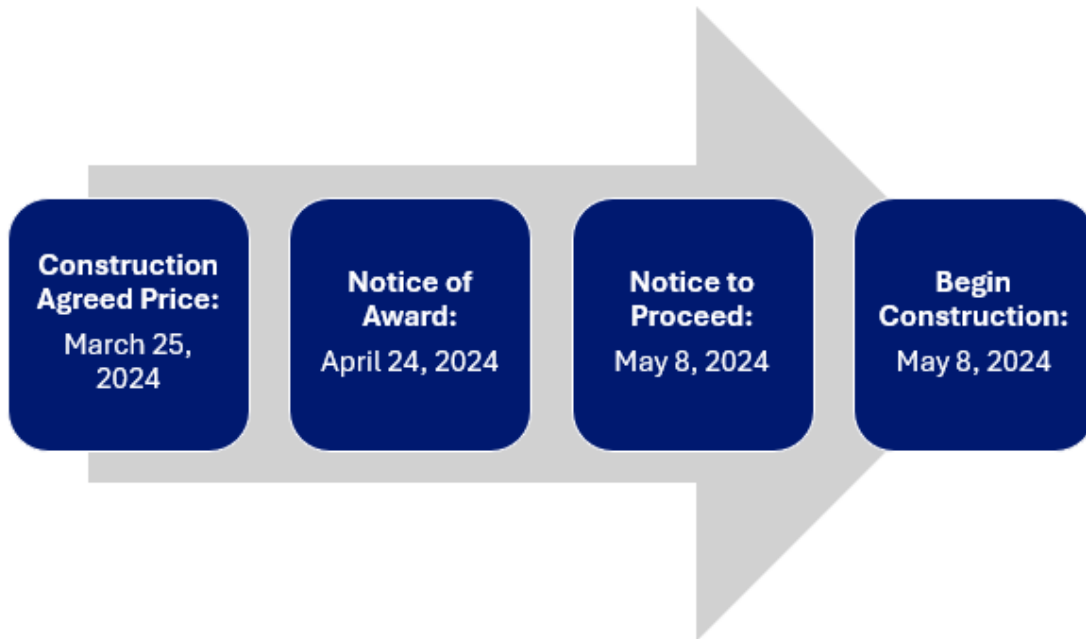

## Construction Package 2

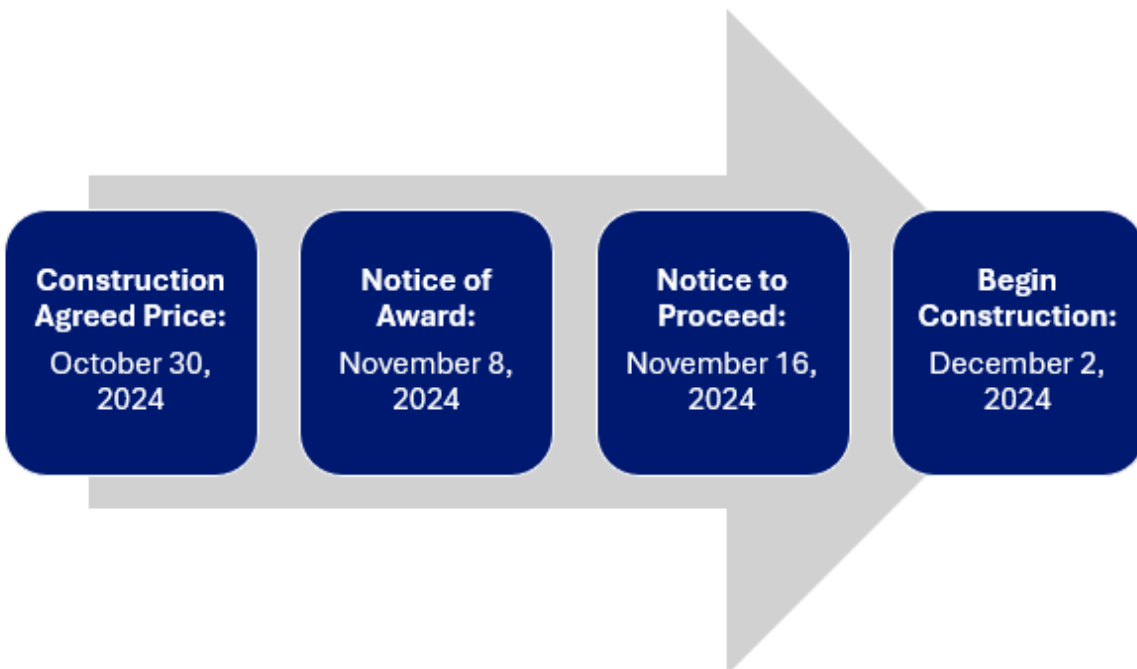

### III. Project Progress by Percent

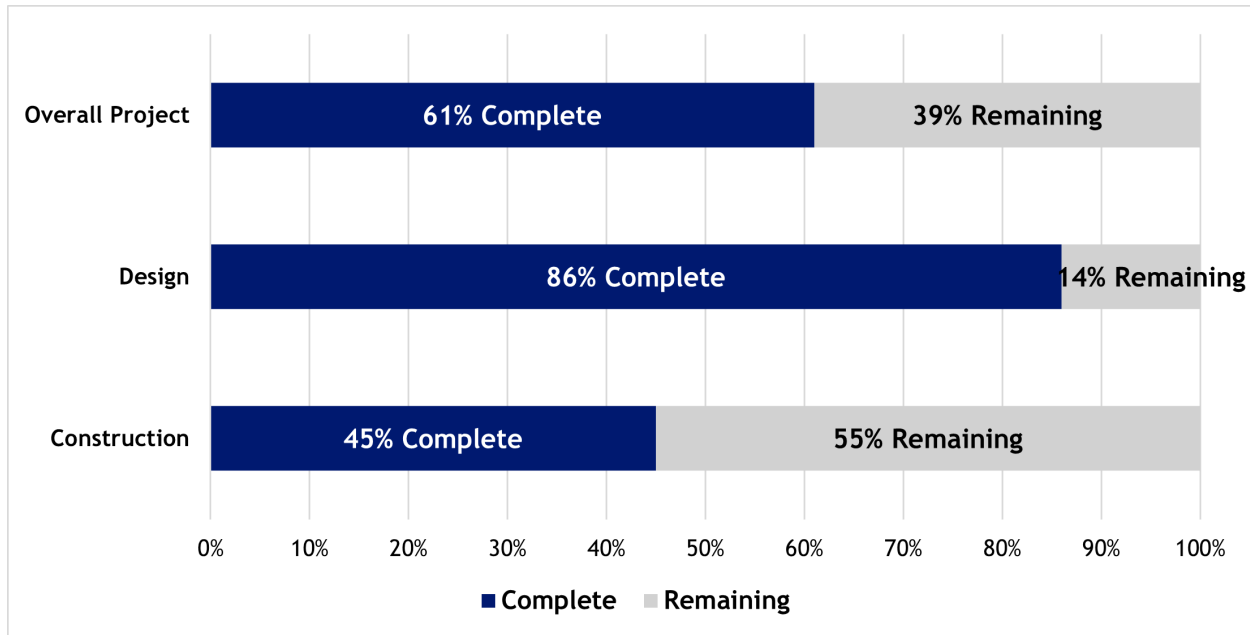


### IV. Financial Contract Information


The following bar charts display the project construction payments versus remaining funds, the current contract total, and the original contract amount for Construction Package 1 and Construction Package 2. There have been no change orders to date.



## Construction Package 1

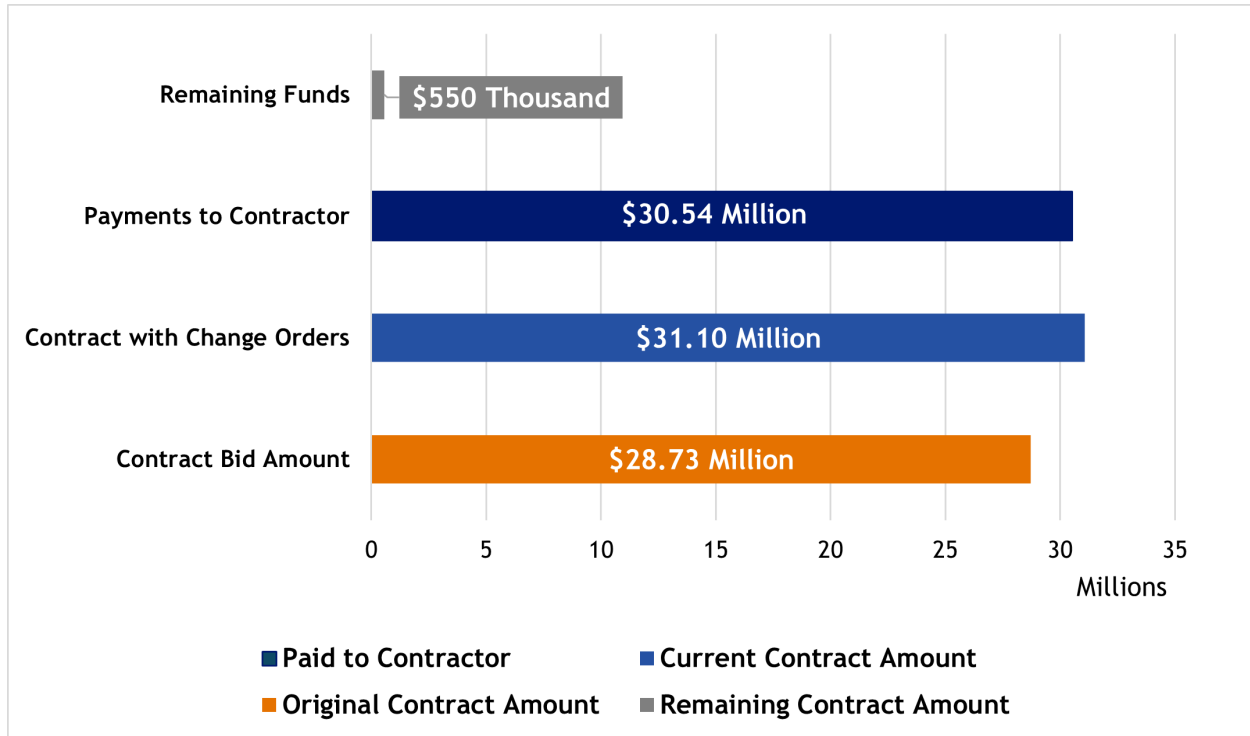


## Construction Package 2

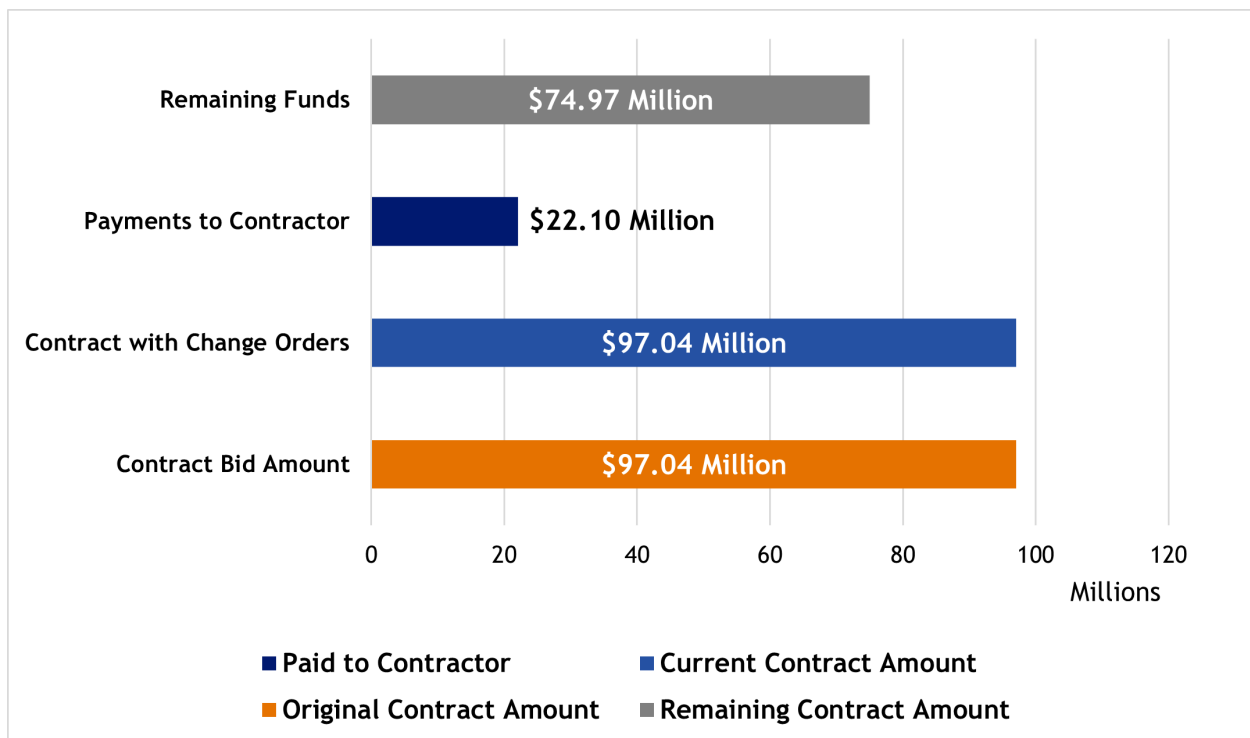

## V. Contract Time


### Design

The Notice-to-Proceed (NTP) was granted on August 31, 2023. The contract expiration date is May 4, 2028. The total contract time is 1708 days.

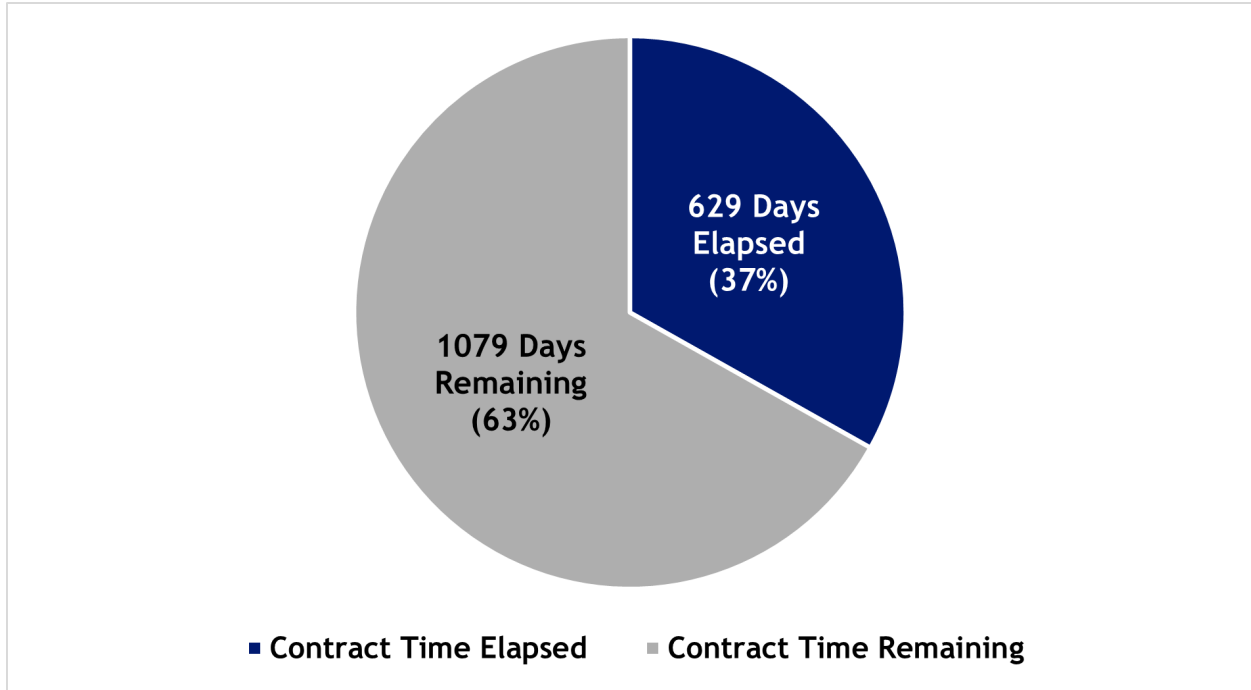

### Construction Package 1 - Complete


The fixed completion date for Construction Package 1 is May 30, 2025. The total contract time is 387 days.

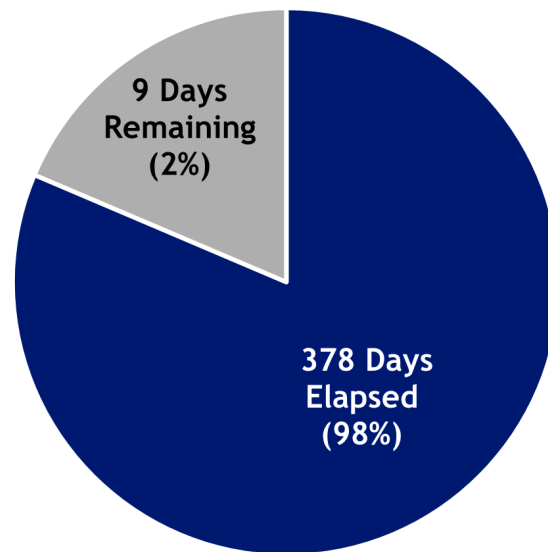

■ Contract Time Elapsed    ■ Contract Time Remaining

## Construction Package 2

The fixed completion date for Construction Package 2 is June 30, 2027. The total contract time is 956 days.

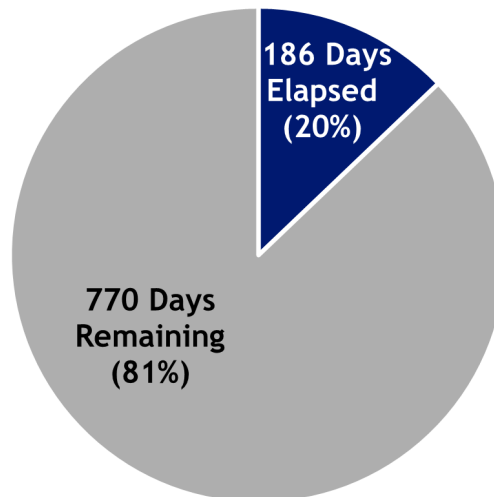

■ Contract Time Elapsed    ■ Contract Time Remaining
