

Region 2 Bridge Bundle Project - May 2023 Dashboard

Project Timeline - Figure 1
Preconstruction through construction start

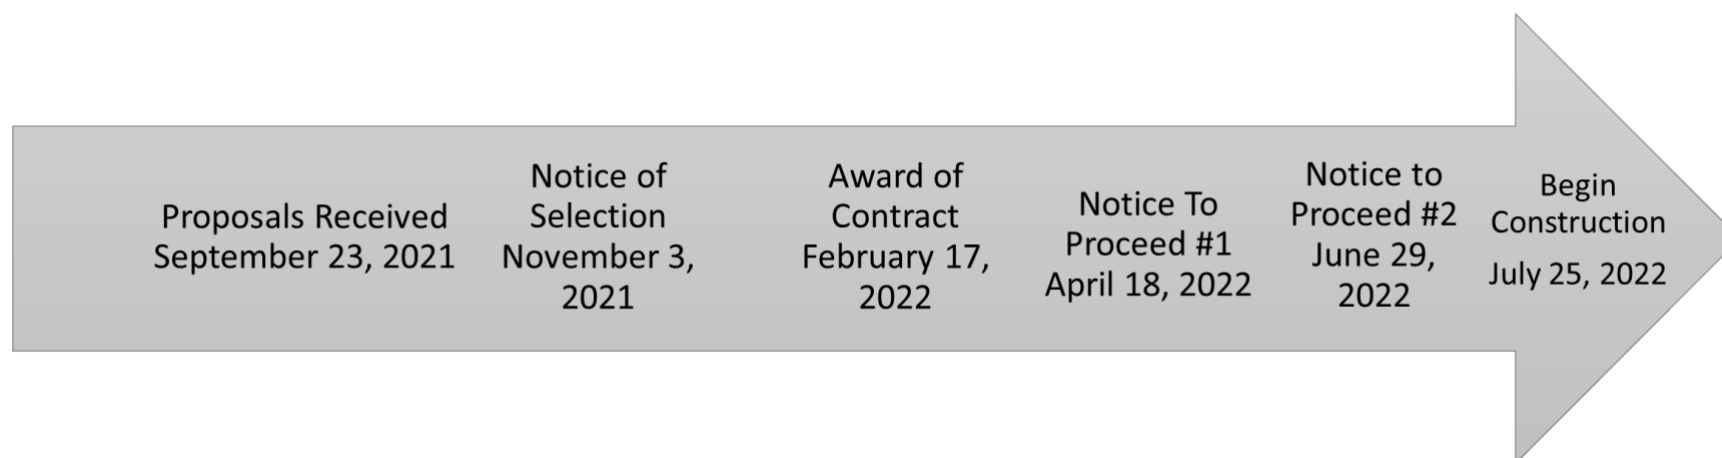


Figure 1: Project timeline showing major project milestones. The timeline starts at proposals received on September 23, 2021 and currently extends to the beginning of construction on July 25, 2022.

May 2023 Progress - Figure 2
Project, design and construction progress

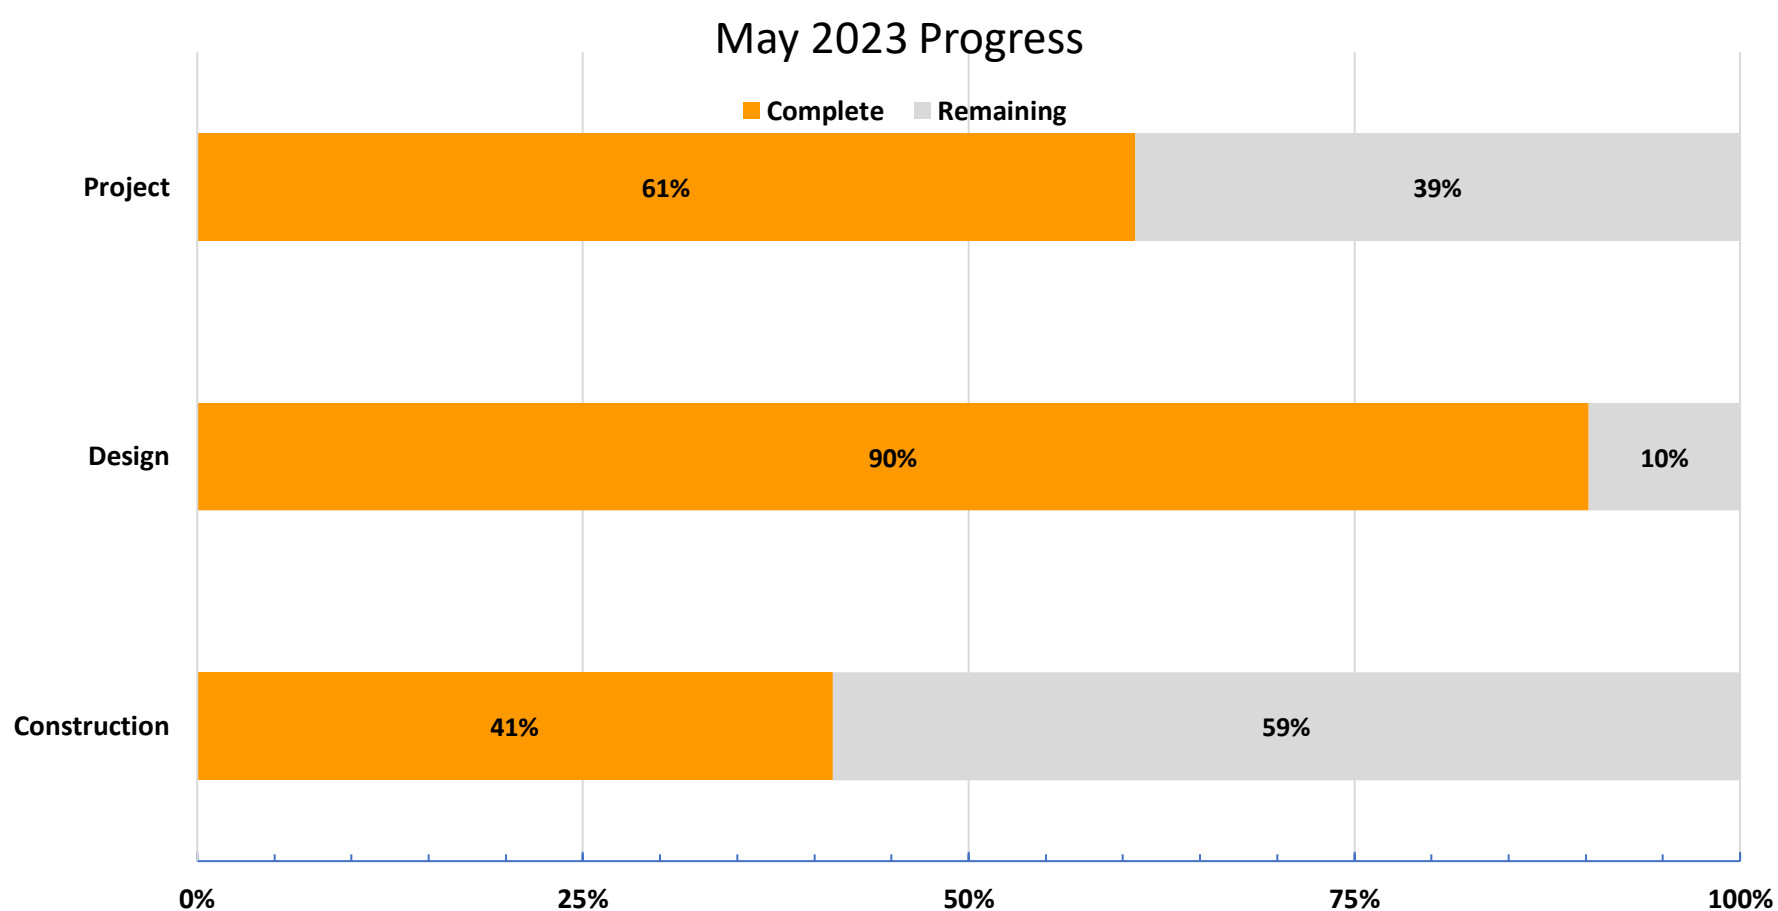


Figure 2: Project progress as of May 2023. The overall project is currently 61% complete - design is 90% complete and construction is 41% complete. Project completion is slated for the end of 2024.

Current Budget - May 2023 - Figure 3
 Payments made, contract with change orders and overall contract bid

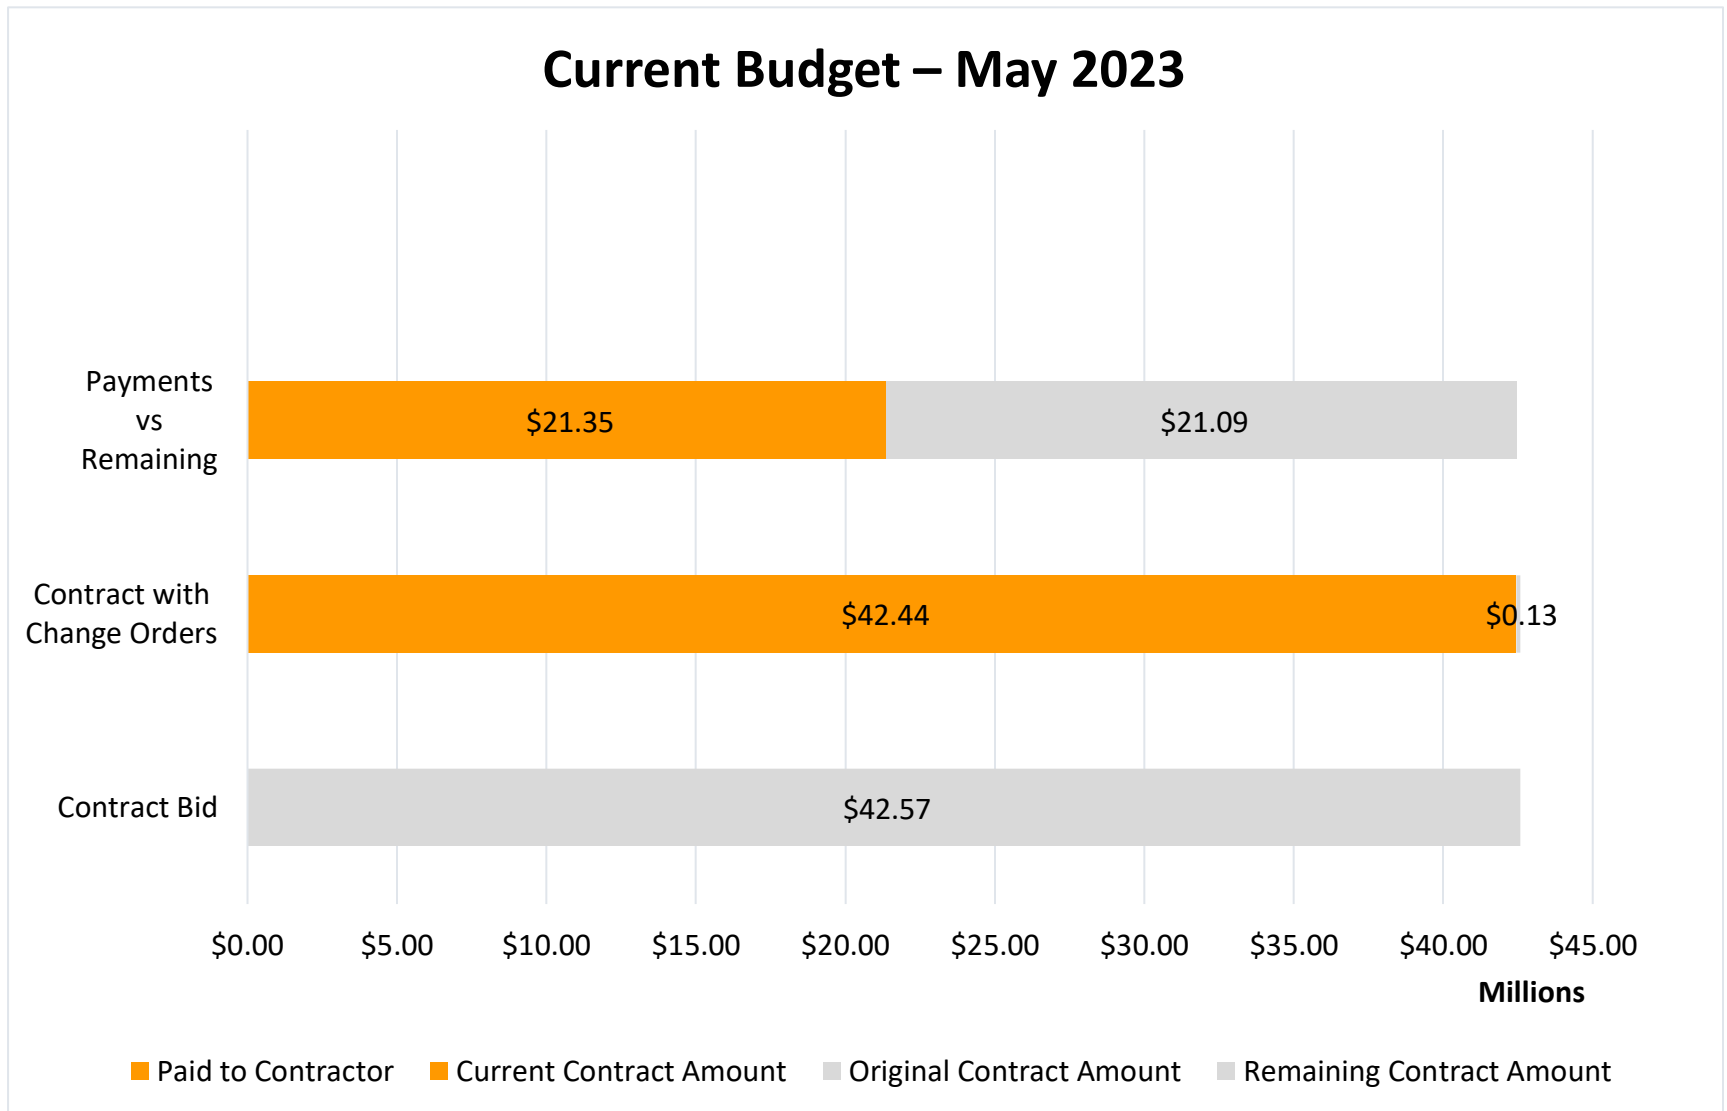


Figure 3: Current budget as of May 2023. The contract was bid at \$42.57 million with change orders. \$21.35 million has been paid to date.

Contract Time 921 Calendar Days - Figure 4
 Percent remaining on the project versus percent elapsed



Figure 4: The percentage of time remaining on the contract out of 921 calendar days. 56% of contract time remains on the project as of May 2023.
