

Project Name: US 6D STR F-06-A Elk Creek - New Castle
 Project Number: 24493, FBR 0063-066
 Date: March, 2026 Update

US 6D STR F-06-A Elk Creek - New Castle Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.



Proposal Received: March 10, 2023

Notice of Selection: March 31, 2023

Award of Contract: August 28, 2023

Notice to Proceed #1: September 18, 2025




Project Name: US 6D STR F-06-A Elk Creek - New Castle

Project Number: 24493, FBR 0063-066

Date: March, 2026 Update

Project Progress by Percent

The following figure shows the percent complete and remaining for the overall project, design, and construction.

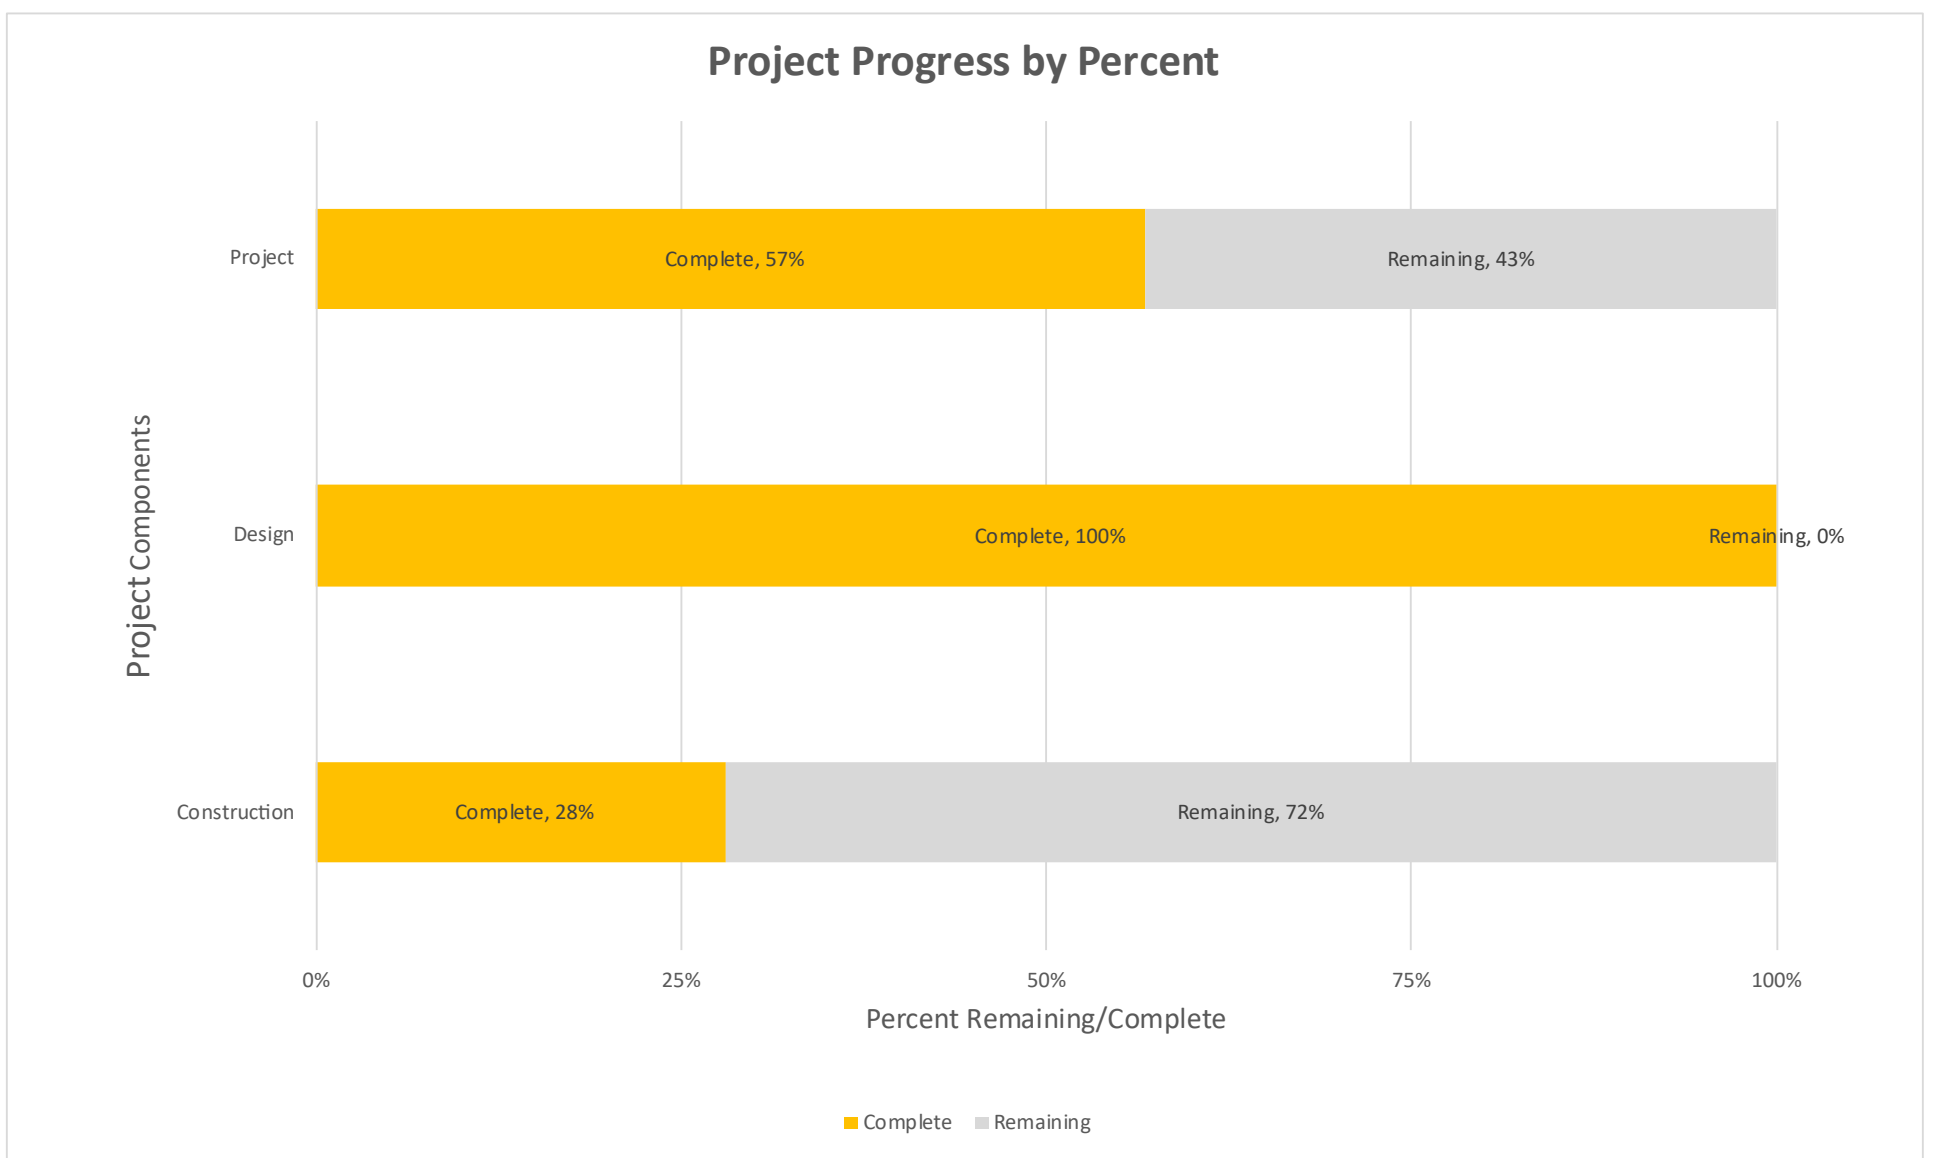

Overall Project: 57% Complete, 43% Remaining


Design: 100% Complete, 0% Remaining

Construction: 28% Complete, 72% Remaining

Project Name: US 6D STR F-06-A Elk Creek - New Castle
 Project Number: 24493, FBR 0063-066
 Date: March, 2026 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract's bid amount.

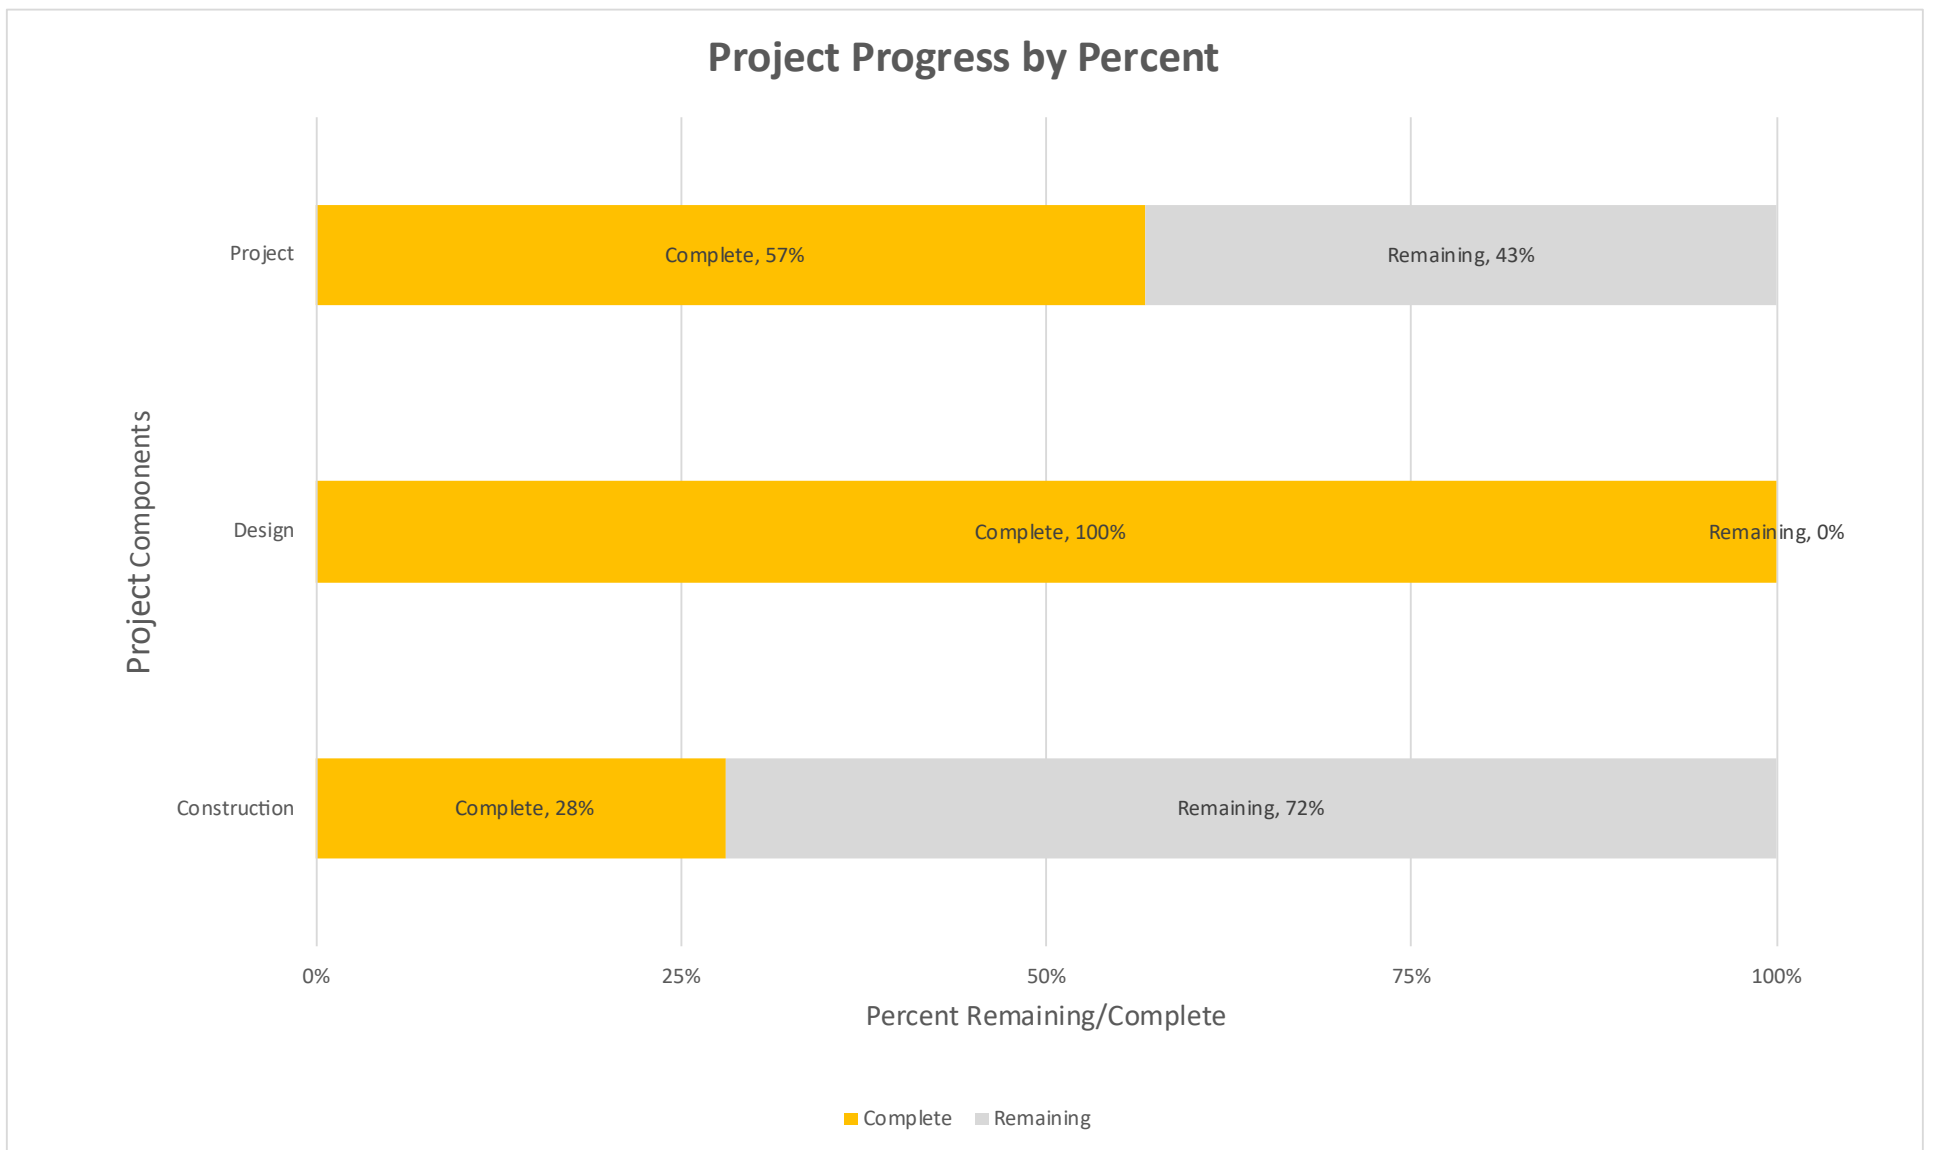

Initial Contract Value: \$10.09 Million

Payments to date: \$1.92 Million, Payments remaining \$8.41 Million

Current Contract Value: \$10.33 Million, Total Change Orders to Date: (\$0.24) Million

Initial Contract Value: \$10.09 Million


Project Name: US 6D STR F-06-A Elk Creek - New Castle

Project Number: 24493, FBR 0063-066

Date: March, 2026 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

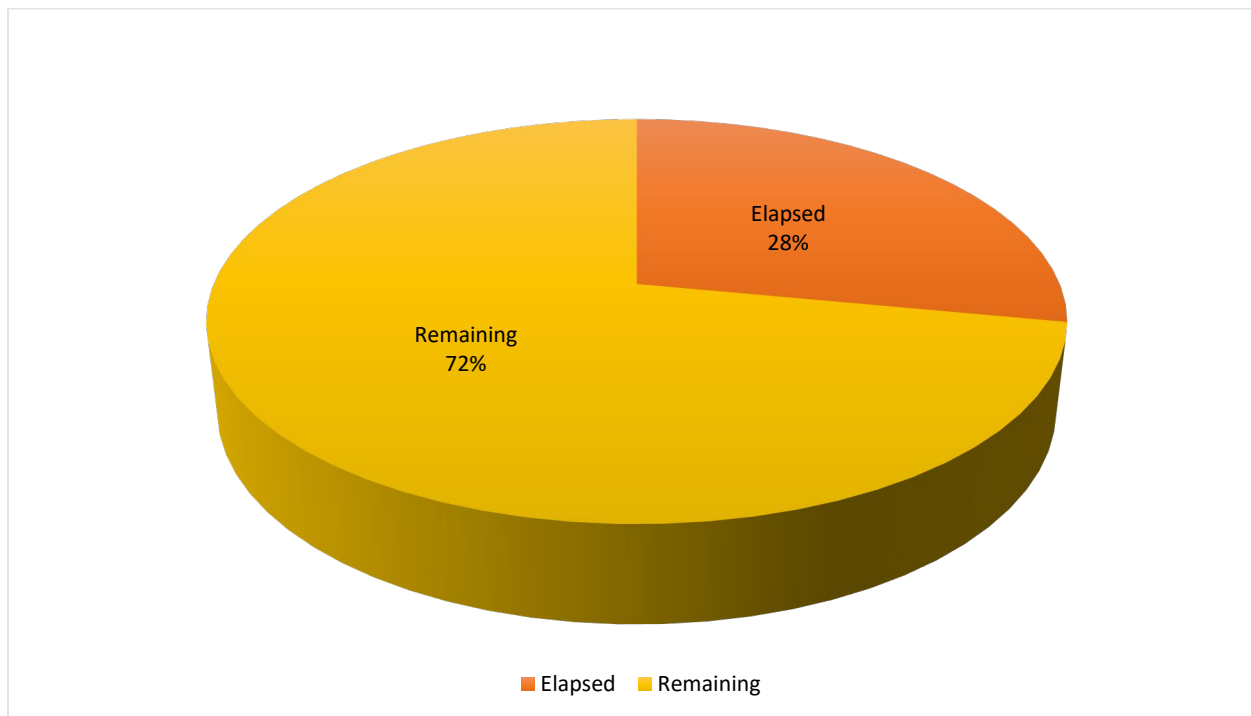

Total Contract time: 425 Calendar Days

Elapsed Contact time: 119 days, 28%

Contract Time Remaining: 306 days ,72%
