

Project Name: US 6D STR F-06-A Elk Creek - New Castle
Project Number: 24493, FBR 0063-066
Date: September, 2026 Update

US 6D STR F-06-A Elk Creek - New Castle Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.




Proposal Received: March 10, 2023
Notice of Selection: March 31, 2023
Award of Contract: August 28, 2023
Notice to Proceed #1: September 18, 2025

Project Name: US 6D STR F-06-A Elk Creek - New Castle
Project Number: 24493, FBR 0063-066
Date: September, 2026 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

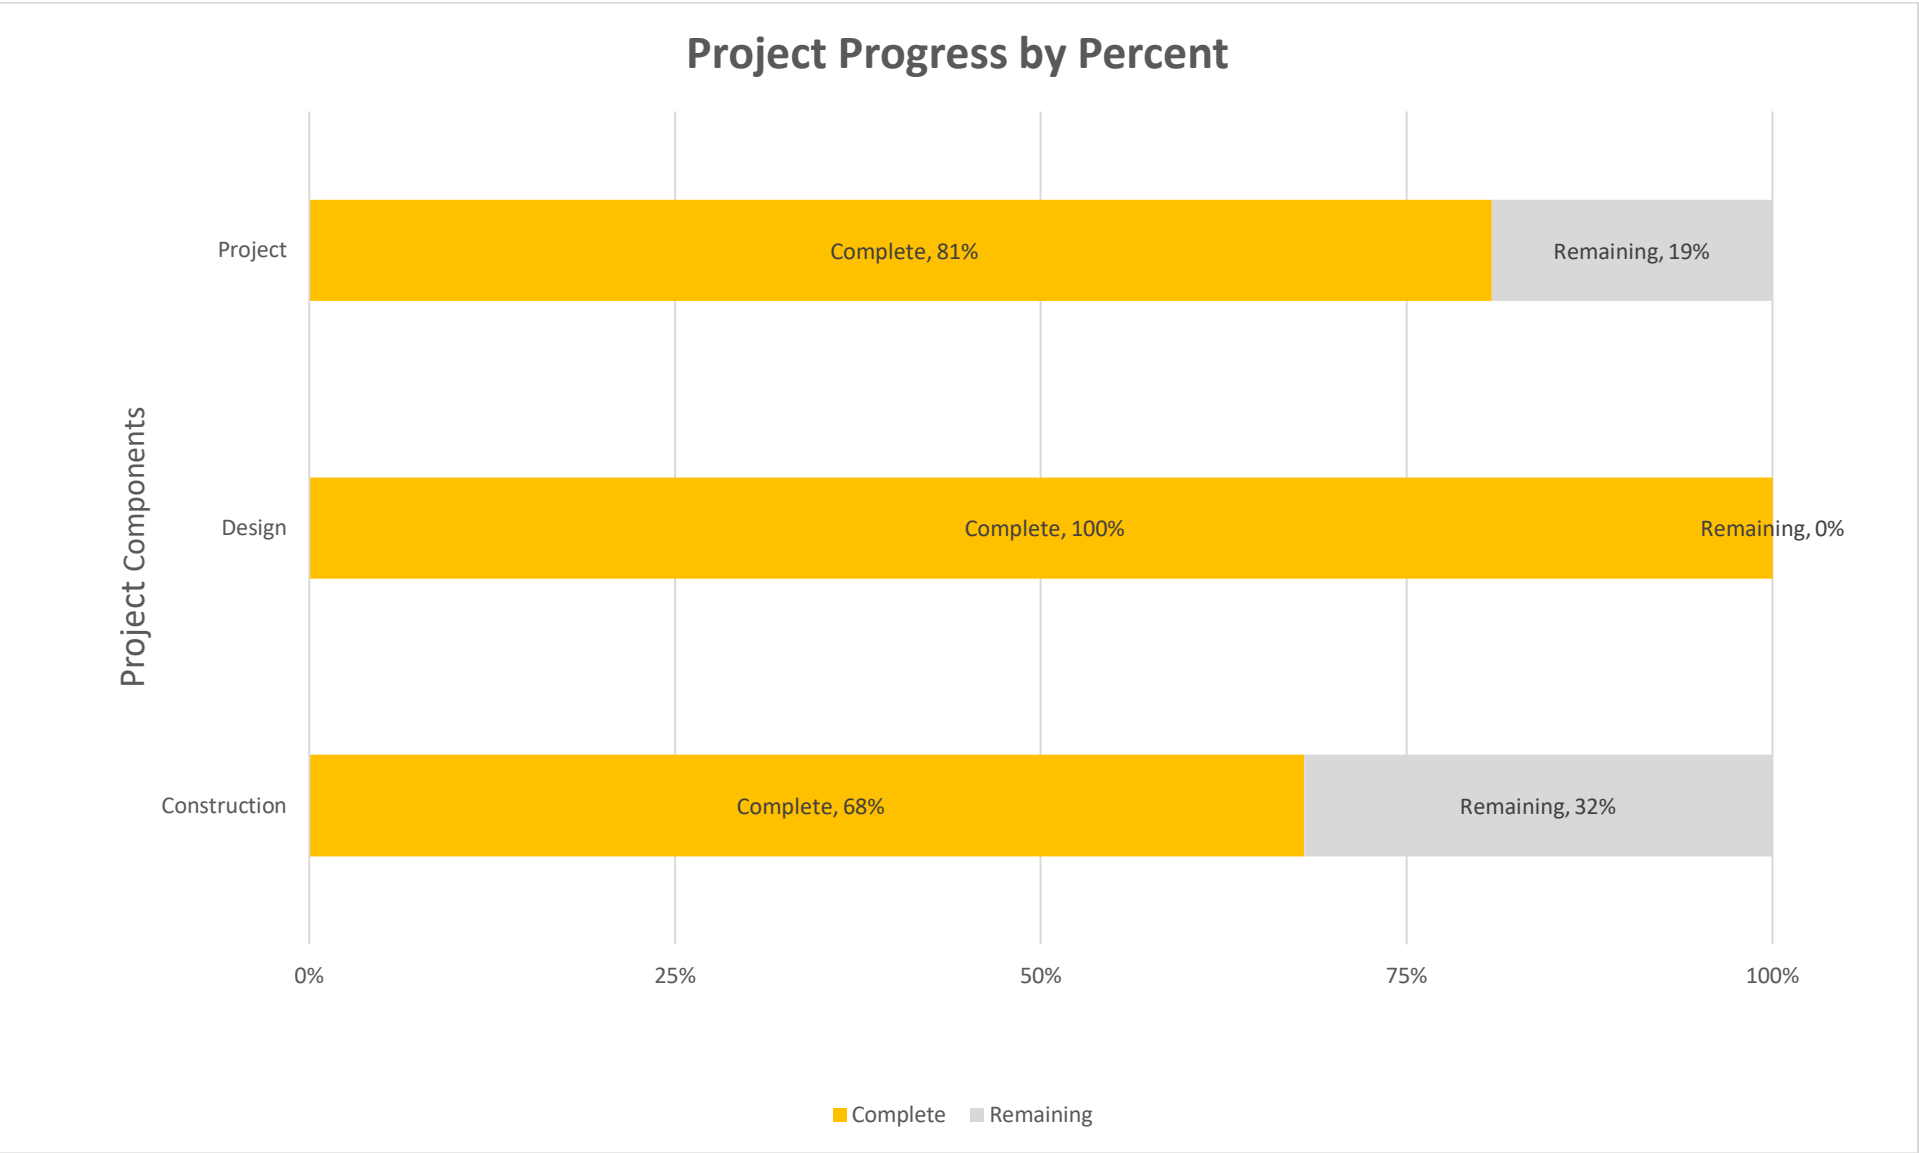

Overall Project: 81% Complete, 19% Remaining
Design: 100% Complete, 0% Remaining
Construction: 68% Complete, 32% Remaining


Project Name: US 6D STR F-06-A Elk Creek - New Castle

Project Number: 24493, FBR 0063-066

Date: September, 2026 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract vale and change orders to date, and contract’s bid amount.

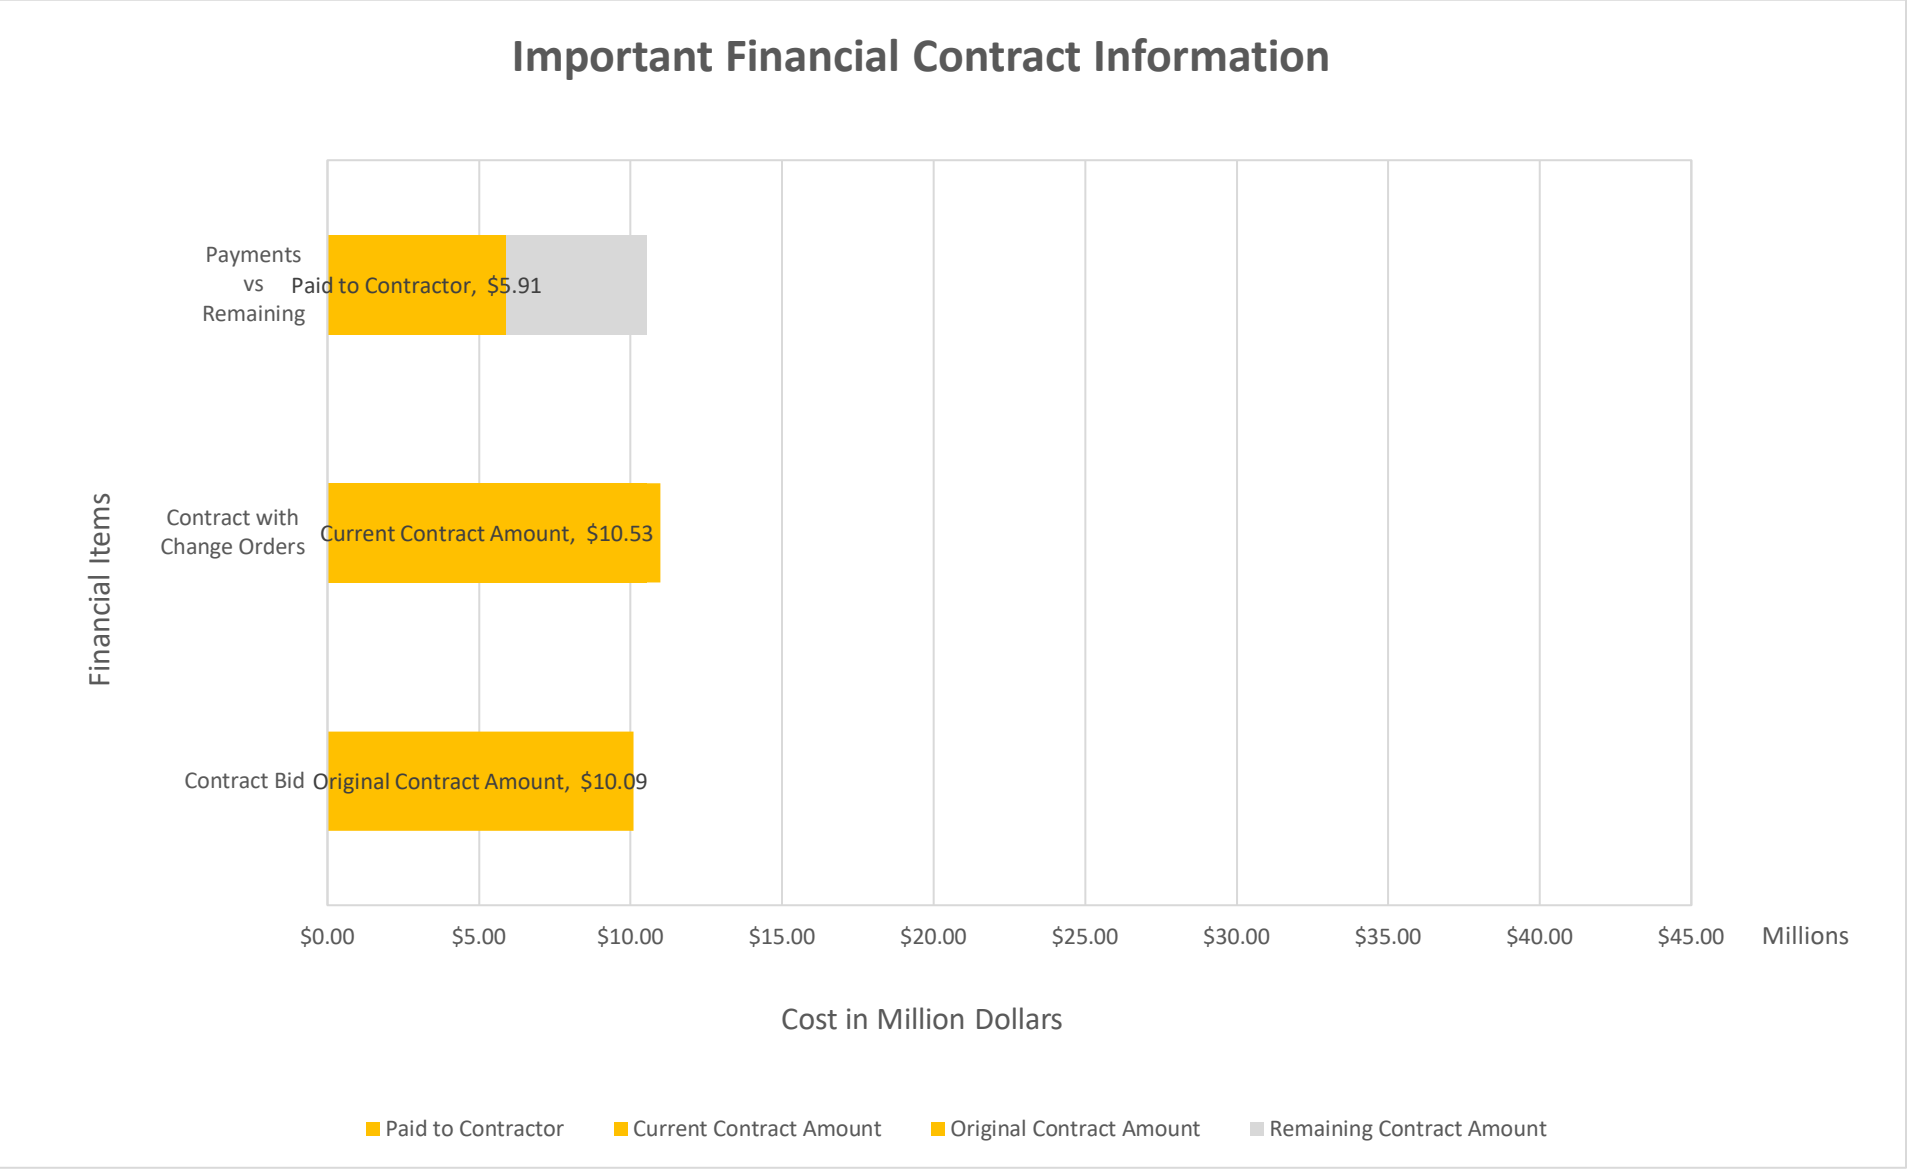

Initial Contract Value: \$10.09 Million

Payments to date: \$5.91 Million, Payments remaining \$4.62 Million


Current Contract Value: \$10.53 Million, Total Change Orders to Date: (\$0.44) Million

Initial Contract Value: \$10.09 Million

Project Name: US 6D STR F-06-A Elk Creek - New Castle
Project Number: 24493, FBR 0063-066
Date: September, 2026 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

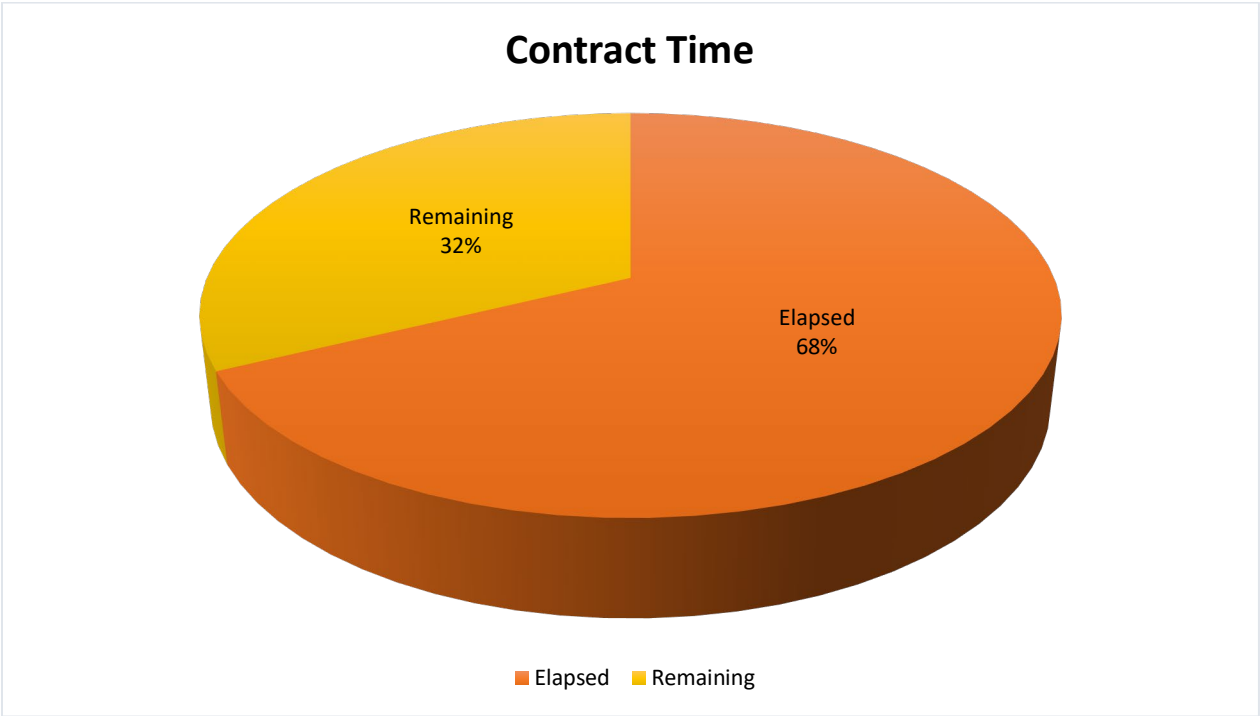

Total Contract time: 425 Calendar Days

Elapsed Contact time: 288 days, 68%

Contract Time Remaining: 137 days ,32%
