


Project Name: Vasquez Blvd – I-270 to 64th Avenue
Project Number: 22922
Date: 7/17/2025 Update

Vasquez Blvd – I-270 to 64th Avenue Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

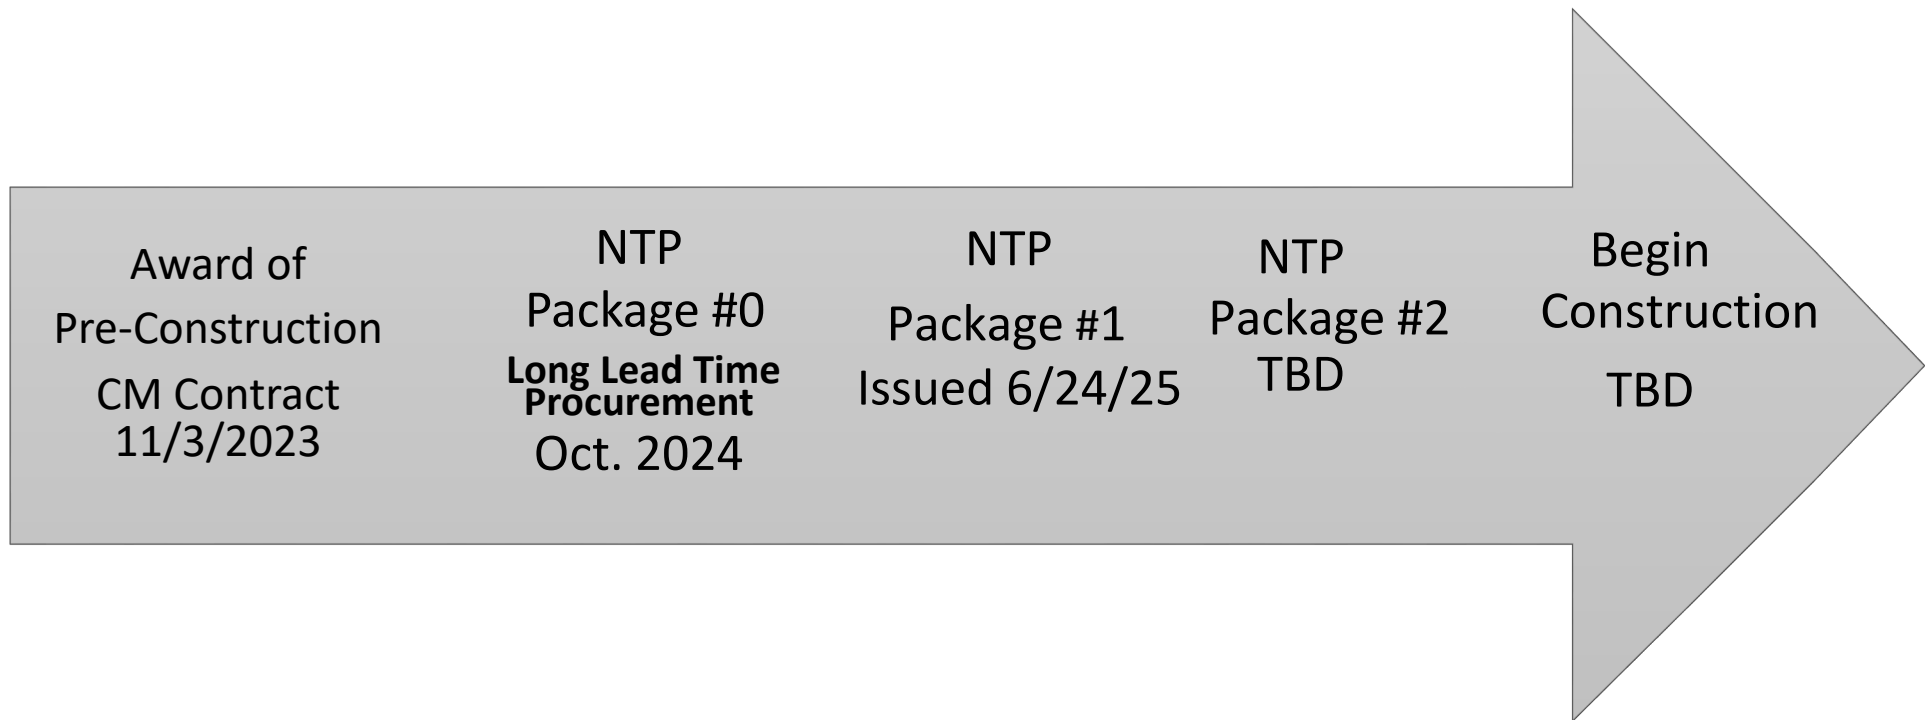

- Award of Pre-Construction CM Contract: 11/3/2023
- Notice to Proceed Package #0: October 2024
- Notice to Proceed Package #1: Issued 6/24/25
- Notice to Proceed Package #2: TBD
- Begin Construction: Package 1 - 7/21/25


Project Name: Vasquez Blvd – I-270 to 64th Avenue

Project Number: 22922

Date: 7/17/2025 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

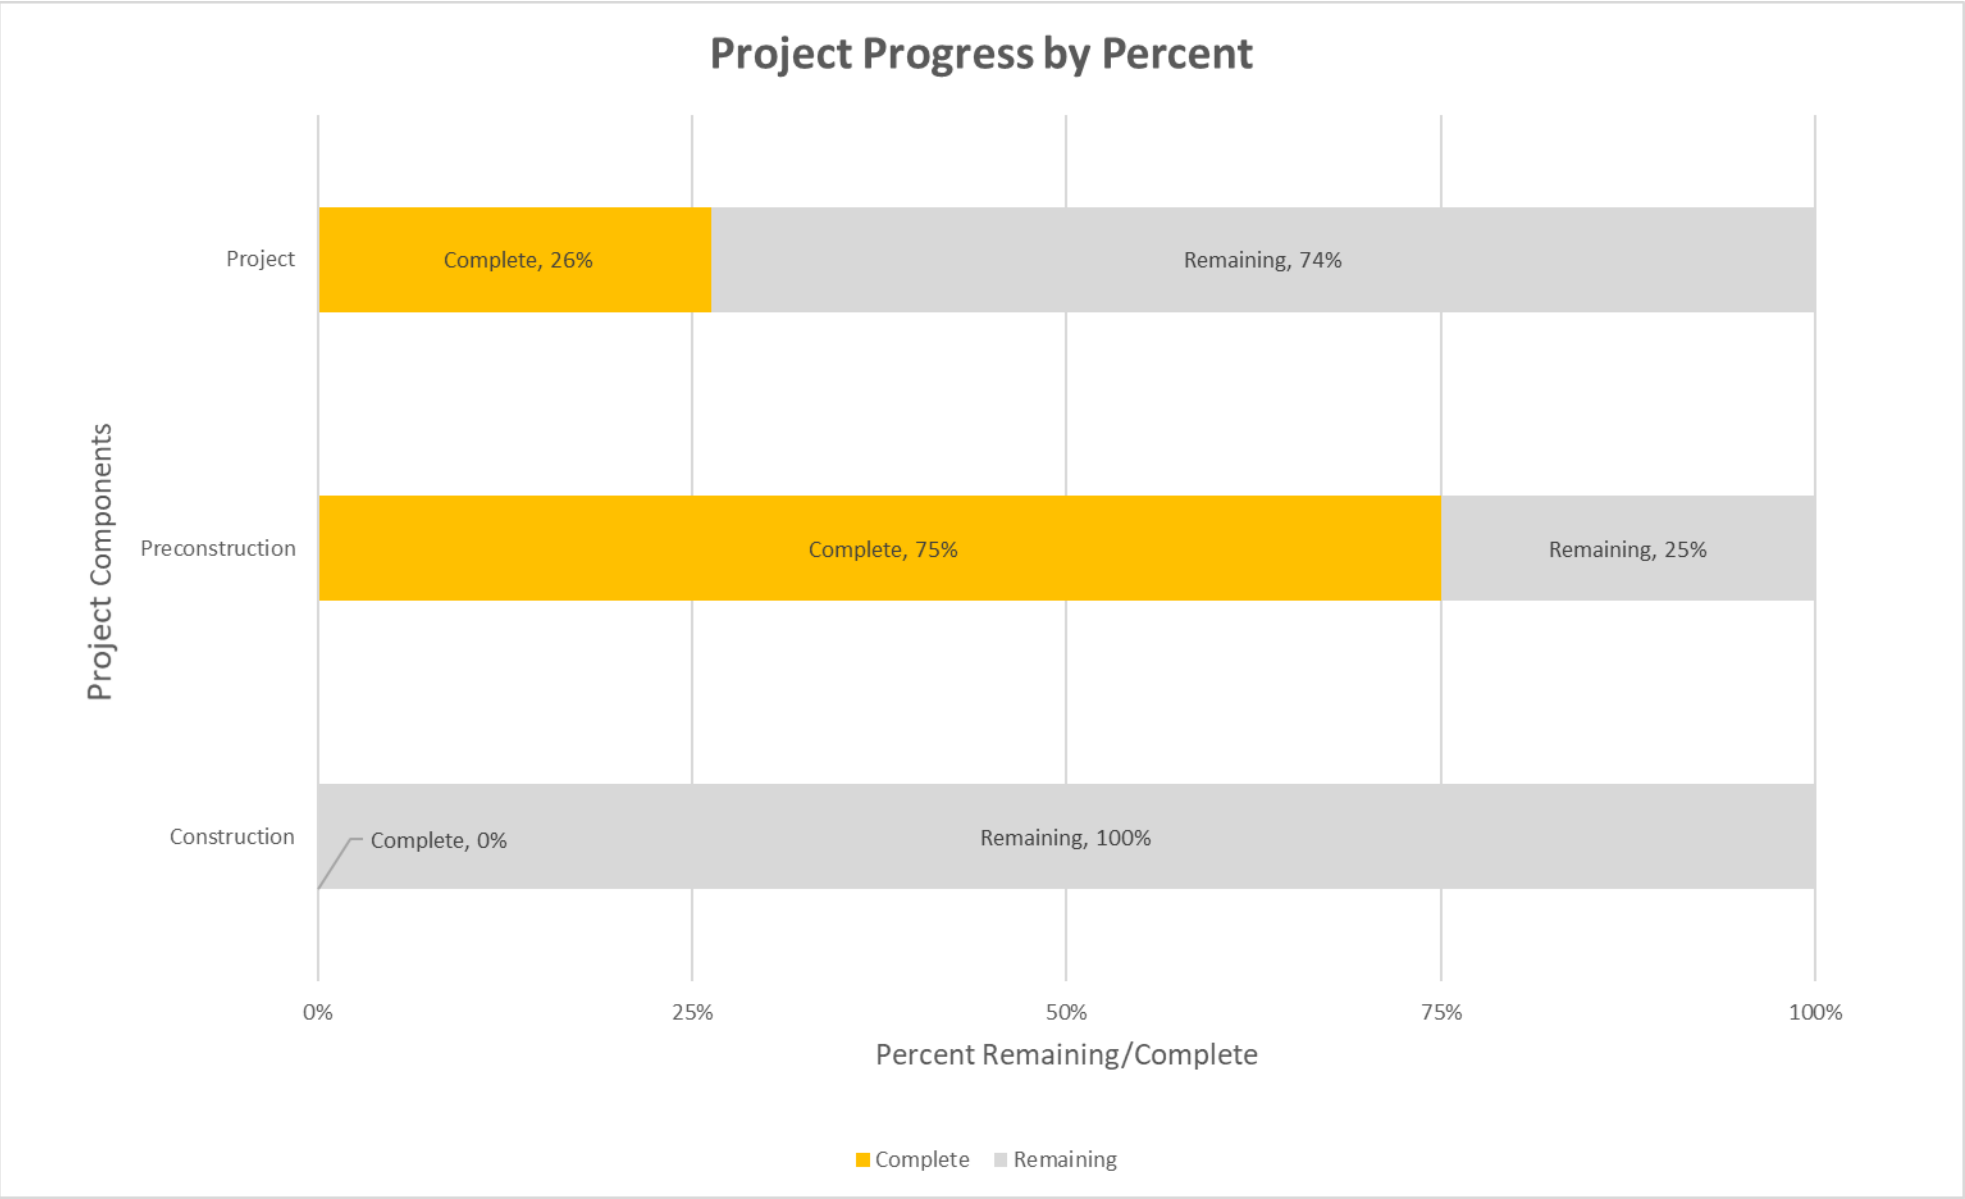

Overall Project: 26% Complete, 74% Remaining

Design: 75% Complete, 25% Remaining

Construction: 0% Complete, 100% Remaining


Project Name: Vasquez Blvd – I-270 to 64th Avenue

Project Number: 22922

Date: 7/17/2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract vale and change orders to date, and contract’s bid amount.

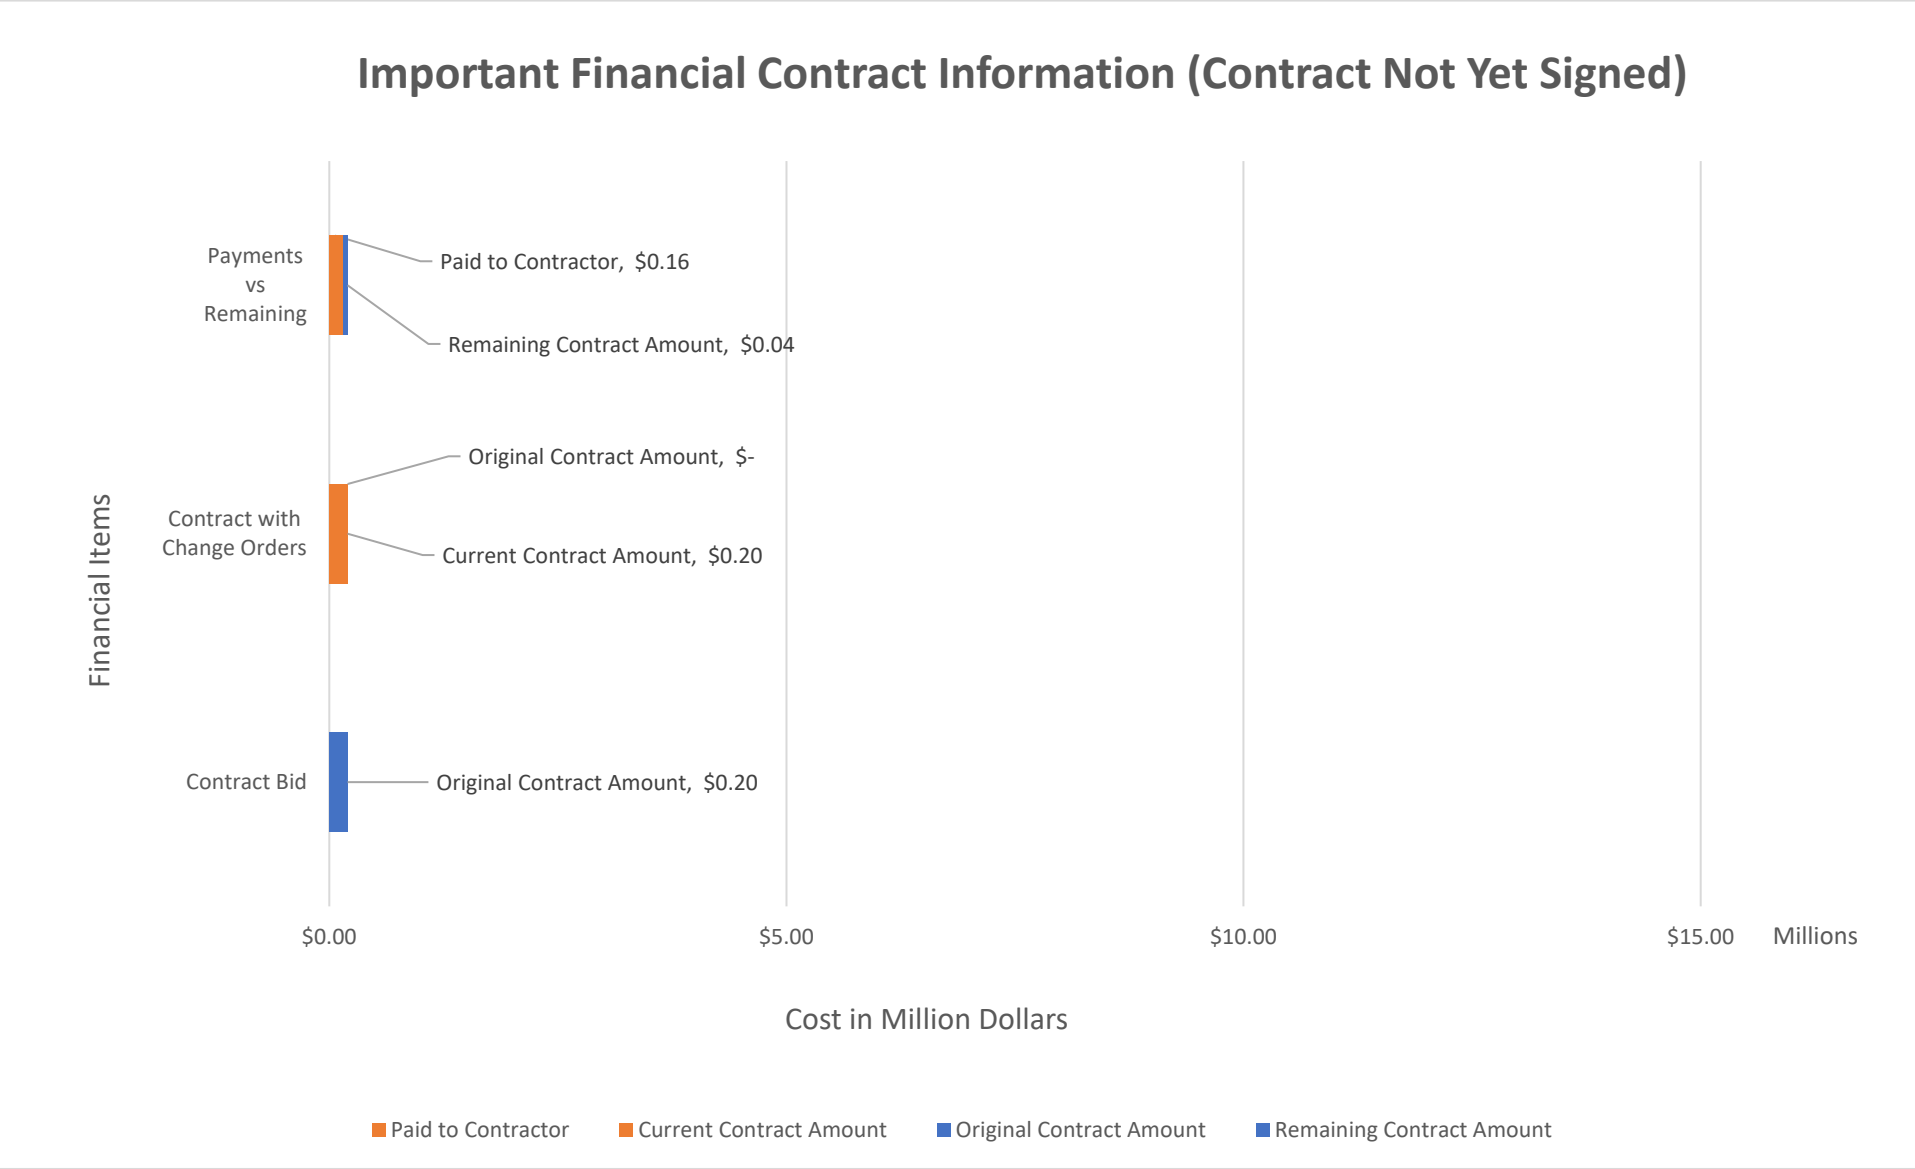

Initial Contract Value: \$200,000

Payments to date: \$162,440 Payments remaining – \$37,560


Current Contract Value: TBD, Total Change Orders to Date: N/A

Initial Contract Value: TBD

Project Name: Vasquez Blvd – I-270 to 64th Avenue
Project Number: 22922
Date: 7/17/2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

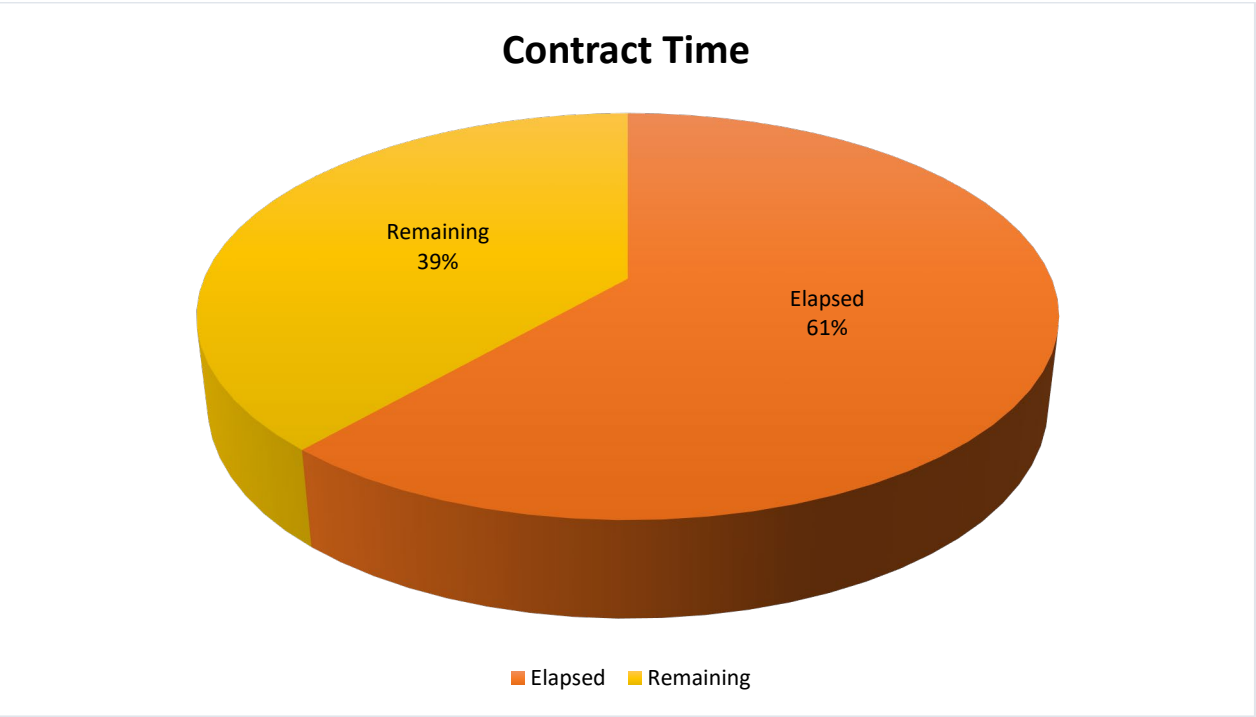

Total Contract time: 200 days
Elapsed Contact time: 123 days, 61%
Contract Time Remaining: 77, 39%
