


Project Name: Vasquez Boulevard – I-270 to 64th
 Avenue Project Number: 22922
 Date: 7/15/2024 Update

Vasquez Boulevard – I-270 to 64th Avenue Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

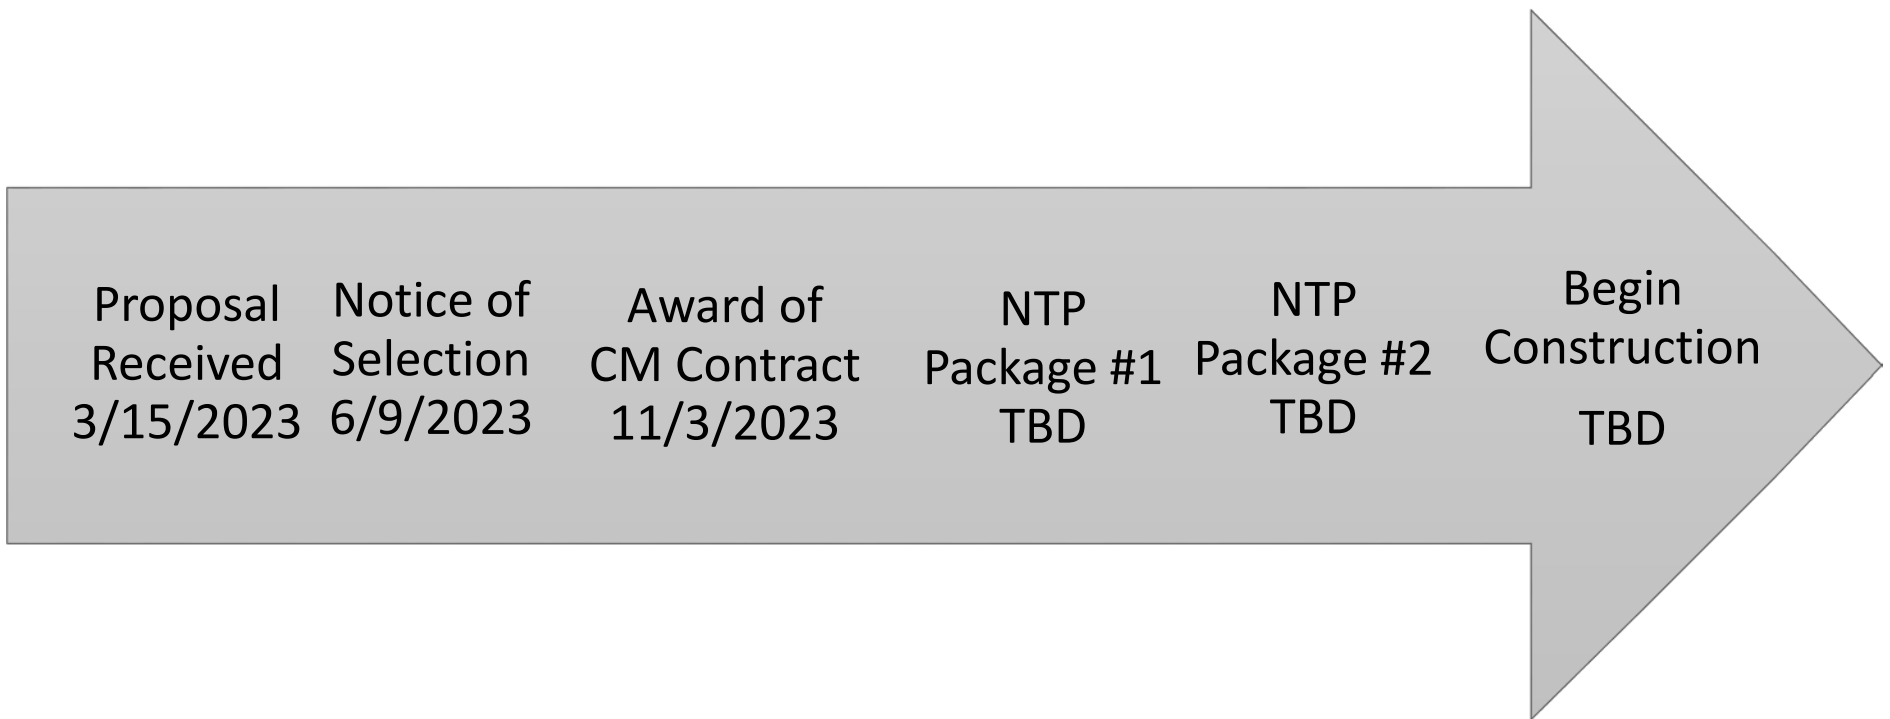

Proposal Received: 3/15/2023

Notice of Selection: 6/9/2023

Award of CM Contract: 11/3/2023

Notice to Proceed Package #1: To be determined

Notice to Proceed Package #2: To be determined

Begin Construction: To be determined




Project Name: Vasquez Boulevard – I-270 to 64th Avenue

Project Number: 22922

Date: 7/15/2024 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

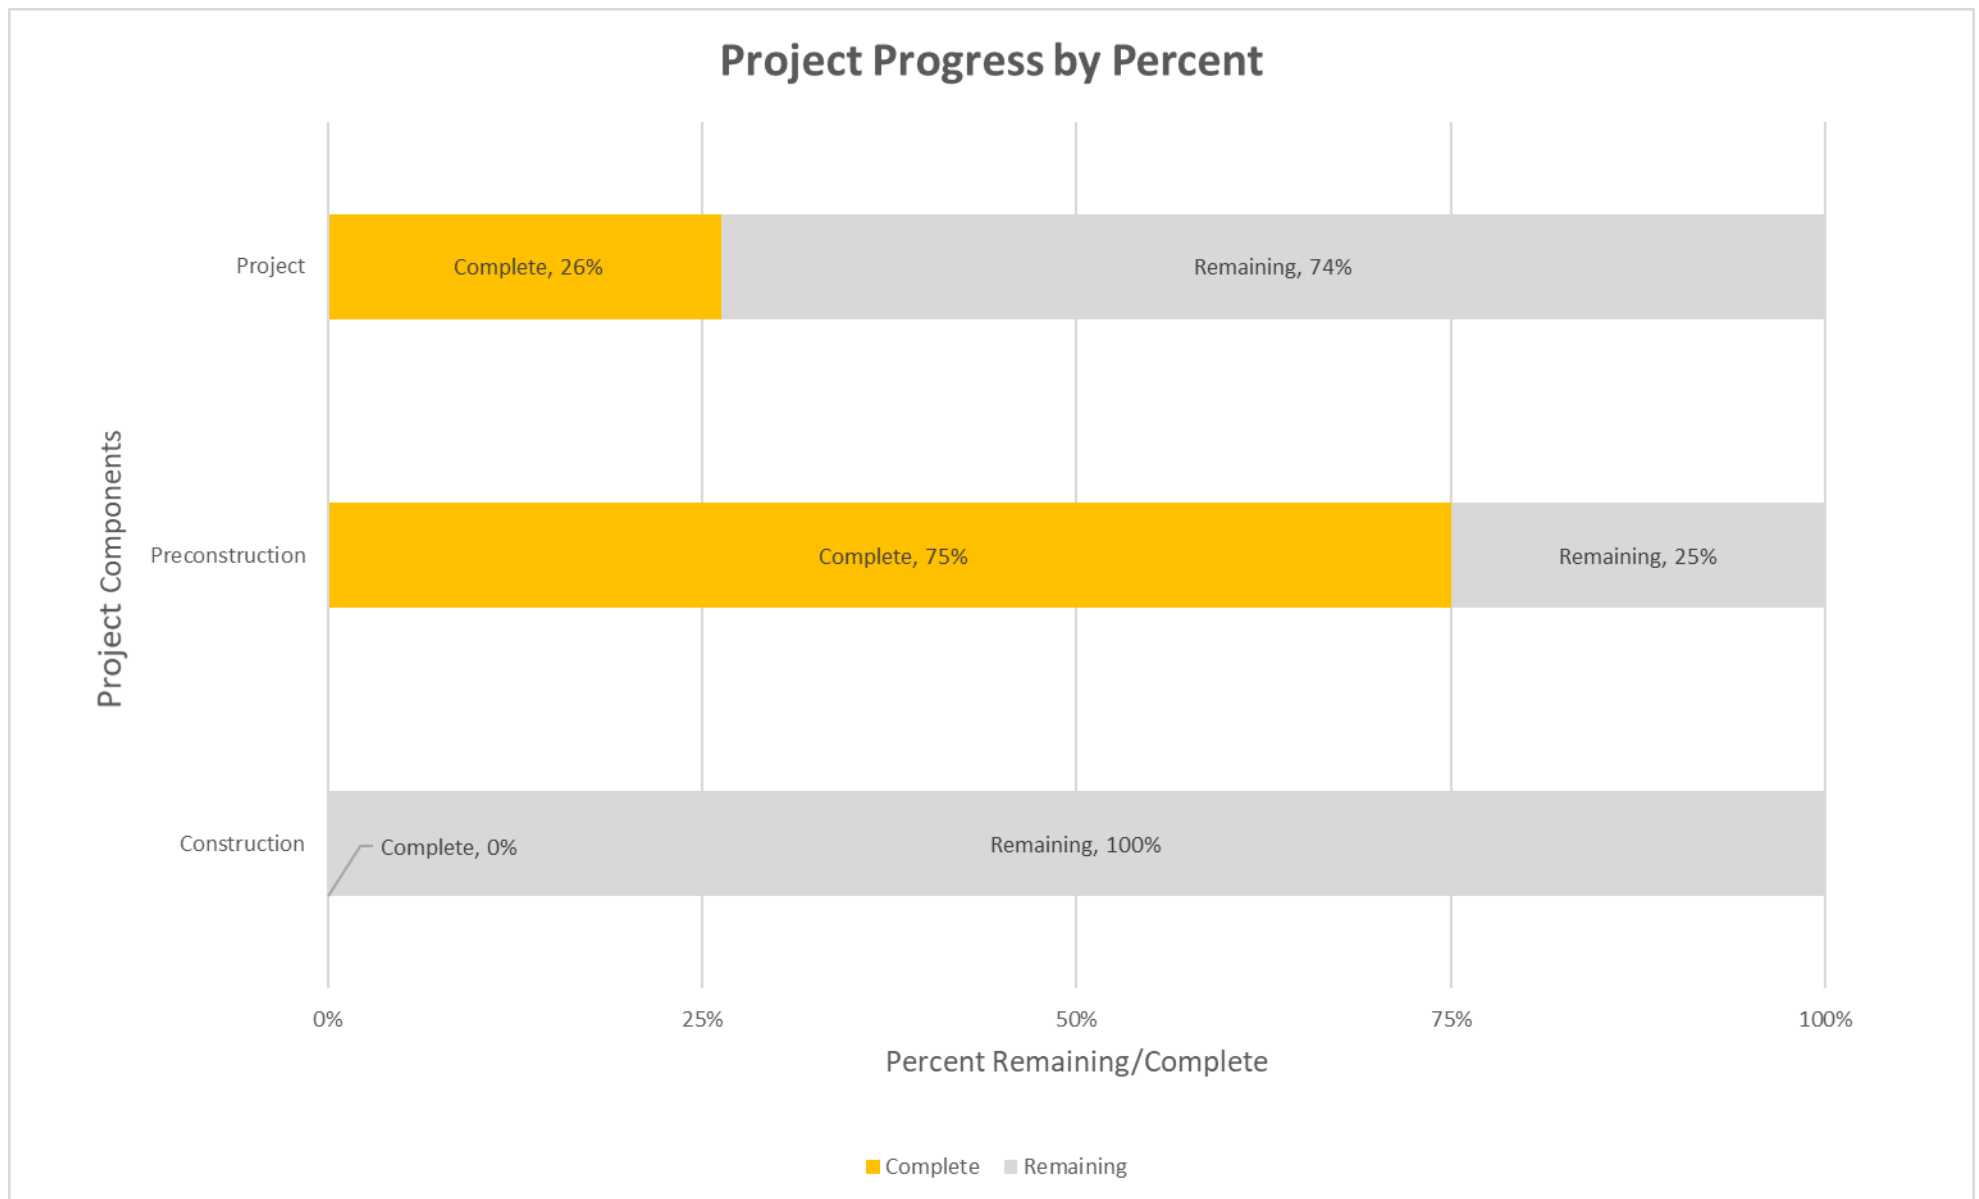

Overall Project: 26% Complete, 74% Remaining

Design: 75% Complete, 25% Remaining

Construction: 0% Complete, 100% Remaining


Project Name: Vasquez Boulevard – I-270 to 64th Avenue

Project Number: 22922

Date: 7/15/2024 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

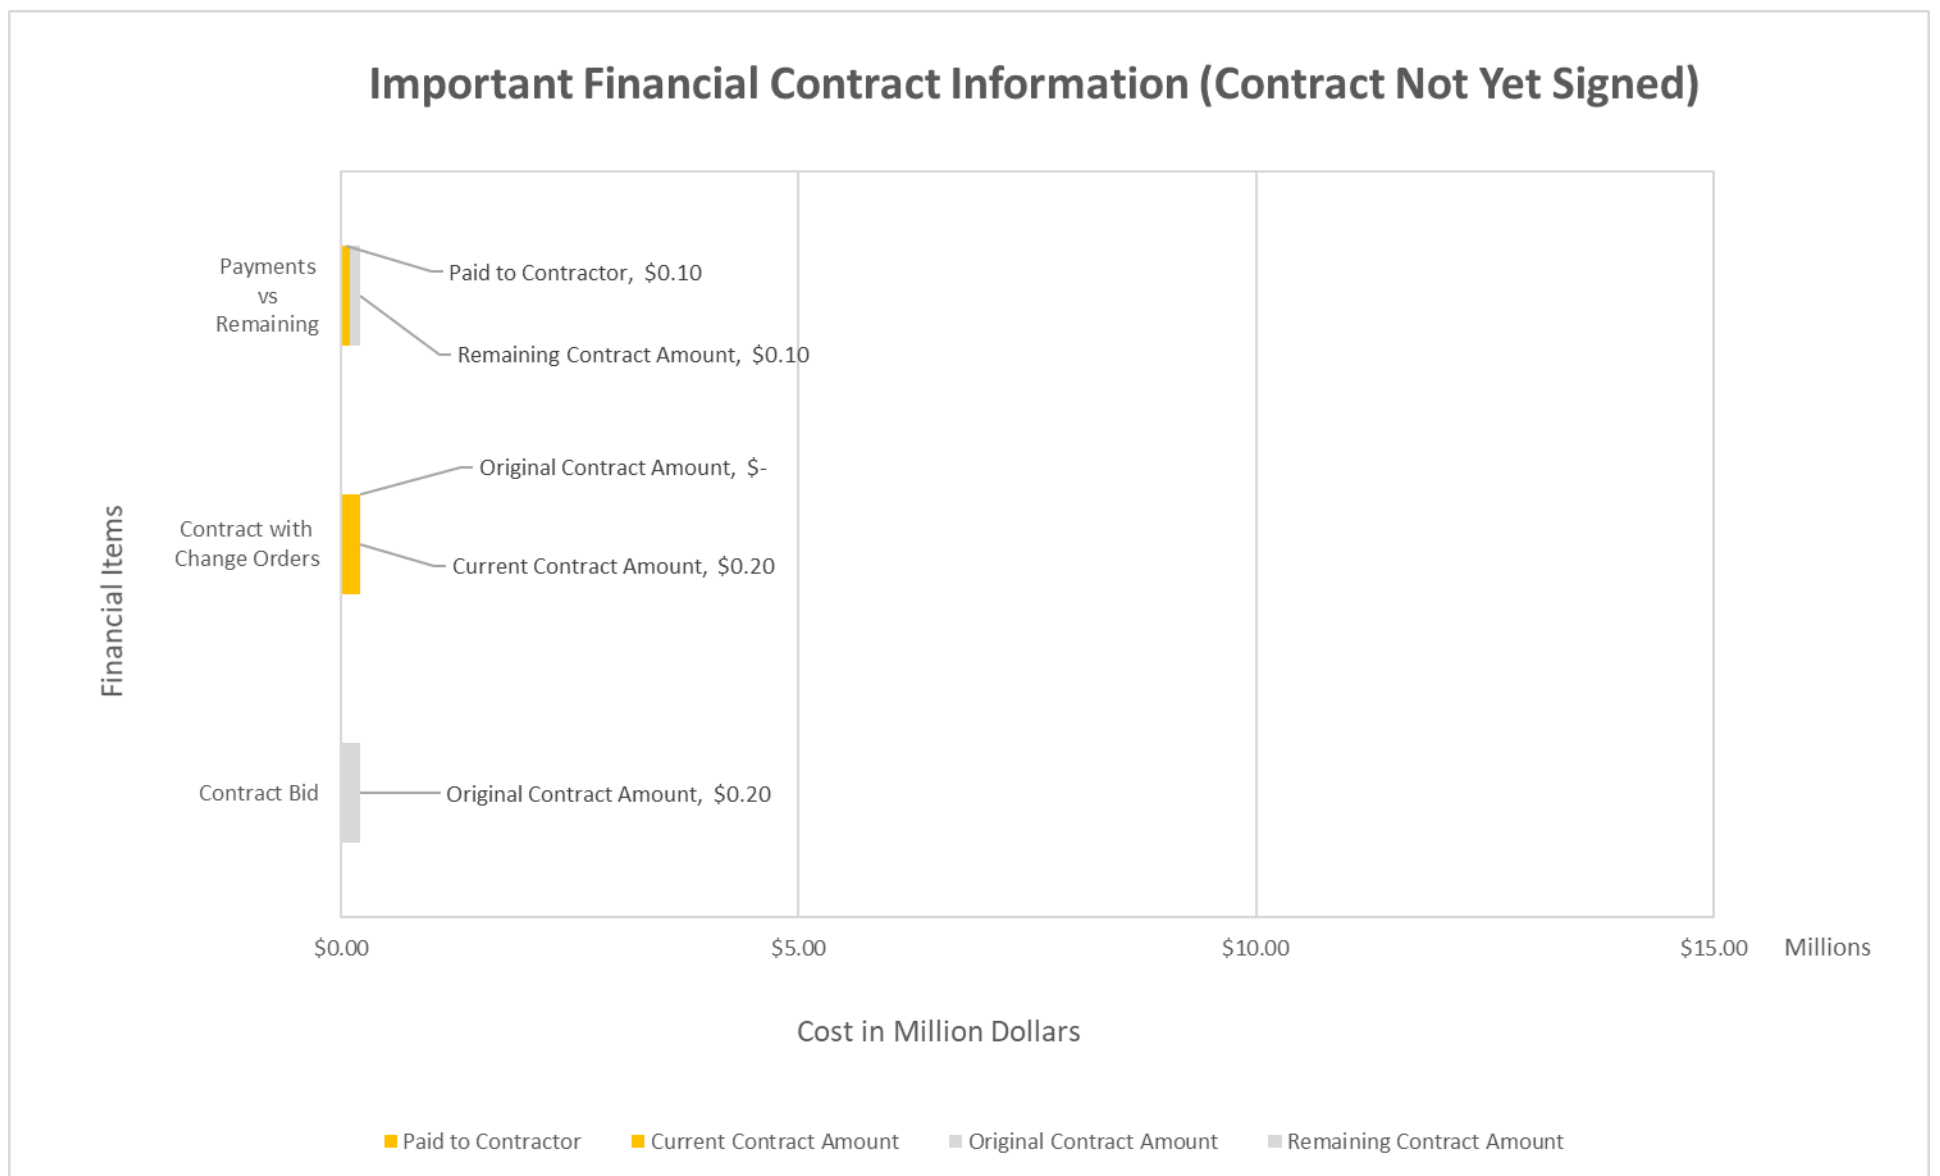

Initial Contract Value: \$200,000

Payments to date: \$99,480

Payments remaining – \$100,520

Current Contract Value: To be determined, Total Change Orders to Date: Not applicable


Initial Contract Value: To be determined



Project Name: Vasquez Boulevard – I-270 to 64th
Avenue Project Number: 22922
Date: 7/15/2024 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

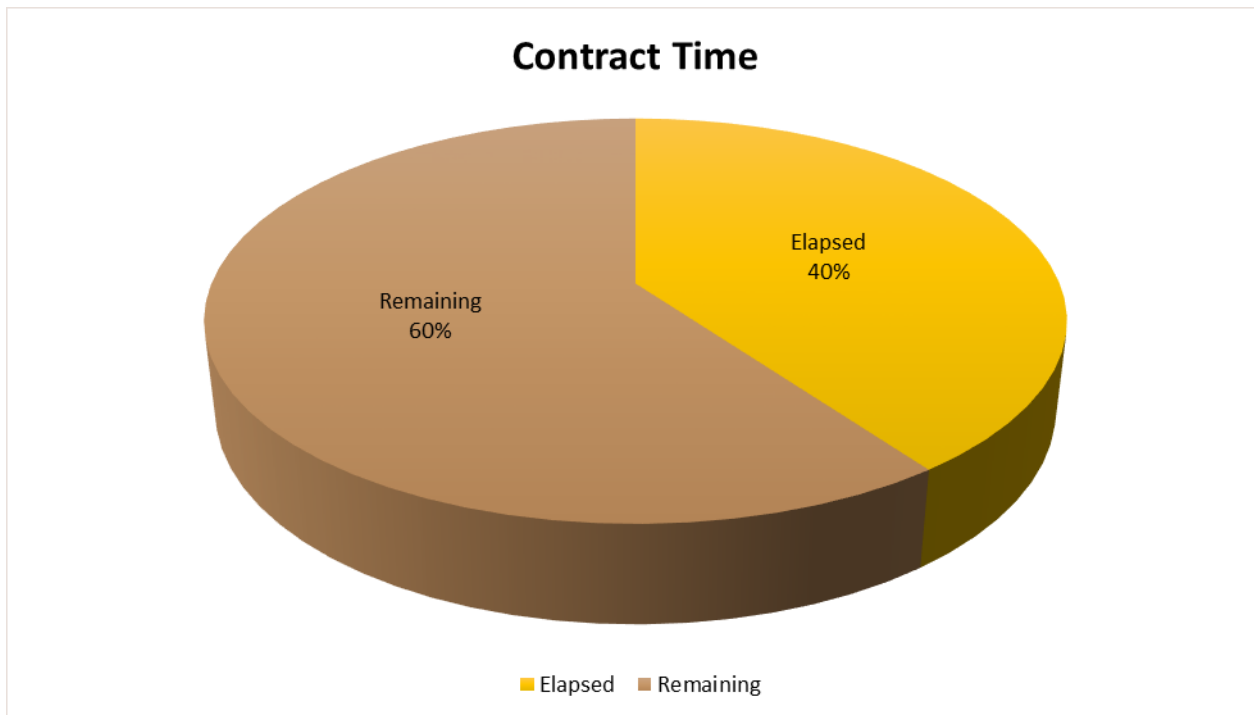

Total Contract time: 200 days

Elapsed Contact time: 80 days, 40%

Contract Time Remaining: 120, 60%
