



Project Name: Vasquez Blvd – I-270 to 64<sup>th</sup> Avenue

Project Number: 22922


Date: 03/13/2026 Update

## Vasquez Blvd – I-270 to 64<sup>th</sup> Avenue Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

### Key Dates

The following image shows the progression of the key project dates.

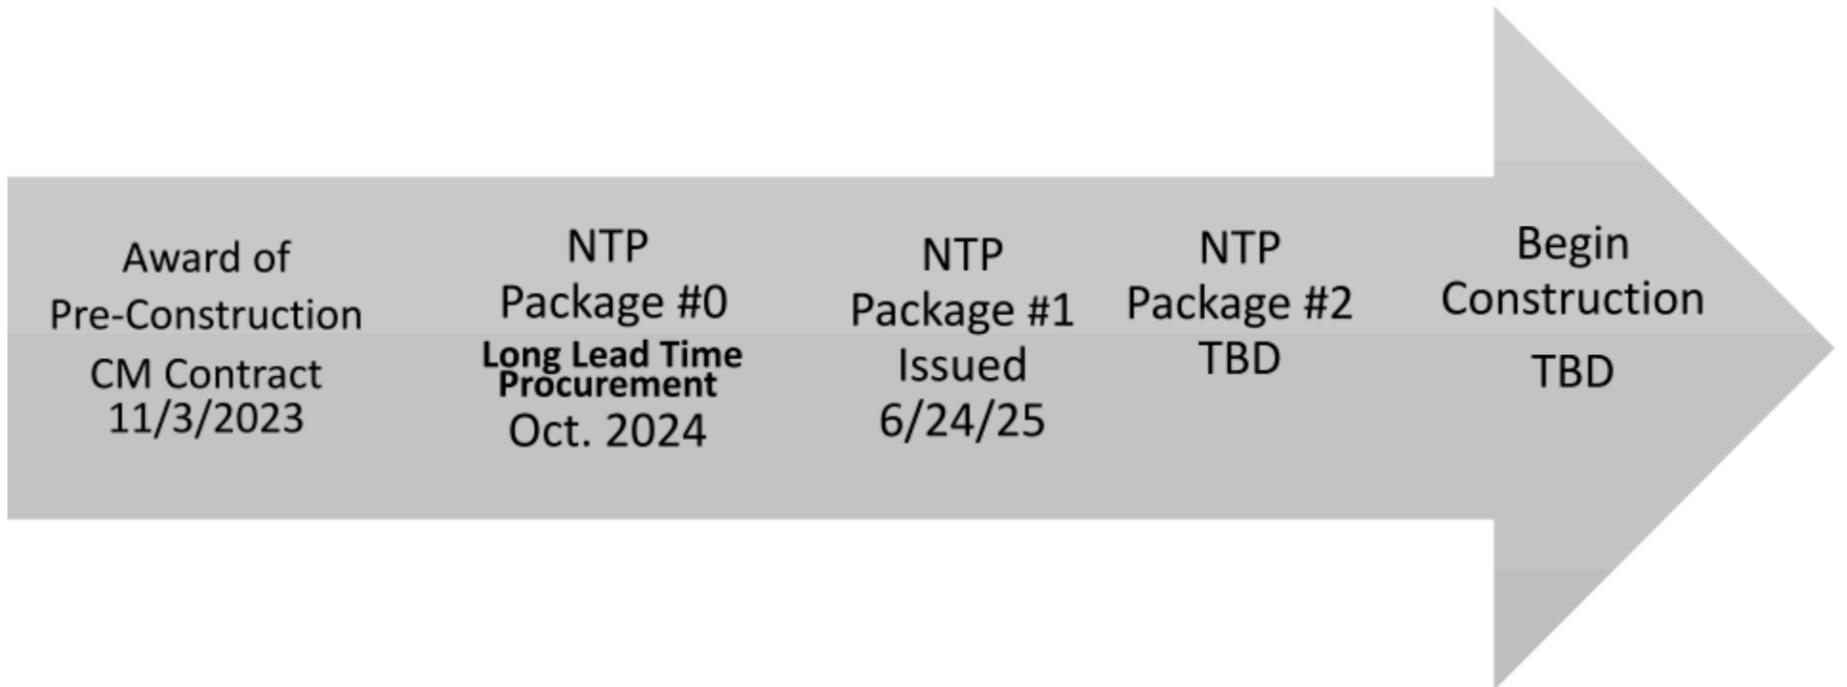

Award of Pre-Construction CM Contract: 11/3/2023

Notice to Proceed Package #0: October 2024

Notice to Proceed Package #1: Issued 6/24/25

Notice to Proceed Package #2: TBD

Begin Construction: Package 1 - 7/21/25




Project Name: Vasquez Blvd – I-270 to 64<sup>th</sup> Avenue

Project Number: 22922

Date: 03/13/2026 Update

### Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

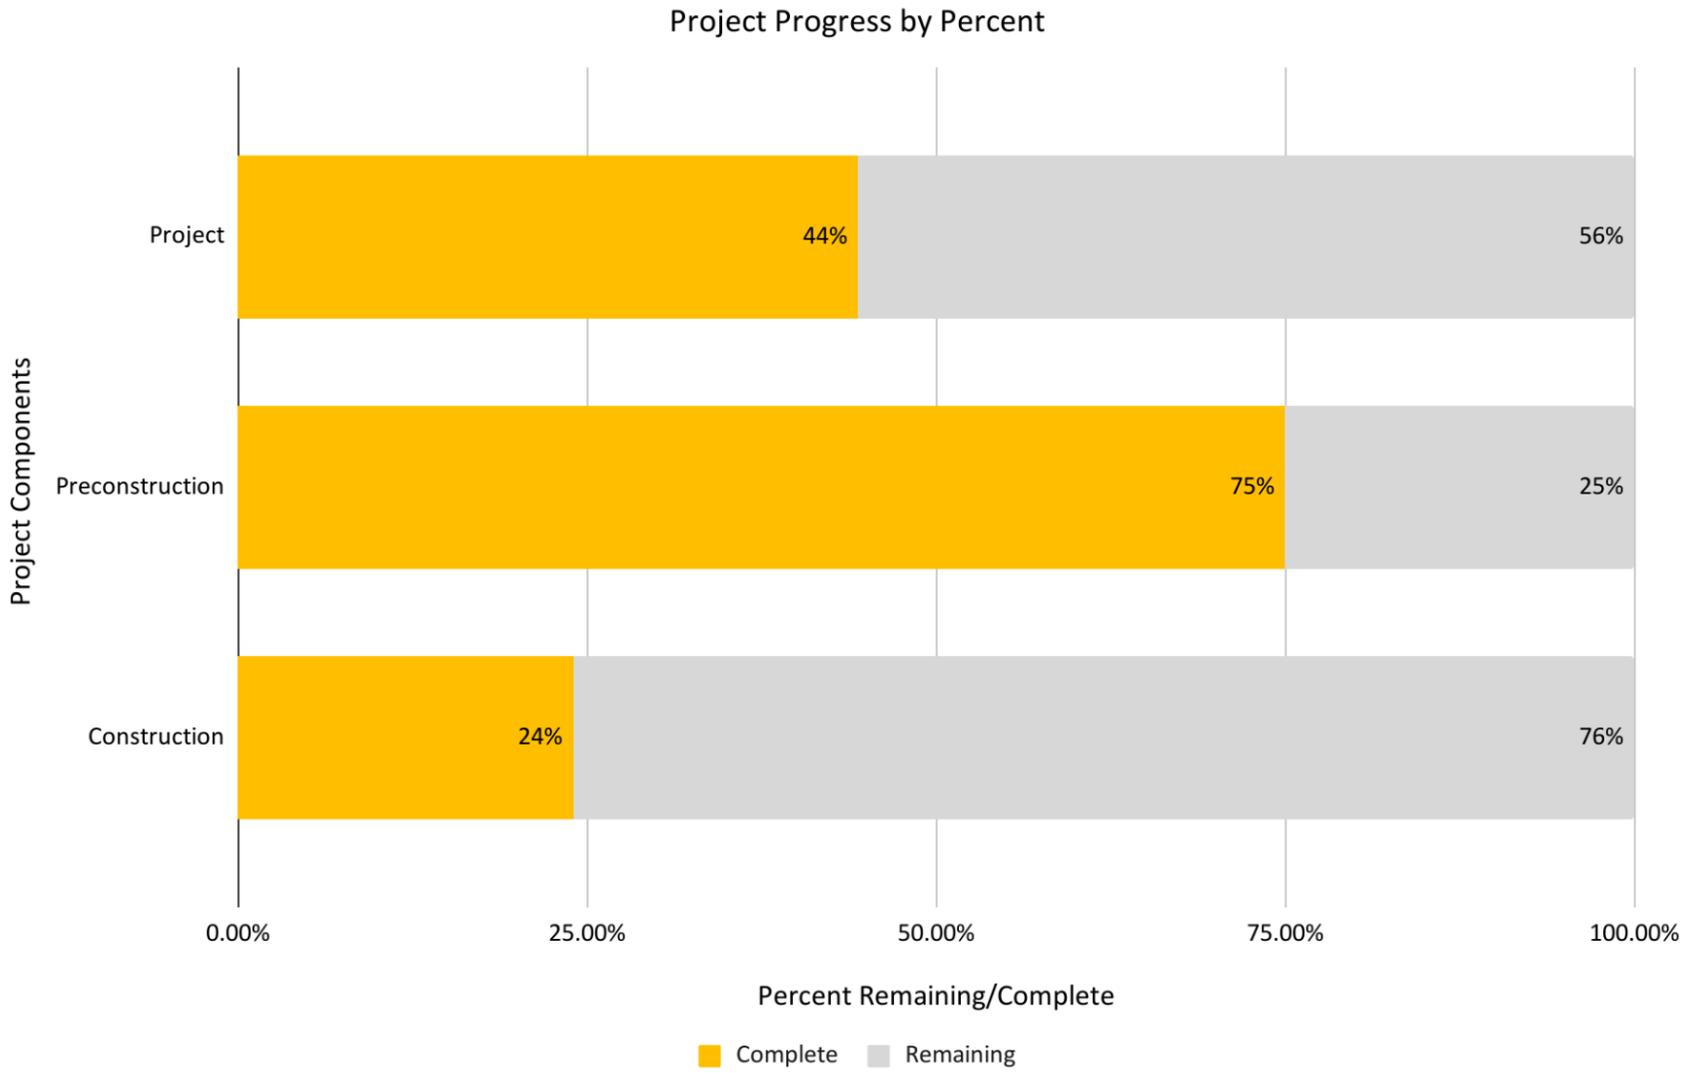

Overall Project: 44% Complete, 56% Remaining

Design: 75% Complete, 25% Remaining

Construction: 24% Complete, 76% Remaining




Project Name: Vasquez Blvd – I-270 to 64<sup>th</sup> Avenue

Project Number: 22922

Date: 03/13/2026 Update

**Important Financial Contract Information**

The following Bar chart shows the projects payments vs remaining amount, total current contract value, change orders to date, and contract’s bid amount.

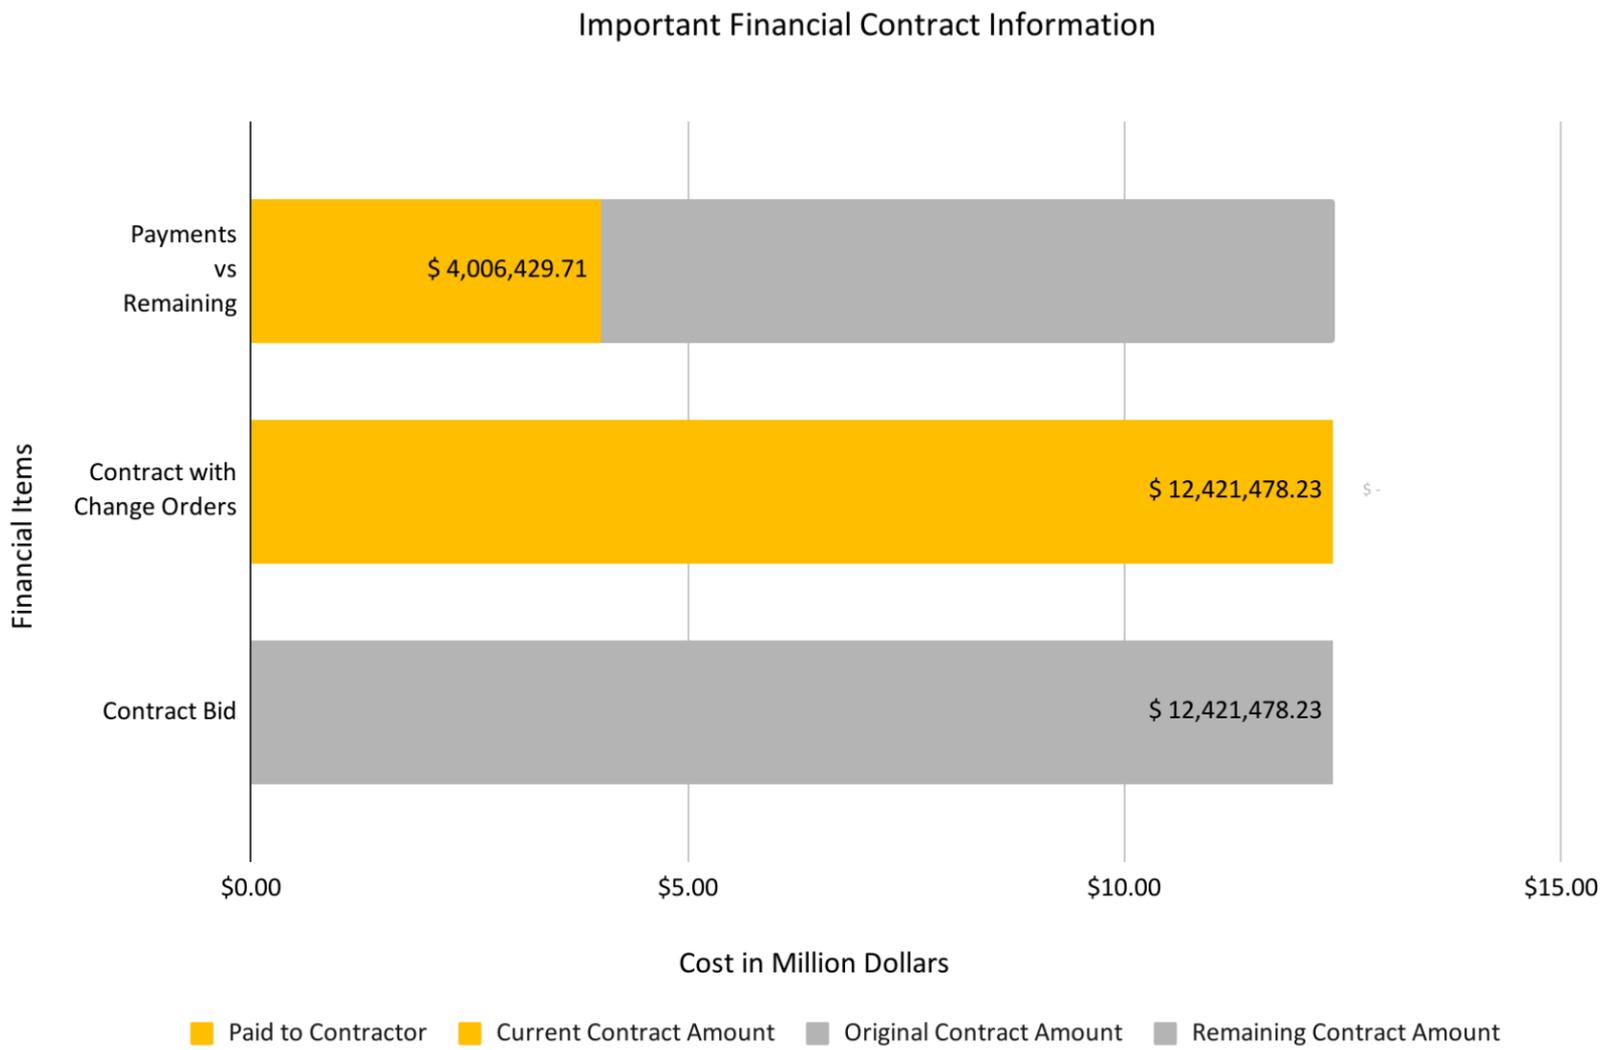

Initial Contract Value: \$12,421,478.23

Payments to date: \$4,006,429.71

Payments remaining – \$,451,378.92

Current Contract Value: \$12,421,478.23

Total Change Orders to Date: N/A



Project Name: Vasquez Blvd – I-270 to 64<sup>th</sup> Avenue


Project Number: 22922

Date: 03/13/2026 Update

### Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

**Contract Time**

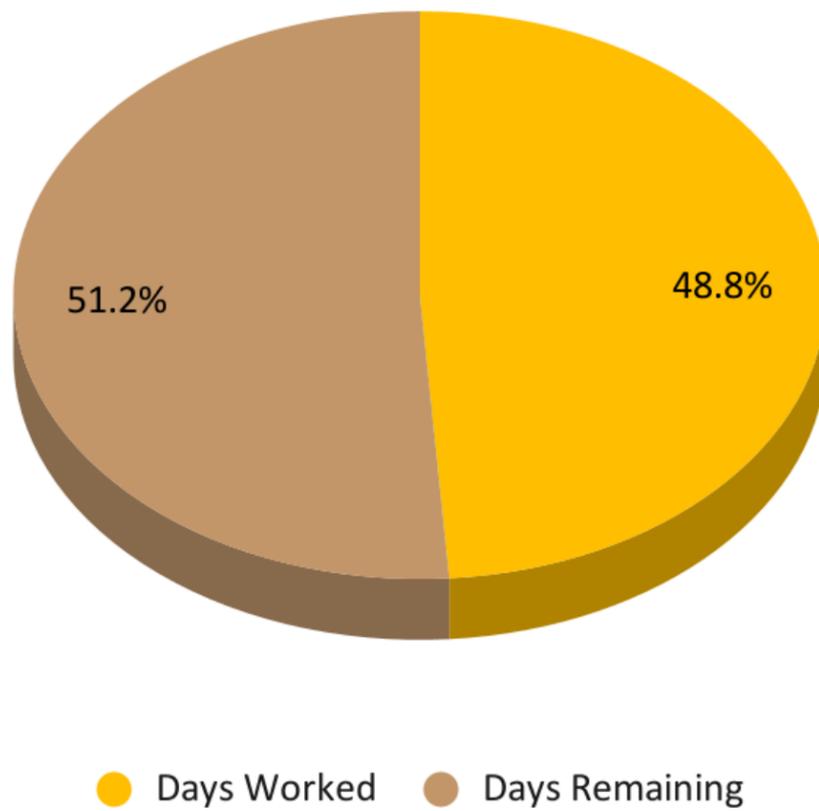

Total Contract time: 303 days

Elapsed Contract time: 148 days, 48.8%

Contract Time Remaining: 155 days, 51.2%
