


Project Name: Cumulative ADP Projects
Date: August, 2025 Update

Cumulative ADP Projects Project Dashboard

This document provides monthly cumulative progress and financial updates on current CDOT ADP projects.

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

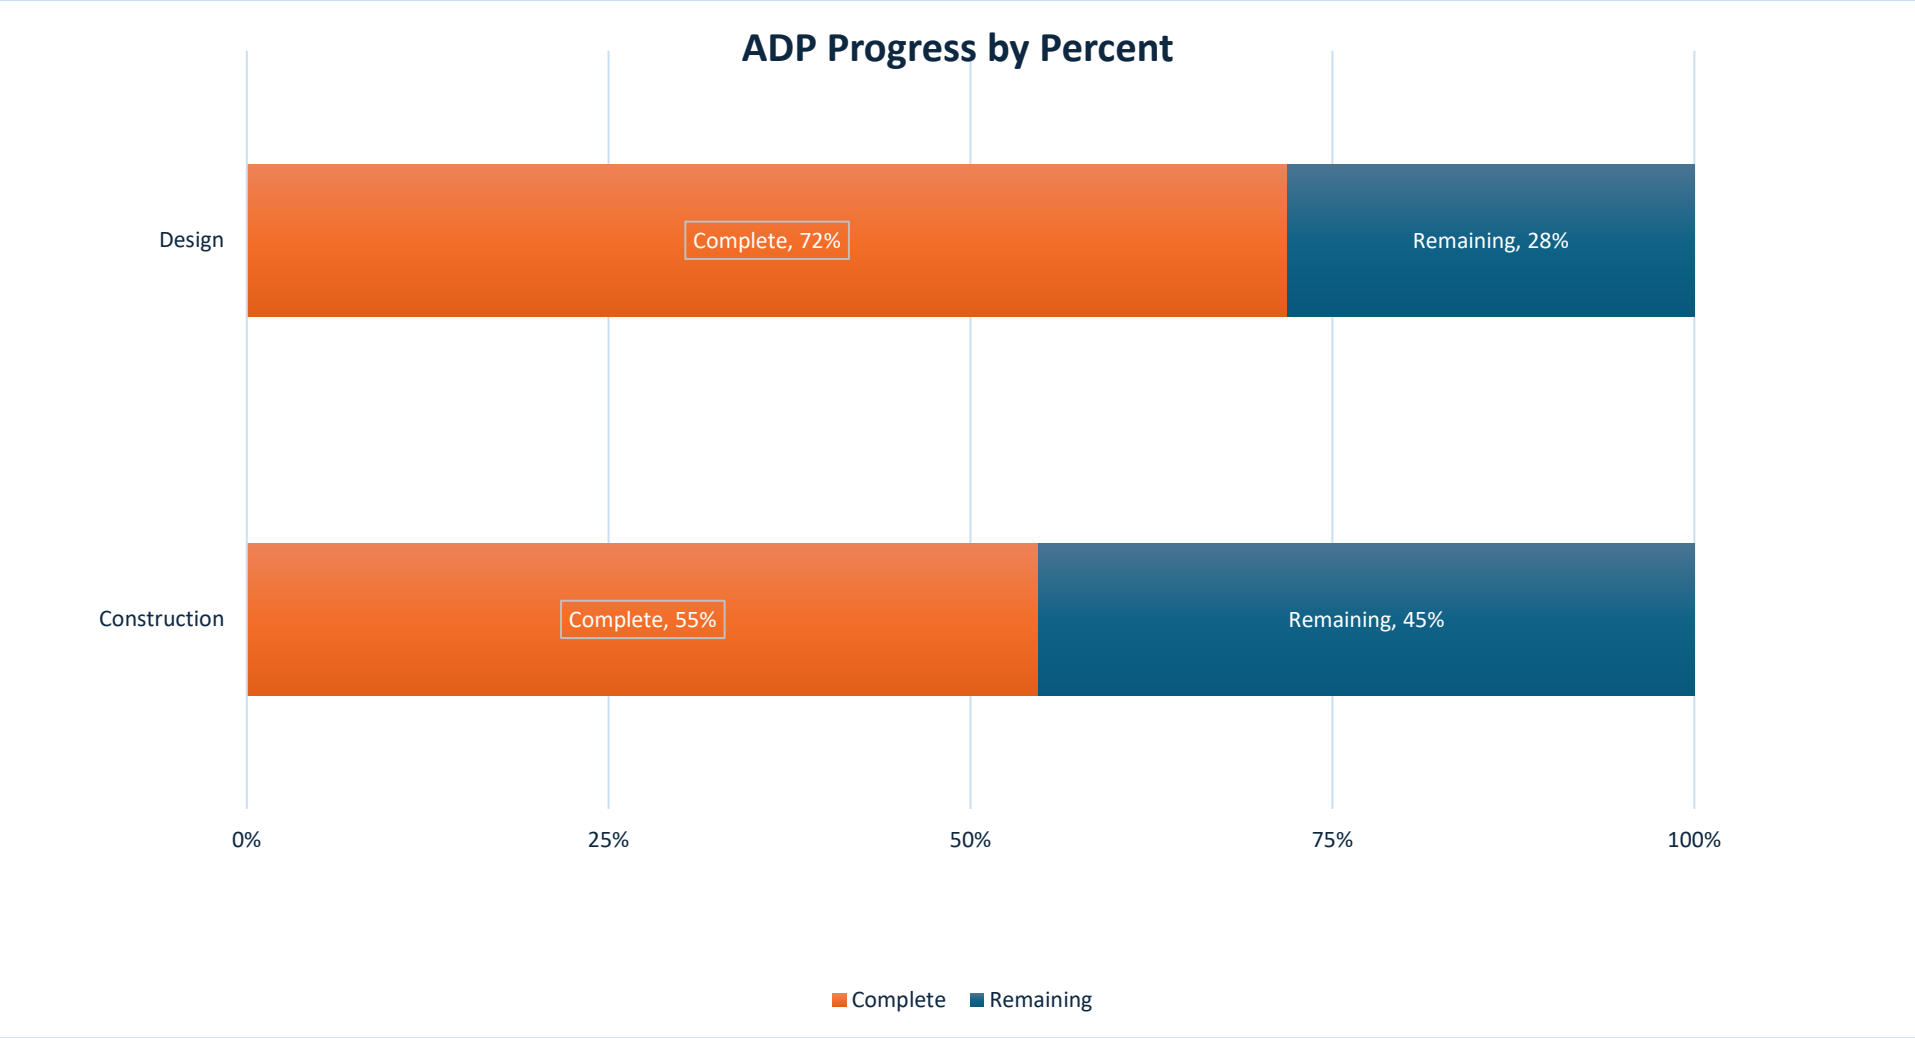


Design: 72% Complete, 28% Remaining
Construction: 55% Complete, 45% Remaining

Project Name: Cumulative ADP Projects
Date: August, 2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract vale and change orders to date, and contract’s bid amount.

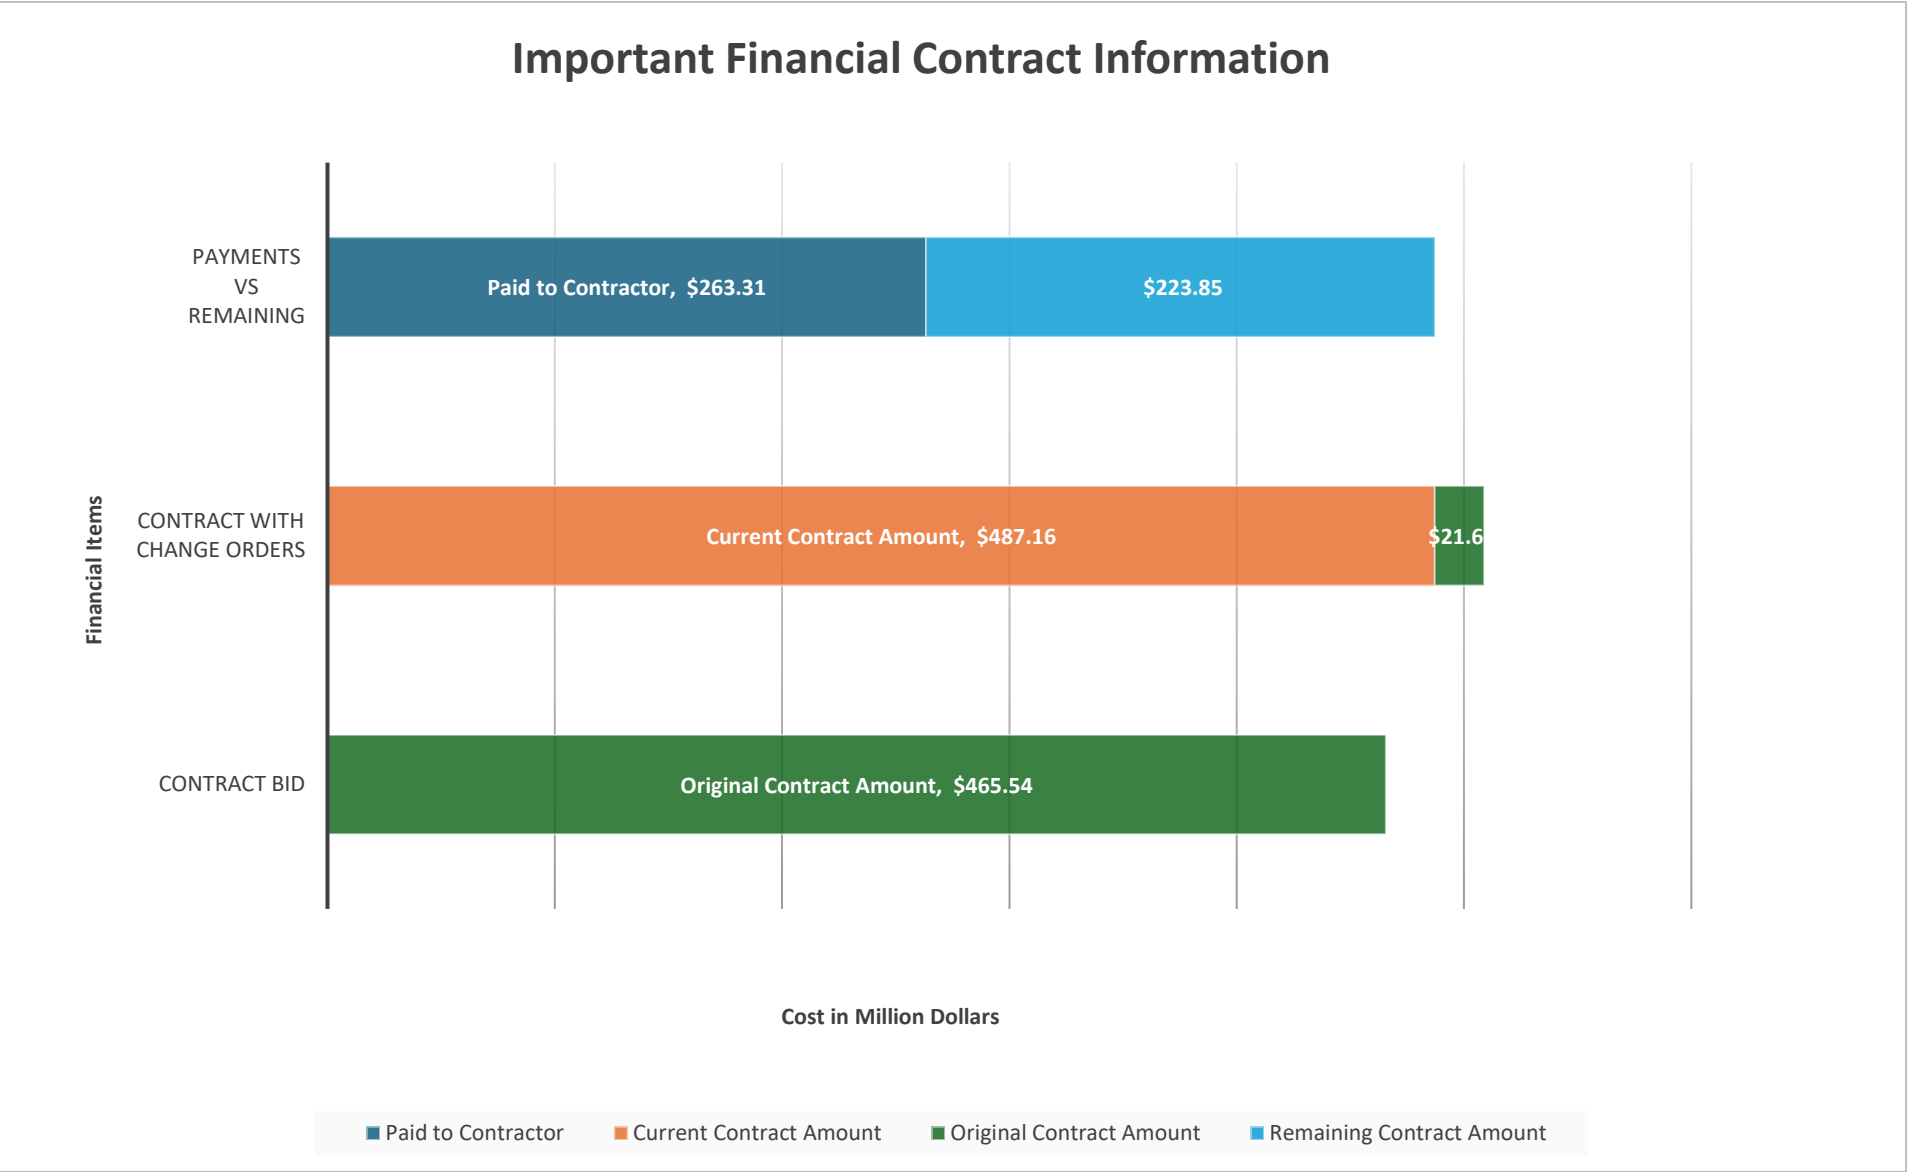


Initial Contract Value: \$465.54 Million
Payments to date: \$263.31 Million, Payments remaining \$223.85 Million
Current Contract Value: \$487.16 Million, Total Change Orders to Date: \$21.60 Million

Project Name: Cumulative ADP Projects
Date: August, 2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

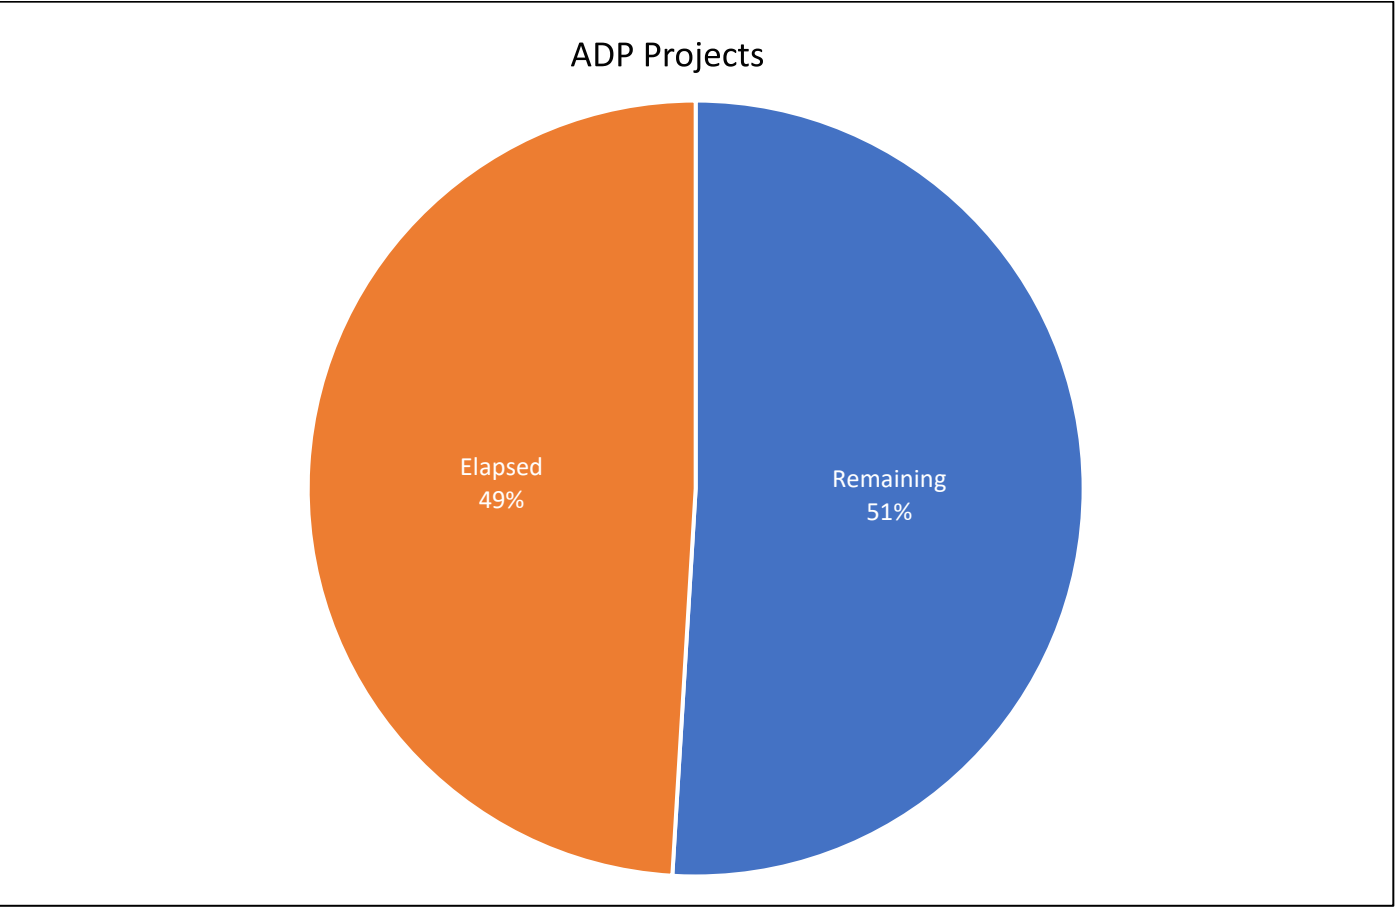

Total Contract time: 11,446 Calendar Days
Elapsed Contact time: 5,267 days, 49%
Contract Time Remaining: 571days ,51%
