

COLORADO

Department of Transportation

Statewide Bridge Enterprise

Colorado Bridge Enterprise

Quarterly Report No. 12 (Q3 FY2014)

August 28, 2014

Introduction

This report is the twelfth Quarterly Report (or Report) published in support of the Colorado Bridge Enterprise (CBE or "Program"). This Report outlines progress and accomplishments associated with the Program for work completed during January, February and March of 2014; which coincides with the third quarter of CDOT's 2014 fiscal year (or Q3 FY2014). Detailed information regarding the FASTER (Funding Advancement for Surface Transportation and Economic Recovery) legislation, program development activities, bond program, previous significant milestones and achievements can be found in the Program Annual Reports and previous Quarterly Reports viewable on CDOT website at www.coloradodot.info/programs/BridgeEnterprise.

During Q3 FY2014, the Program primarily focused on the delivery of bridge projects partially or fully funded by the \$300M bond program. The following is an itemization of significant achievements which are discussed in further detail later in the report:

- Drafted the eleventh Bridge Enterprise Quarterly Report for Q2 FY2014 (October, November and December of 2013).
- Completed monthly updates to the overall program schedule for work complete in January, February and March of 2014.
- Completed the CBE 2013 Annual Report as required by FASTER legislation.
- Presented the CBE/FASTER 2013 Year in Review at the January Board meeting.
- Bond Allocation Plan update through Q2 FY2014 drafted; schedule to be presented at the May Board meeting.
- Drafted a map for DRCOG illustrating BE bridges located within DRCOG.
- Drafted a revision of CBE Guidance Document #8(Quarterly Bridge Assessments).

Program Highlights

There are currently 93 bridges that are partially or fully funded to be completed as part of the \$300M bond program. Over two-thirds of the bond funded bridge projects can be classified as complete, in construction or are waiting to go to construction (67 in total or two-thirds of the population); as compared to the number of bridges in the pre-construction or design phase (26 in total or one-third of the population).

Projects in the preconstruction phase are primarily focused on the completion of the PS&E's (Plans, Specifications and Estimates). In conjunction with this, CDOT specialty groups are diligently working on completing the requisite approvals and permits associated with environmental, railroad, and utility clearances or relocations; securing the necessary Right-of-Way (ROW); and finalizing intergovernmental agreements (as required), etc. Per the current program schedule, construction work is projected to stay at a high level through calendar year 2014, and the work will taper-off during calendar year 2015 into calendar year 2016.

As of the end of March 2014, there were a total of one-hundred and seventy-nine (179) bridges considered eligible to receive FASTER funding. The progress status associated with these 179 structures is itemized in Table 1 below.

Table 1. Project Status as of Q3 FY2014

Project Phase	Bridge Number
Future Projects	21
In Design Phase	28
In Construction Phase	14
Projects Complete ⁽¹⁾	99
No Action Proposed	17
Total ^{(2) (3)}	179

(1) Reference Appendix A for List of Completed Bridges

(2) Reference Appendix B for complete List of FASTER eligible bridges

(3) Reference Appendix C for Colorado State map of FASTER eligible bridges

Other relevant bridge and financial statistics are as follows:

- Approximately 63% of FASTER eligible bridges (14+99) are now in construction or completed.
- Approximately 16% of FASTER eligible bridges (28) are currently in design.
- Only 12% of FASTER eligible bridges remain to be programmed (defined as Future Projects at 21); does not include bridges classified as "No Action Proposed".
- Additionally, \$260.2M and \$40.8M of bond program funds have been expended or encumbered to date, respectively (reference Table 8).

The program schedule progress and performance information presented in Table 2 shows the value of the work complete through Q3 FY2014 as compared to what had been planned to be completed per the baseline schedule. The earned value of work complete to date was \$380.6M as compared to the planned value of the work scheduled to be completed at \$419.5M; which indicates that the program was approximately 9% behind the plan.

Note - Earned Value at the lowest level is attained by multiplying the percent complete of a project activity by its respective budget. Earned value is rolled-up from the project level to the region level, and then again rolled-up from the region level to the program level.

CDOT Region	Planned Value of Work through Mar. 31 st	Earned Value of Work through Mar. 31 st	Schedule Variance
1	256,444	235,698	(20,746)
2	72,949	60,732	(12,217)
3	37,834	37,950	116
4	40,195	34,211	(5,984)
5	12,053	12,053	0
Total	419,475	380,644	(38,831)

Table 2. Q3 FY2014 Earned Value b	v CDOT Region and Program (SK)

The Program utilizes cost and schedule Key Performance Indicators (or KPIs) to track, monitor and report on program performance. As part of the monthly schedule update, a Schedule Performance Index (or SPI) is calculated for each project included within the bond program. The SPI is also calculated and reported at the regional and program levels. The SPI is based upon earned value which compares actual progress to planned performance based upon work complete to date. The program SPI for work complete through March 2014 was 0.91; which represents a 0.02 decrease from the previous quarterly report (December 2013 SPI at 0.93). The program has established an SPI goal during execution of greater than or equal to 0.90.

Program Activities and Accomplishments in Q3 FY2014

The Program's main activities and significant accomplishments are briefly described below.

FASTER Eligible Bridges

There were no newly eligible structures added during Q3 FY2014.

Pre-Construction Phase

There was one project which began the pre-construction phase during this period as itemized in Table 3 below.

Table 3. Projects that began the design phase

Region	Original Bridge Number	Facility Carried over Featured Intersection
1	F-14-Y	I 70 Business Route over I 70 ML

Projects that went to AD (Advertisement for Construction)

There were two projects (or 4 bridges) that went to AD during the period as itemized in Table 4 below.

Table 4. Projects / Bridges that went to AD

Region	Original Bridge Number	Facility Carried over Featured Intersection
1	E-17-DC	I 76 ML Eastbound over UP Railroad
1	E-17-DU	I 76 ML Westbound over UP Railroad
1	F-17-GO	US 40 ML Eastbound over Tollgate Creek
1	F-17-GA	US 40 ML Westbound over Tollgate Creek


Completed Projects

There were no projects completed during this period.

Program Schedule Update

The bond program schedule was updated three times during the period for work complete in January, February and March of 2014. This includes publishing the monthly updated program bar-chart schedule, cost and schedule database, and list of projects with an SPI < 0.90. This information was consolidated and distributed to the Regional Transportation Director's (or RTD's) and their respective program engineers. The SPI's reported for each month during the quarter are graphically depicted on Figure 1 below.

Figure 1. Bond Program SPI Reported by Month

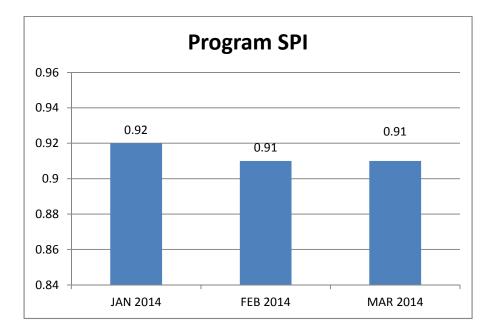

Schedule Change Control Board

The Schedule Change Control Board (SCCB) conducted two meetings during the period on February 13th and March 13th. The SCCB meetings were attended by senior CDOT HQ staff including: Scott McDaniel (Acting Chief Engineer), Scott Richrath (CDOT CFO), Herman Stockinger (government

relations), Regional RTD's and program engineers. The purpose of the SCCB meetings was two-fold: (1) document and review projects with an SPI < 0.90, and (2) allow the RTD's (or their designated delegate) an opportunity to petition the SCCB to make adjustments to a project's baseline schedule when the schedule logic does not reflect current project delivery and is artificially impacting the SPI calculation. Formal meeting minutes were published with a list of attendees and an itemized list of SCCB approved changes; subject changes were incorporated into the program schedule in the subsequent schedule update.

Note - the SCCB policy is not intended to provide relief to poorly performing projects. Any baseline adjustments must properly document project issues, and justifiable rationale on proposed adjustments including recommendations to improved project delivery, issues mitigation, required supplemental staffing, and proposed recovery schedules (as necessary).

Major Project/Program Strategic Planning and Coordination

CBE continues to work intimately with various CDOT project teams on coordination, funding eligibility, and strategic planning issues associated with the following large projects:

- Region 1:
 - I-70 over Havana Street project. Region / project staff issued RFQ for Design / Build contractor. Program staff met to review project cost estimates and railroad coordination and other project challenges. Program staff attended the project Executive Oversight Committee.
 - US 6th Avenue bridge / road improvement project: CBE has three replacement bridges in the project; 6th Ave over BNSF, So. Platte River and Bryant Street. Program staff attended meetings for project team coordination.
 - I-70 viaduct project. Program staff met with region / project team and the CDOT design consultant on the I-70 Viaduct to identify planning issues, railroad risk assessment, forecasted costs and associated drawdowns for future phases until 2017. Discussed project financial decisions, CBE impact and CBE eligibility. Assisted with the February Transportation commission presentation, preparation and attended the future expenses funding meeting.
 - Colfax over Tollgate project. Program staff met with the region/project team to discuss scheduling concerns.
 - US 287 and 69th bridge project. Program staff met with region/project team to discuss budget supplement request.
 - F-14-Y: I-70 business route over I-70 ML: Met with region project team to assist with eligibility evaluation, programming and scheduling questions.
- Region 2:
 - Ilex Design / Build Bridge Replacement/Rehabilitation project. Program staff met with project team to assist with the development of the RFP and FHWA authorization.

- Region 3:
 - SH 82 Grand Ave Bridge in Glenwood Springs. Continued support at Public Open House Hearing(s), City Council meeting, Project Leadership Team (PLT), Project Working Group (PWG), FIR meeting and FHWA overview meeting. Worked diligently with team on estimates for overall project costs, potential cost savings and attended value engineering session. Provided guidance for elevator and ramp options on the pedestrian bridge. Provided NEPA/Environmental and utility coordination and ROW expertise. Coordinated with project management and design team regarding eligibility of design features being considered.

I-70 Viaduct Project

CDOT staff is evaluating the various I-70 funding alternatives. The board was presented alternatives at a workshop in December. The board is requesting more information on the alternatives and impact of them on Bridge Enterprise, the project and CDOT. Program is working with CDOT executive staff on the project financial decisions and the CBE impact. The decision on the I-70 funding alternative will impact the future forecasts, financial forecasts and long term planning for CBE.

Bond Spending

Including net bond proceeds and interest earnings on the bond proceeds, the actual spend down was at 84.4%% on March 31, 2014. The CBE team is continuing its efforts to assure 100% spend down of the bonds by: Transferring Bond budget from substantially complete and slow spending projects to projects that could spend the budget faster; and by the CBE Accountant billing the Trustee weekly rather than monthly to speed up the reimbursement process.

Monthly / Quarterly Program Reports

Q2 FY2014 Quarterly Report. Bridge Enterprise drafted the quarterly report highlighting program progress for work complete in October, November and December of 2013 which coincided with CDOT's second quarter of fiscal year 2014 (or Q2 FY2014).

Q2 FY2014 Quarterly Bond Program Update. The \$300M bond program allocation plan was updated for work complete through December 2013 (or Q2 FY2014).

FASTER Job Creation

FHWA tracks the economic benefits of highway capital investments (which include bridge replacement projects), and from a job creation perspective employment impacts fall into three categories as listed below:

- Direct jobs are occupations that work directly on the project such as project planners, designers, engineers and construction workers.
- Indirect jobs means positions at suppliers of materials for the project, such as steel, concrete, wood, etc.

 Induced jobs are jobs created by the spending of monies provided as project salaries [or employee payroll] for items such as mortgage payments, groceries, gas entertainment, etc.

According to an FHWA report from April 2012, there are approximately 10.3 <u>direct jobs</u> created for every \$1 million of construction spending. This correlates into approximately 155 full-time positions; primarily construction craft labor. In addition, preconstruction program expenditures (i.e., engineering and project designs) created another approximately 74 full-time positions; primarily engineers. Combined, there were approximately 229 <u>direct jobs</u> created by the FASTER program spending during the reporting period. Included within the above number are approximately 49 CDOT FTE's (or full-time equivalents); staff responsible for the day-to-day delivery of the program based upon CDOT payroll records.

Resolutions Approved by the Statewide Bridge Enterprise Board

The following is a brief overview of resolutions passed by the Statewide Bridge Enterprise BOD or significant topics discussed during Q3 FY2014 as itemized in Table 7 below.

Table 7. Board Resolution / Significant Topics

January BOD Meeting (No workshop)
 Adoption of 6th budget supplement for FY2014 FASTER Lawsuit Appeal Update Monthly Progress Report Bridge Enterprise 2013 Year in Review
February BOD Meeting (No workshop)
 Adoption of 7th budget supplement for FY2014 Bridge Enterprise 2013 Annual Financial Statements Program funding Progression Overview Engineering News-Record Mountain States: Pecos Bridge Article Monthly Progress Report
March BOD Meeting (No workshop)
 Adoption of 8th budget supplement for FY2014 Update on US 6 Design/Build Bridge Project Monthly Progress Report

Other Significant Achievements

- Program staff working with CDOT DTD on Transportation Deficit Report.
- Program staff worked with CDOT government relations on the FASTER report.
- Coordinated with DTD regarding updating current progress and performance metrics for FY 2013.
- Working with DYE management to develop a forecasting model for estimating drawdown schedule on individual projects.
- Assisted CBE budget analyst on development of FY 2015 draft annual program budget.

- Program staff in concert with CDOT F&A continues to tracking bond expenditures as compared to forecasted bond spending and identify factors impacting bond spending.
- Program staff continues to work with CDOT HQ railroad liaison to identify and minimize coordination delays with UP and BNSF RR railroads.
- BE staff continues to provide progress reports to the portfolio team as required by CDOT.
- Program staff worked with CBE accountant on Q3 and Q4 FY2014 CBE maintenance invoice.
- Program staff working with CBE budget analyst on de-programming dollars for completed phases and actively re-programming the surplus dollars back into the program via new work scope or used to cover increases to planned budgets.
- Program staff working with CBE budget analyst on reallocating bond budget from projects due to adjusting schedules and bond interest.
- CBE staff met with Region project engineers to discuss project closeout for completed BE projects.
- CBE staff continues to track and report on actual expenditures compared with forecasted spending.
- Developed a worksheet to project BE budget available for reconstruction and rehab through FY2043 for Staff Bridge.
- CBE staff continues to support CDOT's Public Relations and Government Relations with ongoing updates to the CDOT/Bridge Enterprise website and monthly "dash-board" performance metric updates.

Financial Information

The following is a program overview of financial statistics as of March 31, 2014.

- The program has multiple funding sources including: proceeds from the Build America Bond program, FASTER bridge dollars which is commonly referred to as the statewide pay-go program (collected yearly revenues from vehicle registrations), Bank of America Loan, and Other Funds which are primarily Federal-aid BR funding.
- From program inception (or life-to-date), a total of \$655.3M has been budgeted (all funding sources), and Expenditures and Encumbrances are \$369.4M and \$145.0M (all funding sources), respectively. Reference Table 8 below for details by funding source.
- For comparison purposes, the totals from the previous quarterly report (Q2 FY2014) are also reported in the far right column.
- Based upon the \$300M bond program baseline schedule developed in February 2011, approximately \$308.1M of bond dollars were projected to be expended by Q3 FY2014; whereas, actual expenditures were \$260.2M and with \$40.8M in encumbrances.

	Build America Bonds 2010 A Proceeds	FASTER Bridge	Bank of America Loan	Other Funds	Total Q3 FY2014	Total Q2 FY2014
Budget	\$303.2	\$280.6	\$40.3	\$31.2	\$655.3	\$656.4
Expenditures	\$260.2	\$46.9	\$38.3	\$24.0	\$369.4	\$349.9
Encumbrances	\$40.8	\$100.2	\$1.1	\$2.9	\$145.0	\$119.3

Table 8. Program Financial Statistics as of (\$ in Millions).

The \$300M bond program currently consists of ninety-three (93)bridges; fifty-five (55) of these bridges are fully funded, and thirty-eight (38) of these bridges are partially funded with current available sources and will require future funding (future bond issuance or other funding) to complete. The estimated total cost for these ninety- three bridges is approximately \$811.0M. Table 9 below provides an itemization of current funding sources and indicates that \$417.6M of additional future funding will be necessary to complete all bridges that may include a second bond issuance. The timing and projected value of any future bond offering is yet to be determined.

Table 9.	Current Bond	Allocation	Plan (\$ in Millions)
----------	---------------------	------------	--------	-----------------

Build America Bonds	FASTER Bridge	Other Funds	Future Funding	Bond Interest	Total
\$298.1	\$45.7	\$39.4	\$417.6	\$10.2	\$811.0

Economic Outlook

The following are highlights from project bid data results maintained by CDOT's Engineering Estimates and Market Analysis (EEMA) group for transportation related projects advertised during the period.

- There were on average 3.58 bidders per project during the period; a decrease from 4.4 bidders
 per project from the previous quarter.
- On average, the low bid on 31 transportation related projects (bid during the reporting period) was lower than the engineer's estimate by approximately 0.72%.
- There was 1 FASTER project bid during the period, and the low bid was approximately 7.4% lower than the engineer's estimate.

The following economic statistics were reported by the Chief Economist from the Associated General Contractors (AGC) of America as reported by AGC's Data DIGest or Press Releases during the quarter. The data provides insight on economic movement associated with the Producer Price Index, Construction Employment and other economic indicators (both state and national) month-to month or year-over-year (e.g., March 2013 to March 2014).

Producer Price Index

The Producer Price Index (PPI) for inputs to construction – a weighted average of the cost of all materials used in construction plus items consumed by contractors such as diesel fuel – rose 0.5% for the month [March 2014] and 1.1% over twelve months (Vol. 14, No. 15Data DIGest).

Construction Employment

Construction employment increased in 38 states between March 2013 to March 2014; eleven states lost construction jobs for the year. Construction employment remained the same in one state year to year. (Vol. 14, No. 16 Data DIGest).
 Construction employment increased in 197 out of 220 metropolitan areas, declined in 87 and was

Construction employment increased in 197 out of 339 metropolitan areas, declined in 87 and was stagnant in 55 between March 2013 to March 2014; (AGC Data DIGest Vol. 14, No. 18).

Other

- Construction spending in March totaled \$943 billion at a seasonally adjusted annual rate, up 0.2% from February total and up 8.4% from March2013. (Vol. 14, No. 18; Data DIGest).
- Colorado continued to be ranked 8th (tied with California) best in the country in the percent of new construction jobs [7,300] gained at 5.9% year-over-year (March 2013 to March 2014) as reported by the AGC from the Bureau of Labor Statistics and U.S. Department of Labor.
- The Denver-Aurora-Broomfield, CO metropolitan area was ranked 117th out of 339 metropolitan areas in the percent of new construction jobs [3,300] gained at 4% year-over-year (March 2013 to March 2014).

The economic indicators at the national level were generally more positive than negative; 76 percent or 38 states reported increases in construction employment year-to-year, construction employment was up in 52% of the reported metropolitan areas. At the state level, Colorado held steady in employment gains tied for 8th best in the country with California reporting 7,300 new jobs or a 5.9% growth in new jobs year-over-year.

2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection	Work Completed
1	E-16-FP	ADAMS	80TH AVE over US 36 ML	Replaced
1	E-16-GQ	ADAMS	SH 95 ML (SHERIDAN BLVD) over UP RR, RR SPUR	Replaced
1	E-17-AR	ADAMS	SH 7 ML over SOUTH PLATTE RIVER	Replaced
1	E-17-DM	ADAMS	I 76 ML WBND over UP RR	Replaced
1	E-17-DN	ADAMS	I 76 ML EBND over UP RR	Replaced
1	E-17-EX	ADAMS	PEORIA STREET over I 76 ML	Replaced
1	E-17-EZ	ADAMS	84TH AVE over I 25 ML	Replaced
1	E-17-GL	ADAMS	I 76 ML WBND over SOUTH PLATTE RIVER	Replaced
1	E-17-GM	ADAMS	I 76 ML EBND over SOUTH PLATTE RIVER	Replaced
1	E-17-HG	ADAMS	104TH AVE over I 25 ML	Replaced
1	E-17-HL	ADAMS	I 76 ML EBND over SH 224 ML	Replaced
1	F-16-F	ARAPAHOE	US 85(SANTA FE) ML NBND over DAD CLARK GULCH	Replaced
1	F-16-FY	ARAPAHOE	US 285 ML SBND over SH 88 ML	Replaced
1	F-16-FZ	ARAPAHOE	US 285 ML NBND over SH 88 ML	Replaced
1	F-19-B	ARAPAHOE	US 36 ML over COMANCHE CREEK	Replaced
1	E-16-FL	BROOMFIELD	CNTY RD / OLD WADS over US 36 ML (DENVER/BOULDER TNPK)	Replaced
1	E-16-FK	BROOMFIELD	SH 121 ML SBND- WADSWORTH PKWY over US 36 ML (DENVER/BOULDER TNPK)	Replaced
1	F-14-B	CLEAR CREEK	I 70 FRONTAGE RD over CLEAR CREEK (SR)	Replaced
1	E-16-FW	DENVER	PECOS STREET over I 70 ML	Replaced
1	E-17-BY	DENVER	I 70 ML EBND over SAND CREEK	Replaced
1	E-17-GE	DENVER	I 70 ML WBND over SAND CREEK	Replaced
1	F-16-BM	DENVER	SH 88 ML over RR, LAKEWOOD GULCH	Replaced
1	F-16-DP	DENVER	I 25 ML over RDWY,RR, SOUTH PLATTE RVR; BRONCO BRIDGE	Replaced
1	F-16-DT	DENVER	I 25 ML NBND over US 85 ML (SANTA FE)	Replaced
1	F-16-DW	DENVER	I 25 ML SBND over US 85 ML (SANTA FE)	Replaced
1	F-16-FW	DENVER	US 287+SH 88 (FEDERAL) over US 40 ML (COLFAX)	Replaced
1	F-16-OG	DENVER	RAMP to I 25 NBND over US 6 ML	Repaired
1	F-17-AE	DENVER	SH 30 ML/HAVANA ST over CHERRY CREEK	Replaced

2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection	Work Completed
1	G-16-B	DOUGLAS	US 85 ML over DRAW; COOK RANCH to LOUVIERS	Replaced
1	G-16-C	DOUGLAS	US 85 ML over DRAW; COOK RANCH to LOUVIERS	Replaced
1	E-16-FX	JEFFERSON	WASHINGTON STREET over SH 58 ML	Replaced
1	E-16-HI	JEFFERSON	SH 58 ML over CO. RD,RR SPUR	Replaced
1	F-16-AM	JEFFERSON	US 285 ML SBND over SH 121 ML	Replaced
1	F-16-AY	JEFFERSON	US 285 ML NBND over SH 121 ML	Replaced
1	F-16-CS	JEFFERSON	SH121 ML-WADSWORTH over BEAR CREEK	Replaced
1	F-16-FL	JEFFERSON	US 6 ML over SH 95 ML/SHERIDAN AVE.	Replaced
1	F-16-I	JEFFERSON	US 285 ML SBND over PIERCE STREET	Replaced
2	O-25-H	BACA	US 160 ML over N FK SAND ARROYO	Replaced
2	O-25-I	BACA	US 160 ML over DRAW	Replaced
2	O-26-L	BACA	US 160 ML over CAT CREEK	Replaced- minor structures
2	L-24-F	BENT	SH 101 ML over PURGATOIRE RIVER	Repaired
2	M-24-B	BENT	SH 101 ML over DRAW	Replaced
2	L-21-U	CROWLEY	SH 96 ML over NUMA DRAIN CANAL	Replaced- minor structure
2	L-22-F	CROWLEY	SH 96 ML over BLACK DRAW	Replaced
2	H-18-A	EL PASO	US 24 ML over BLACK SQUIRREL CREEK	Replaced
2	I-17-AE	EL PASO	US 24 ML EBND over FOUNTAIN CREEK	Repaired
2	I-18-G	EL PASO	US 24 ML over DRAW	Replaced
2	J-18-S	EL PASO	I 25 ML NBND over DRAW	Replaced- minor structure
2	J-18-T	EL PASO	I 25 ML NBND over DRAW	Replaced- minor structure
2	J-15-B	FREMONT	SH 9 ML over CURRANT CREEK	Replaced
2	K-16-Q	FREMONT	SH 120 ML over HARDSCRABBLE CREEK	Replaced
2	N-16-L	HUERFANO	SH 69 ML over TURKEY CREEK	Replaced
2	N-17-N	HUERFANO	I 25 ML NBND over MISSOURI CREEK	Replaced
2	O-16-A	HUERFANO	SH 12 ML over CUCHARAS RIVER	Replaced
2	К-23-В	KIOWA	SH 96 ML over DRAW	Replaced
2	K-23-C	KIOWA	SH 96 ML over DRAW	Replaced

2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection	Work Completed
2	K-24-A	KIOWA	SH 96 ML over DRAW	Replaced
2	O-19-J	LAS ANIMAS	US 350 ML over DRAW	Replaced
2	P-17-H	LAS ANIMAS	SH 12 ML over PURGATOIRE RIVER	Replaced
2	P-18-B	LAS ANIMAS	I 25 ML NBND over PURGATOIRE RIVER	Replaced
2	P-18-S	LAS ANIMAS	I 25 ML SBND over PURGATOIRE RIVER	Replaced
2	P-19-AD	LAS ANIMAS	SH 239(CO RD 75) ML over IRRIGATION CANAL	Replaced
2	L-22-E	OTERO	SH 266 ML over FT LYON STORAGE CANAL	Replaced
2	L-22-K	OTERO	SH 71 ML over FT LYON CANAL	Replaced
2	L-22-0	OTERO	SH 266 ML over HOLBROOK CANAL	Replaced
2	M-21-D	OTERO	US 350 ML over DRAW	Replaced
2	G-12-L	PARK	SH 9 ML over BUCKSKIN GULCH	Repaired
2	L-28-F	PROWERS	SH 89 ML over ARKANSAS RIVER	Replaced
2	K-18-Z	PUEBLO	SH 96 ML over RDWY, RR, ARKANSAS RVR	Replaced
2	L-19-C	PUEBLO	US 50 BUS. RT WBND over ST CHARLES RIVER	Replaced
2	M-17-R	PUEBLO	I 25 ML over DRAW	Repaired
2	M-20-A	PUEBLO	SH 10 ML over SAUNDERS ARROYO	Replaced
2	H-16-K	TELLER	SH 67 ML over DRAW	Replaced
2	I-15-Y	TELLER	US 24 ML over TWIN CREEK	Repaired
3	F-08-F	EAGLE	I 70 SERVICE RD over COLORADO RIVER (SR)	Replaced
3	F-09-H	EAGLE	US 6 ML over EAGLE RIVER	Replaced
3	J-09-C	GUNNISON	US 50 SERVICE RD over GUNNISON RVR OVERFLOW (SR)	Repaired
3	J-09-D	GUNNISON	US 50 SERVICE RD over GUNNISON RVR (SR)	Repaired
3	J-09-G	GUNNISON	SH 114 ML over TOMICHI CREEK	Replaced
3	G-11-F	LAKE	US 24 ML over UP RR	Replaced
3	H-11-D	LAKE	US 24 ML over CALIFORNIA GULCH	Replaced
3	H-11-F	LAKE	US 24 ML over CALIFORNIA GULCH	Replaced- minor structure
3	H-09-B	PITKIN	SH 82 ML over CO RD, CASTLE CREEK	Repaired
3	C-09-C	ROUTT	US 40 ML over E FORK ELK RIVER	Replaced

2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection	Work Completed
4	G-21-B	ELBERT	I 70 FRONTAGE RD over DRAW (SR)	Replaced
4	B-16-AE	LARIMER	US 287 ML over DRAW	Replaced
4	C-15-I	LARIMER	US 34 ML over BIG THOMPSON RIVER	Replaced
4	C-15-J	LARIMER	US 34 ML over BIG THOMPSON RIVER	Replaced
4	G-22-J	LINCOLN	US 24 ML over DRAW	Replaced
4	A-24-C/A-26-F	LOGAN SEDGWICK	US 138 ML over DITCH/DRAW	Replaced- minor structure
4	B-17-L	WELD	SH 14 ML over COALBANK CREEK	Replaced
4	C-17-BN	WELD	I 25 SERVICE RD over LITTLE THOMPSON RIVER	Replaced
4	D-17-AK	WELD	SH 66 ML over ST VRAIN RIVER	Replaced
4	D-28-B	YUMA	US 34 ML over N FK REPUBLICAN RIVER	Replaced
5	O-05-AQ	LA PLATA	US 160 ML over ANIMAS RIVER	Repaired
5	L-05-B	OURAY	SH 62 ML over UNCOMPAHGRE RIVER	Replaced
5	L-06-A	OURAY	US 550 ML over BEAR CREEK	Replaced
5	M-06-K	SAN JUAN	US 550 ML over MINERAL CREEK	Replaced
5	L-04-B	SAN MIGUEL	SH 145 ML over LEOPARD CREEK	Replaced

2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection		Budget	Status	Construction Start Date	Construction Completion Date	Project Delivery Method
1	F-19-AF	ADAMS	COUNTY ROAD over I 70 ML		TBD	Not Programmed	TBD	TBD	TBD
1	E-17-EZ	ADAMS	84TH AVE over I 25 ML	\$	11,949,000	Construction	02/24/11	10/31/12	D-B-B
			I 76 ML EBND over SOUTH PLATTE RIVER			Construction			
1	E-17-GM	ADAMS	NE of JCT I 270 I 76 ML WBND over SOUTH PLATTE RIVER	\$	13,120,000	Complete Construction	09/12/11	07/23/12	D-B-B
1	E-17-GL	ADAMS	NE of JCT I 270		See E-17-GM	Complete	09/12/11	07/23/12	D-B-B
1	E-16-AA	ADAMS	US 287 ML over BNSF RR SPUR SH 95 ML (SHERIDAN BLVD) over UP RR, RR	\$	17,320,000	In Design Construction	09/30/14	03/05/16	D-B-B
1	E-16-GQ	ADAMS	SPUR	\$	7,310,000	Complete	04/24/12	11/01/13	D-B-B
1	E-16-FP	ADAMS	80TH AVE over US 36 ML	\$	11,359,000	Construction Complete	05/06/10	10/20/11	D-B-B
1	E-17-ER	ADAMS	SH 44 ML(104TH AVE) over BULL SEEP W of US 85	\$	13,700,000	In Construction	01/06/14	06/30/15	D-B-B
1	E-17-CA	ADAMS	SH 44 ML(104TH AVE) over SOUTH PLATTE RIVER W of JCT US 85		See E-17-ER	In Construction	01/06/14	06/30/15	D-B-B
1	E-17-EX	ADAMS	PEORIA STREET over I 76 ML NE of JCT US 85	\$	5,930,000	Construction Complete	07/24/13	12/05/13	D-B-B
1	E-17-DC	ADAMS	I 76 ML EBND over UP RR E of JCT US 85	\$		Design	06/02/14	06/01/16	D-B-B
			I 76 ML WBND over UP RR	ļ		Design			
1	E-17-DU	ADAMS	E of JCT US 85		See E-17-DC	Completed Construction	06/02/14	06/01/16	D-B-B
1	E-17-HG	ADAMS	104TH AVE over I 25 ML	\$	8,540,000	Complete Construction	05/21/09	12/20/10	Construction Complete
1	E-17-AR	ADAMS	SH 7 ML over SOUTH PLATTE RIVER	\$		Complete Construction	05/19/09	01/07/11	Construction Complete
1	E-17-DM	ADAMS	I 76 ML WBND over UP RR	\$	6,750,000	Complete			Construction Complete
1	E-17-DN	ADAMS	I 76 ML EBND over UP RR	\$	-	Construction Complete			Construction Complete
1	E-17-HL	ADAMS	I 76 ML EBND over SH 224 ML	\$	-	Construction Complete			Construction Complete
1	E-17-EP	ADAMS	SH 6 DITCH RIDER RD over BURLINGTON CANAL SR	\$	-	No Action Proposed			
1	E-17-IC	ADAMS	YORK STREET over I 270 ML	. •	TBD		TBD	TBD	TBD
			US 36 ML over COMANCHE CREEK			Not Programmed Construction			
1	F-19-B	ARAPAHOE	E of STRASBURG US 40 ML(E COLFAX) EBND over SAND CREEK	\$	1,860,000	Complete	04/23/12	06/15/12	D-B-B
1	F-17-F	ARAPAHOE	E of I-225 US 40 ML(E COLFAX) WBND over SAND CREEK	\$	10,610,000	In Construction	07/23/13	12/22/14	D-B-B
1	F-17-BS	ARAPAHOE	E of I-225		See F-17-F	In Construction	07/23/13	12/22/14	D-B-B
1	F-16-F	ARAPAHOE	US 85(SANTA FE) ML NBND over DAD CLARK GULCH in LITTLETON	\$	3,030,000	Construction Complete	11/27/12	09/05/13	Streamlined D/B
1	F-17-DM	ARAPAHOE	SH 88 ML/ARAP RD over CHERRY CREEK W OF SH 83(PARKER RD)	\$	31,450,000	In Construction	10/21/13	05/01/15	D-B-B
1	F-17-GO	ARAPAHOE	US 40 ML(E COLFAX) EBND over TOLLGATE CREEK W of I-225	\$	16,960,000	Design Completed	06/01/14	01/31/16	D-B-B
1	F-17-GA	ARAPAHOE	US 40 ML(E COLFAX) WBND over TOLLGATE CREEK W of I-225		See F-17-GO	Design Completed	06/01/14	01/31/16	D-B-B
1	F-16-FY	ARAPAHOE	US 285 ML SBND over SH 88 ML		See F-16-AM	Construction Complete	08/31/10	07/31/11	Construction Complete
		ARAPAHOE	US 285 ML NBND over SH 88 ML		See F-16-AM	Construction			
1	F-16-FZ			1		Complete	08/31/10	07/31/11	Construction Complete
1	F-19-F	ARAPAHOE	US 36 ML over DRAW US 160 ML over CAT CREEK		TBD	Not Programmed Construction	TBD	TBD	TBD
2	0-26-L	BACA	W of SPRINGFIELD US 160 ML over DRAW	\$	3,960,000	Complete Construction	03/29/12	12/13/12	Modified D/B
2	O-25-I	BACA	W of PRITCHETT	r	See O-26-L	Complete	03/29/12	12/13/12	Modified D/B
2	O-25-H	BACA	US 160 ML over N FK SAND ARROYO SW of PRITCHETT		See O-26-L	Construction Complete	03/29/12	12/13/12	Modified D/B
2	M-24-B	BENT	SH 101 ML over DRAW S of LAS ANIMAS and JCT US 50	\$	4,560,000		03/29/12	10/31/12	Modified D/B
2	L-24-F	BENT	SH 101 ML over PURGATOIRE RIVER S of LAS ANIMAS		See M-24-B	Construction Complete	03/29/12	10/31/12	Modified D/B
4	E-15-AA	BOULDER	SH 170 ML over COMMUNITY DITCH AR	\$	_	No Action Proposed			
1	E-16-FL	BROOMFIELD	CNTY RD / OLD WADS over US 36 ML (DENVER/BOULDER TNPK) SE of JCT SH 121	\$		Construction	05/10/12	10/30/13	D/B
		BROOMFIELD	SH 121 ML SBND- WADSWORTH PKWY over US			Construction		•	D/B
1	E-16-FK		36 ML (DENVER/BOULDER TNPK) I 70 FRONTAGE RD over CLEAR CREEK (SR)	\$		Construction	05/10/12	10/30/13	
1	F-14-B	CLEAR CREEK	W IDAHO SPRINGS	\$			07/19/10	11/23/10	Construction Complete
1	F-14-Y	CLEAR CREEK	I 70(BUSINESS RT) over I 70 ML	\$	3,900,000	In Design No Action	01/01/15	10/30/15	CMGC
1	F-15-BL	CLEAR CREEK	I 70 ML WBND over US 6, CLEAR CREEK	\$	-	Proposed			
1	F-15-D	CLEAR CREEK	I 70 FRONTAGE RD over CLEAR CREEK (SR)	\$	-	No Action Proposed			
5	O-12-AD	CONEJOS	SH 371 ML over ALAMOSA RIVER	\$	-	No Action Proposed			
2	L-22-F	CROWLEY	SH 96 ML over BLACK DRAW		See K-23-B	Construction Complete	08/18/10	09/21/11	Construction Complete
2	L-21-U	CROWLEY	SH 96 ML over NUMA DRAIN CANAL	\$	-	Construction Complete			Construction Complete
1	F-17-AE	DENVER	SH 30 ML/HAVANA ST over CHERRY CREEK	\$		Construction	02/07/11	06/15/12	Construction Complete
			I 70 ML WBND over SAND CREEK			Construction			
1	E-17-GE	DENVER	E of QUEBEC ST	\$	10,770,000	Complete	07/29/11	07/06/12	D-B-B w/ A+B bid

2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection		Budget	Status	Construction Start Date	Construction Completion Date	Project Delivery Method
1	E-17-BY	DENVER	I 70 ML EBND over SAND CREEK E of QUEBEC ST		See E-17-GE	Construction Complete	07/29/11	07/06/12	D-B-B w/ A+B bid
1	F-16-DP	DENVER	I 25 ML over RDWY,RR, SOUTH PLATTE RVR BRONCO BRIDGE	\$		Construction	05/02/11	07/11/13	Construction Complete
1	F-16-DT	DENVER	I 25 ML NBND over US 85 ML (SANTA FE)	\$		Construction	07/11/11	09/19/13	D-B-B
				ļ		Construction			
1	F-16-DW	DENVER	I 25 ML SBND over US 85 ML (SANTA FE) US 287+SH 88 (FEDERAL) over US 40 ML	I	See F-16-DT	Complete Construction	07/11/11	09/19/13	D-B-B
1	F-16-FW	DENVER	(COLFAX) PERRY STREET over US 6 ML	\$	8,290,000	Complete No Action	09/26/11	01/16/13	D-B-B
1	F-16-GG	DENVER	W of FEDERAL US 6 ML over BNSF RR	\$	-	Proposed			Transfer out of CBE
1	F-16-EJ	DENVER	E SIDE OF I-25 PECOS STREET over I 70 ML	\$	14,140,000	In Construction Construction	06/30/13	09/30/15	D/B
1	E-16-FW	DENVER	in DENVER US 6 ML over SOUTH PLATTE RIVER	\$	25,500,000		11/05/12	10/01/13	CMGC
1	F-16-EF	DENVER	W SIDE of I-25	\$	16,380,000	In Construction	06/30/13	09/30/15	D/B
1	F-16-EN	DENVER	US 6 ML over BRYANT STREET W SIDE OF I-25	\$	36,210,000	In Construction	06/30/13	09/30/15	D/B
1	E-17-AH	DENVER	ON 40TH AVE W of SH 2 ML over BNSF RR	\$	-	No Action Proposed			Transfer out of CBE
1	E-17-EW	DENVER	I 70 ML EBND over UP RR; W of QUEBEC STREET		TBD	Not Programmed	TBD	TBD	TBD
1	F-16-BM	DENVER	SH 88 ML over RR, LAKEWOOD GULCH	\$	-	Construction Complete			Construction Complete
1	E-17-FX	DENVER	I 70 ML over US 6, RR, CITY ST	\$	39,500,000	In Design	TBD	TBD	TBD
1	E-17-DF	DENVER	I 70 ML WBND over UP RR; W of QUEBEC STREET	, ,	TBD	Not Programmed	TBD	TBD	TBD
1	E-17-JP	DENVER	I 70 ML over HAVANA ST, UP RR	\$			11/18/14	05/02/16	D/B
						Construction	11/10/14	03/02/18	
1	F-16-OG	DENVER	RAMP to I 25 NBND over US 6 ML	\$		Complete		-	CDOT Maintenance
1	E-17-KR	DENVER	I 270 ML EBND over I 70 ML	1	TBD	Not Programmed	TBD	TBD	TBD
1	G-16-B	DOUGLAS	US 85 ML over DRAW; COOK RANCH to LOUVIERS	\$	3,410,000		10/19/12	11/15/13	D-B-B
1	G-16-C	DOUGLAS	US 85 ML over DRAW; COOK RANCH to LOUVIERS		See G-16-B	Construction Complete	10/19/12	11/15/13	D-B-B
1	G-17-A	DOUGLAS	US 85 ML over SAND CREEK	\$	490,000	In Design	TBD	TBD	Design to be Shelved
3	F-09-H	EAGLE	US 6 ML over EAGLE RIVER E of EAGLE	\$	4,510,000	Construction Complete	07/20/11	05/18/12	D-B-B
3	F-08-D	EAGLE	I 70 SERVICE RD over UP RR (SR)		TBD	Not Programmed	TBD	TBD	TBD
3	F-08-F	EAGLE	I 70 SERVICE RD over COLORADO RIVER (SR) N. of DOTSERO INT.	\$	10,540,000	Construction Complete	09/04/12	09/30/13	CMGC
3	F-11-AC	EAGLE	I 70 ML EBND over US 6, RR, EAGLE RIVER E of JCT SH 131	\$			10/11/14	03/29/16	D-B-B w/ A+B bid
3	F-11-AB	EAGLE	I 70 ML WBND over US 6, RR, EAGLE RIVER E of JCT US 24		See F-11-AC	In Design	10/11/14	03/29/16	D-B-B w/ A+B bid
3	F-10-L	EAGLE	170 ML EBND over US 6, RR, EAGLE RIVER	1	TBD	Not Programmed	TBD	TBD	TBD
			170 ML EBND over TIMBER CREEK			No Action			001
3	F-11-AO	EAGLE	US 24 ML over BLACK SQUIRREL CREEK	\$		Proposed Construction			
2	H-18-A	EL PASO	W of PEYTON	\$	3,280,000	Complete Construction	11/15/11	08/17/12	D-B-B
2	I-17-AE	EL PASO	US 24 ML EBND over FOUNTAIN CREEK		See H-16-K	Complete	08/04/10	10/21/10	Construction Complete
2	H-17-M	EL PASO	I 25 ML over DRAW US 24 ML over DRAW	\$	-	In Construction Construction	03/01/13	12/31/14	D/B
2	I-18-G	EL PASO	E of FALCON I 25 ML NBND over DRAW	\$		Complete Construction			Construction Complete
2	J-18-S	EL PASO	S of FOUNTAIN I 25 ML NBND over DRAW	\$	1,150,000		02/20/12	08/17/12	Streamlined D/B
2	J-18-T	EL PASO	S of FOUNTAIN		See J-18-S	Complete No Action	02/20/12	08/17/12	Streamlined D/B
2	I-17-0	EL PASO	S of JCT SH 56	\$	190,000	Proposed			-
4	G-21-B	ELBERT	I 70 FRONTAGE RD over DRAW (SR)	\$	1,360,000		01/28/13	05/23/13	D-B-B
4	G-21-Y	ELBERT	I 70 BUSINESS SPUR over I 70 ML	\$		No Action Proposed			
2	К-16-К	FREMONT	SH 120 ML over RR, ARKANSAS RIVER E of PORTLAND	\$	6,130,000	In Construction	10/08/12	04/30/14	D-B-B
2	J-15-B	FREMONT	SH 9 ML over CURRANT CREEK NW of JCT US 50	\$	1,860,000	Construction Complete	05/04/11	10/31/11	Modified D/B
2	K-16-S	FREMONT	SH 120 ML over DRAW, UP RR E of FLORENCE	\$	5, <u>2</u> 00,000	Design Completed	06/24/14	03/20/15	D-B-B
2	K-16-Q	FREMONT	SH 120 ML over HARDSCRABBLE CREEK	\$		Construction Complete			Construction Complete
2	K-14-J	FREMONT	US 50 ML over DRAW, near COTOPAXI	\$			07/08/14	11/21/14	D-B-B
·		FREMONT	SH 67 ML over DRAW			No Action Proposed	07/00/14	17/27/14	
2	K-16-W			\$				-	
2	K-14-B	FREMONT	US 50 ML over OAK CREEK SH 82 ML over I 70 ML, COLORADO RVR,RR		TBD	Not Programmed	TBD	TBD	TBD
3	F-07-A	GARFIELD	GLENWOOD SPRINGS	\$			04/01/15	11/20/17	CMGC
3	F-05-L	GARFIELD	I 70 ML WBND over COLORADO RIVER		TBD	Not Programmed	TBD	TBD	TBD

2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection		Budget	Status	Construction Start Date	Construction Completion Date	Project Delivery Method
3	F-05-C	GARFIELD	SH 13 ML over RIFLE CREEK	\$	-	No Action Proposed			
3	D-13-A	GRAND	US 34 ML over N FK COLORADO RIVER	ļ	TBD	Not Programmed	TBD	TBD	TBD
	J-09-C	GUNNISON	US 50 SERVICE RD over GUNNISON RVR OVERFLOW (SR) W. SIDE of GUNNISON			Construction	08/29/11	08/31/12	D-B-B
3			US 50 SERVICE RD over GUNNISON RVR (SR)	\$		Construction			
3	J-09-D	GUNNISON	W. SIDE of GUNNISON	I	See J-09-C	Complete Construction	08/29/11	08/31/12	D-B-B
3	J-09-G	GUNNISON	SH 114 ML over TOMICHI CREEK	\$	-	Complete Construction		-	Construction Complete
2	N-17-N	HUERFANO	I 25 ML NBND over MISSOURI CREEK SH 12 ML over CUCHARAS RIVER	\$	2,520,000	Complete Construction	01/27/11	09/01/11	Construction Complete
2	O-16-A	HUERFANO	S of LA VETA		See P-17-H	Complete Construction	02/19/12	11/15/12	Modified D/B
2	N-16-L	HUERFANO	SH 69 ML over TURKEY CREEK	\$	2,475,000		06/22/11	07/15/11	Construction Complete
2	N-17-AD	HUERFANO	I 25 ML SBND over US 160 ML, RR SPUR	\$	-	Proposed			
2	M-16-P	HUERFANO	SH 69 ML over MILLIGAN ARROYO	\$	450,000	In Design			Design to be Shelved
2	N-17-C	HUERFANO	I 25 BUS RT over SULL CREEK	\$	2,920,000	In Construction	02/17/14	09/30/14	D-B-B
2	N-17-BN	HUERFANO	125 ML SBND over CO RD 640, BUTTE CREEK		TBD	Not Programmed	TBD	TBD	TBD
2	N-17-S	HUERFANO	125 ML NBND over CO RD 103, BUTTE CREEK		TBD	Not Programmed	TBD	TBD	TBD
1	F-16-CS	JEFFERSON	SH 121 ML-WADSWORTH over BEAR CREEK N OF 285	\$	10,300,000	Construction Complete	03/26/12	08/30/13	D-B-B
1	F-16-FL	JEFFERSON	US 6 ML over SH 95 ML/SHERIDAN AVE.	\$		Construction	01/03/12	07/12/13	D-B-B
1	F-16-AM	JEFFERSON	US 285 ML SBND over SH 121 ML	s		Construction	08/31/10	07/31/11	Construction Complete
				Ψ		Construction			
1	F-16-AY	JEFFERSON	US 285 ML NBND over SH 121 ML		See F-16-AM	Complete Construction	08/31/10	07/31/11	Construction Complete
1	F-16-I	JEFFERSON	US 285 ML SBND over PIERCE STREET	1	See F-16-AM	Complete Construction	08/31/10	07/31/11	Construction Complete
1	E-16-FX	JEFFERSON	WASHINGTON STREET over SH 58 ML	\$	6,100,000	Complete Construction	02/20/08	11/02/09	Construction Complete
1	E-16-HI	JEFFERSON	SH 58 ML over CO.RD,RR SPUR	\$	9,150,000	Complete			Construction Complete
1	E-16-HA	JEFFERSON	SH 58 ML over FORD STREET, WASH	\$	6,650,000	In Construction	06/04/13	06/15/14	D-B-B
1	F-16-ER	JEFFERSON	US 6 ML over GARRISON STREET	\$	13,200,000		09/15/14	12/31/15	Streamlined D/B
2	K-23-B	KIOWA	SH 96 ML over DRAW	\$	3,590,000	1	08/18/10	09/21/11	Construction Complete
2	K-23-C	KIOWA	SH 96 ML over DRAW		See K-23-B	Construction Complete	08/18/10	09/21/11	Construction Complete
2	K-24-A	KIOWA	SH 96 ML over DRAW		See K-23-B	Construction Complete	08/18/10	09/21/11	Construction Complete
	11277	NOWA			000112010	Construction	00/10/10	00/21/11	Construction Complete
5	O-05-AQ	LA PLATA	US 160 ML over ANIMAS RIVER	\$	810,000	Complete Construction	07/26/10	11/23/10	Construction Complete
3	G-11-F	LAKE	US 24 ML over UP RR	\$	6,890,000		12/30/10	11/09/11	Construction Complete
3	H-11-D	LAKE	US 24 ML over CALIFORNIA GULCH	\$	-	Complete	07/26/12	11/02/12	Construction Complete
3	H-11-F	LAKE	US 24 ML over CALIFORNIA GULCH	\$	-	Construction Complete	07/26/12	11/02/12	Construction Complete
4	B-16-AE	LARIMER	US 287 ML over DRAW N of JCT SH 1	\$	3,960,000	Construction Complete	07/25/11	05/01/12	D-B-B
4	B-16-D	LARIMER	SH 14 ML over CACHE LA POUDRE RIVER E of JCT US 287	\$	14,640,000	, and a second s	08/14/14	09/30/15	D-B-B
4	C-15-I	LARIMER	US 34 ML over BIG THOMPSON RIVER	\$	5,360,000		08/17/09	06/30/10	Construction Complete
4	C-15-J	LARIMER	US 34 ML over BIG THOMPSON RIVER	_	See C-15-I	Construction Complete	08/17/09	06/30/10	Construction Complete
4	C-17-EL	LARIMER	I 25 ML over DRAW	\$		No Action Proposed			
4	B-16-EU	LARIMER	COUNTY ROAD 48 over I 25 ML		TBD	Not Programmed	TBD	TBD	TBD
2	P-17-H	LAS ANIMAS	SH 12 ML over PURGATOIRE RIVER NW of WESTON	\$		Construction	02/19/12	11/15/12	Modified D/B
2		LAS ANIMAS	US 350 ML over PURGATOIRE RIVER NE of JCT US 160				04/29/13	04/01/14	D-B-B
	O-19-H			\$		In Construction Construction			
2	P-18-B	LAS ANIMAS	I 25 ML NBND over PURGATOIRE RIVER	\$		Complete Construction			Construction Complete
2	P-18-S	LAS ANIMAS	I 25 ML SBND over PURGATOIRE RIVER US 350 ML over DRAW	\$		Complete Construction		-	Construction Complete
2	O-19-J	LAS ANIMAS	S of MODEL SH 239(CO RD 75) ML over IRRIGATION CANAL	\$	2,410,000		12/03/12	06/18/13	D-B-B
2	P-19-AD	LAS ANIMAS	in TRINIDAD		See O-19-J	Complete	12/03/12	06/18/13	D-B-B
2	P-23-A_MINOR	LAS ANIMAS	US 160 ML over SMITH CANYON TRIBUTARY US 24 ML over DRAW	\$	1,470,000	In Design Construction	06/01/14	08/31/14	D-B-B
4	G-22-J	LINCOLN	E of LIMON	\$	1,040,000	Complete	05/02/11	08/24/11	D-B-B
4	A-24-C A-26-F	LOGAN SEDGWICK	US 138 ML over DITCH/DRAW	\$	870,000	Construction Complete	10/01/10	12/15/10	Construction Complete
3	G-03-Q	MESA	I 70 ML WBND over COLORADO RIVER OVERFLOW		TBD	Not Programmed	TBD	TBD	TBD
2	L-22-0	OTERO	SH 266 ML over HOLBROOK CANAL NE of ROCKY FORD	\$	8,370,000	Construction Complete	08/20/12	03/07/13	CMGC


2013 Regions	Original Bridge Number	County	Facility Carried over Featured Intersection		Budget	Status	Construction Start Date	Construction Completion Date	Project Delivery Method
2	L-22-E	OTERO	SH 266 ML over FT LYON STORAGE CANAL NE of ROCKY FORD		See L-22-0	Construction Complete	08/20/12	03/07/13	CMGC
2	L-22-K	OTERO	SH 71 ML over FT LYON CANAL NW of ROCKY FORD		See L-22-0	Construction Complete	08/20/12	03/07/13	CMGC
2	M-21-D	OTERO	US 350 ML over DRAW SW of LA JUNTA & TIMPAS	\$	1,960,000	Construction Complete	10/19/11	05/18/12	D-B-B
2	L-22-L	OTERO	SH 71 ML over ARKANSAS RIVER		TBD	Not Programmed	TBD	TBD	TBD
5	L-05-B	OURAY	SH 62 ML over UNCOMPAHGRE RIVER SHERMAN ST in RIDGWAY	\$	7,800,000	Construction Complete	04/24/12	11/09/12	D-B-B
5	L-06-A	OURAY	US 550 ML over BEAR CREEK	\$	5,850,000	Construction Complete	07/26/10	10/24/11	Construction Complete
2	G-12-L	PARK	SH 9 ML over BUCKSKIN GULCH in ALMA	\$	320,000	Construction Complete	9/5/11	12/29/11	D-B-B
2	G-12-C	PARK	SH 9 ML over PLATTE GULCH		TBD	Not Programmed	TBD	TBD	TBD
3	H-09-B	PITKIN	SH 82 ML over CO RD, CASTLE CREEK	\$	980,000	Construction Complete	01/27/11	07/21/11	Construction Complete
2	L-28-F	PROWERS	SH 89 ML over ARKANSAS RIVER S of HOLLY	\$	6,370,000	Construction Complete	02/16/11	12/01/11	D-B-B
2	L-27-S	PROWERS	US 50 ML over DRAW E of LAMAR		See L-28-C	In Design	07/07/14	06/01/15	D-B-B
2	L-28-C	PROWERS	US 50 ML over BNSF RR E of GRANADA	\$	6,700,000		07/07/14	06/01/15	D-B-B
2	K-18-AX	PUEBLO	I 25 ML NBND over US 50 BUS. RTE.	\$	2,560,000	In Design	08/01/14	09/01/15	D/B
2	K-18-CL	PUEBLO	I 25 ML SBND over NP RR,ILEX ST,BENNET ST S of JCT SH 96	\$	45,980,000	In Design	08/01/14	07/01/16	D/B
2	K-18-CK	PUEBLO	I 25 ML NBND over NP RR,ILEX ST,BENNET ST N of JCT SH 50 E		See K-18-CL	In Design	08/01/14	07/01/16	D/B
2	K-18-R	PUEBLO	US 50 BUS EBND over ARKANSAS RIVER	\$	1,680,000	In Design	08/01/14	09/01/15	D/B
2	K-18-Z	PUEBLO	SH 96 ML over RDWY, RR, ARKANSAS RVR	\$	-	Construction Complete	11/07/07	04/01/11	Construction Complete
2	L-18-AQ	PUEBLO	NORTHERN AVE over I 25 ML	\$	2,900,000	In Design	08/01/14	09/01/15	D/B
2	L-18-M	PUEBLO	I 25 ML NBND over INDIANA AVE	\$	1,540,000	In Design	08/01/14	09/01/15	D/B
2	L-18-W	PUEBLO	I 25 ML SBND over INDIANA AVE	\$	780,000	In Design	08/01/14	09/01/15	D/B
2	L-19-C	PUEBLO	US 50 BUS RT WBND over ST CHARLES RIVER	\$	2,960,000	Construction Complete	10/16/09	07/22/10	Construction Complete
2	M-17-R	PUEBLO	I 25 ML over DRAW	\$	-	Construction Complete			Construction Complete
2	M-20-A	PUEBLO	SH 10 ML over SAUNDERS ARROYO	\$	2,000,000	Construction Complete			Construction Complete
2	L-18-AU	PUEBLO	MESA AVE over I 25 ML	\$	1,930,000	In Design	08/01/14	09/01/15	D/B
2	K-17-F	PUEBLO	SH 96 ML over RUSH CREEK		TBD	Not Programmed	TBD	TBD	TBD
2	L-19-G	PUEBLO	SH 96 ML over BOB CREEK CANAL		TBD	Not Programmed	TBD	TBD	TBD
5	N-11-C	RIO GRANDE	SH 112 ML over RIO GRANDE CANAL		TBD	Not Programmed	TBD	TBD	TBD
3	C-09-C	ROUTT	US 40 ML over E FORK ELK RIVER W of STEAMBOAT SPGS	\$	6,560,000	Construction	02/28/13	11/19/13	D-B-B
5	M-06-K	SAN JUAN	US 550 ML over MINERAL CREEK	\$	3,650,000	Construction Complete	08/17/09	06/01/11	Construction Complete
5	L-04-B	SAN MIGUEL	SH 145 ML over LEOPARD CREEK JCT SH 62 - PLACERVILLE	\$	4,270,000	Construction Complete	05/15/12	12/07/12	D-B-B
3	E-12-I	SUMMIT	SH 9 ML over BLUE RIVER	\$	-	No Action Proposed			
2	H-16-K	TELLER	SH 67 ML over DRAW	\$	2,620,000	Construction Complete	08/04/10	12/31/10	Construction Complete
2	I-15-Y	TELLER	US 24 ML over TWIN CREEK		See H-16-K	Construction Complete	08/04/10	10/21/10	Construction Complete
4	C-17-BN	WELD	I 25 SERVICE RD over LITTLE THOMPSON RIVER S of JCT SH 56	\$	2,720,000	Construction	09/04/12	04/12/13	D/B
4	D-17-AK	WELD	SH 66 ML over ST VRAIN RIVER W of PLATTEVILLE	\$	6,000,000	Construction	11/05/12	10/30/13	D-B-B
4	C-18-BK	WELD	US 85 BYPASS SBND over US 85 BUS RT	\$	-	No Action Proposed			
4	D-19-A	WELD		\$	-	No Action Proposed			
4	B-17-L	WELD	SH 14 ML over COALBANK CREEK W of AULT	\$	7,530,000	Construction	02/01/13	09/30/13	D-B-B
4	B-17-C	WELD	US 85 ML (NUNN BRIDGE) over UPRR	\$		In Construction	03/17/13	06/01/14	D-B-B
4	С-17-В	WELD	SH 60 ML over SOUTH PLATTE RIVER		TBD	Not Programmed	TBD	TBD	TBD
4	D-28-B	YUMA	US 34 ML over N FK REPUBLICAN RIVER W of LAIRD	\$	3,470,000	Construction	06/25/12	12/14/12	D-B-B
4	U-20-D	I UIVIA	W UI LAIND	φ	3,470,000	Jomplete	00/20/12	12/14/12	U-D-D

0 1

2

5

 \bigcirc 3 • 4

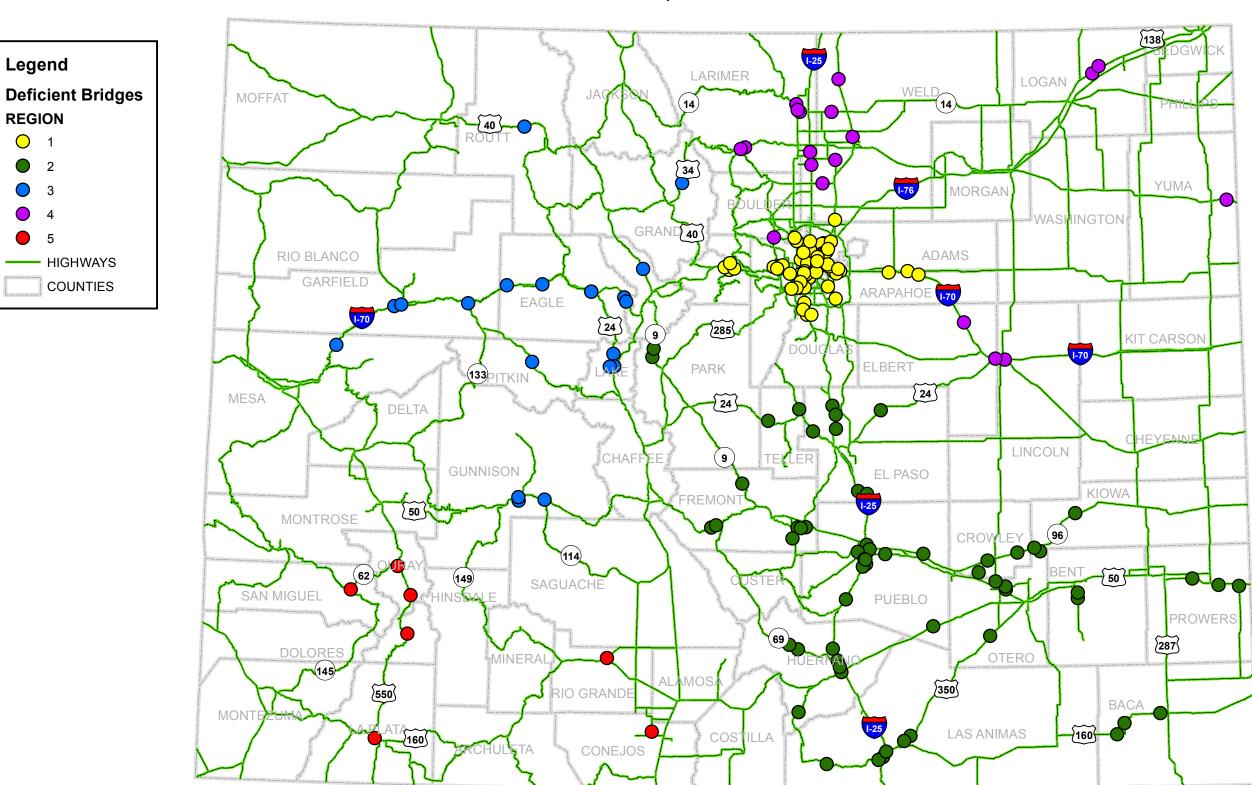

Colorado State Map of FASTER Eligible Bridges Q3-FY2014

179 Faster Eligible Bridges
