

Project Name: I-70 Floyd Hill West Section

Project Number: 25175


Date: January 2024 Update

## I-70 Floyd Hill West Section Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

### Key Dates

The following image shows the progression of the key project dates.

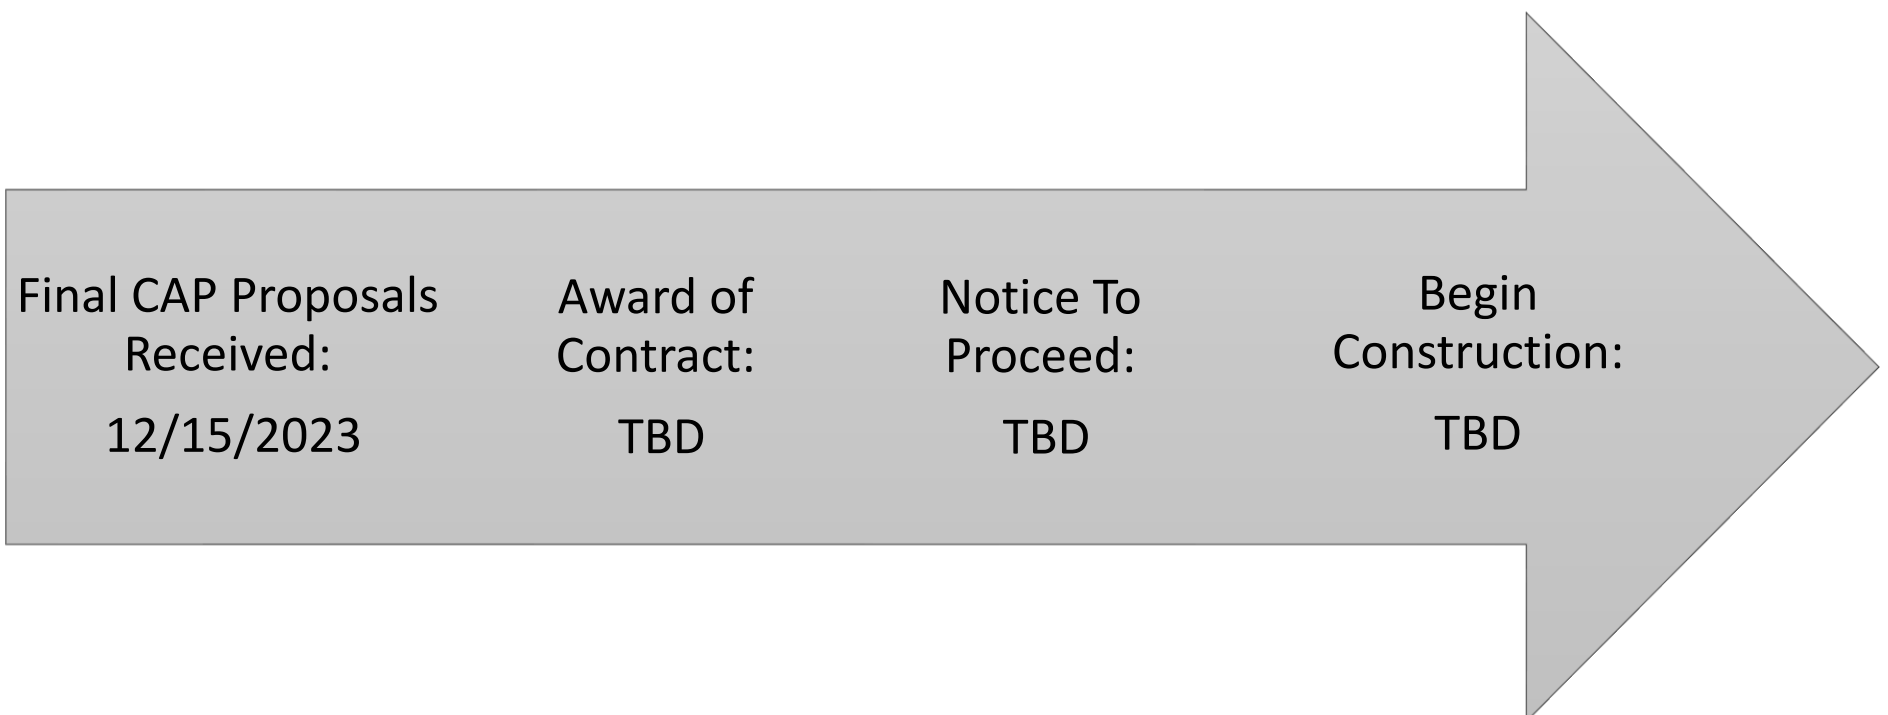

Final CAP Proposals Received: 12/15/2023

Award of Contract: TBD

Notice To Proceed: TBD

Begin Construction: TBD




Project Name: I-70 Floyd Hill West Section

Project Number: 25175

Date: January 2024 Update

### Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

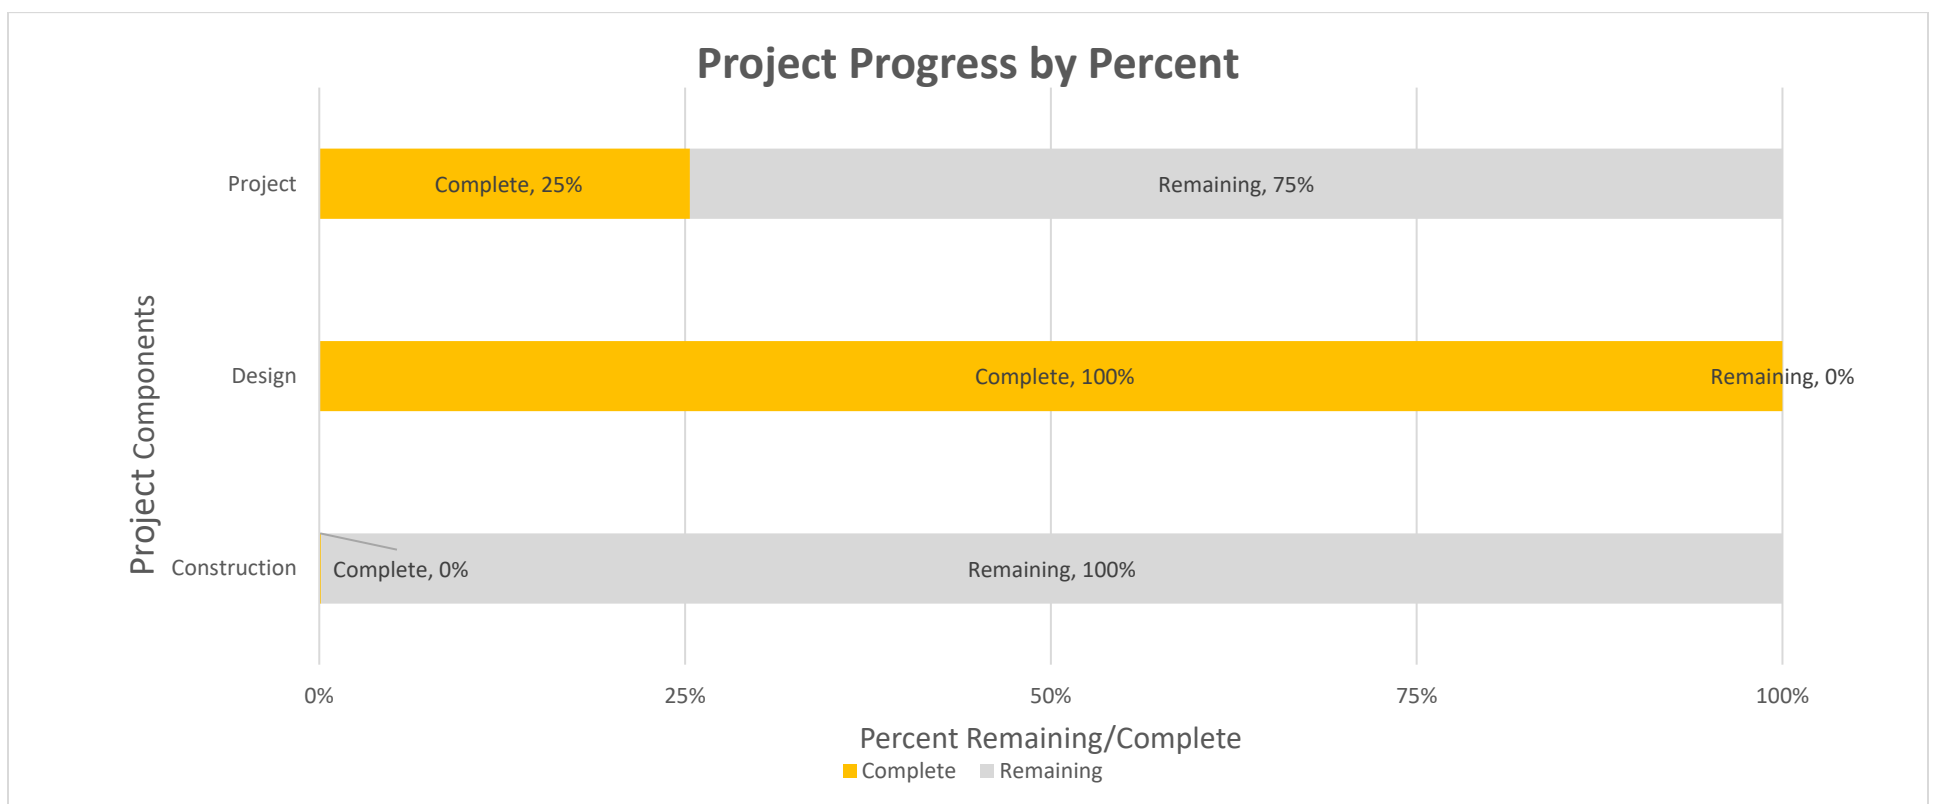

Overall Project: 25% Complete, 75% Remaining

Design: 100% Complete, 0% Remaining

Construction: 0% Complete, 100% Remaining


Project Name: I-70 Floyd Hill West Section

Project Number: 25175

Date: January 2024 Update

### Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

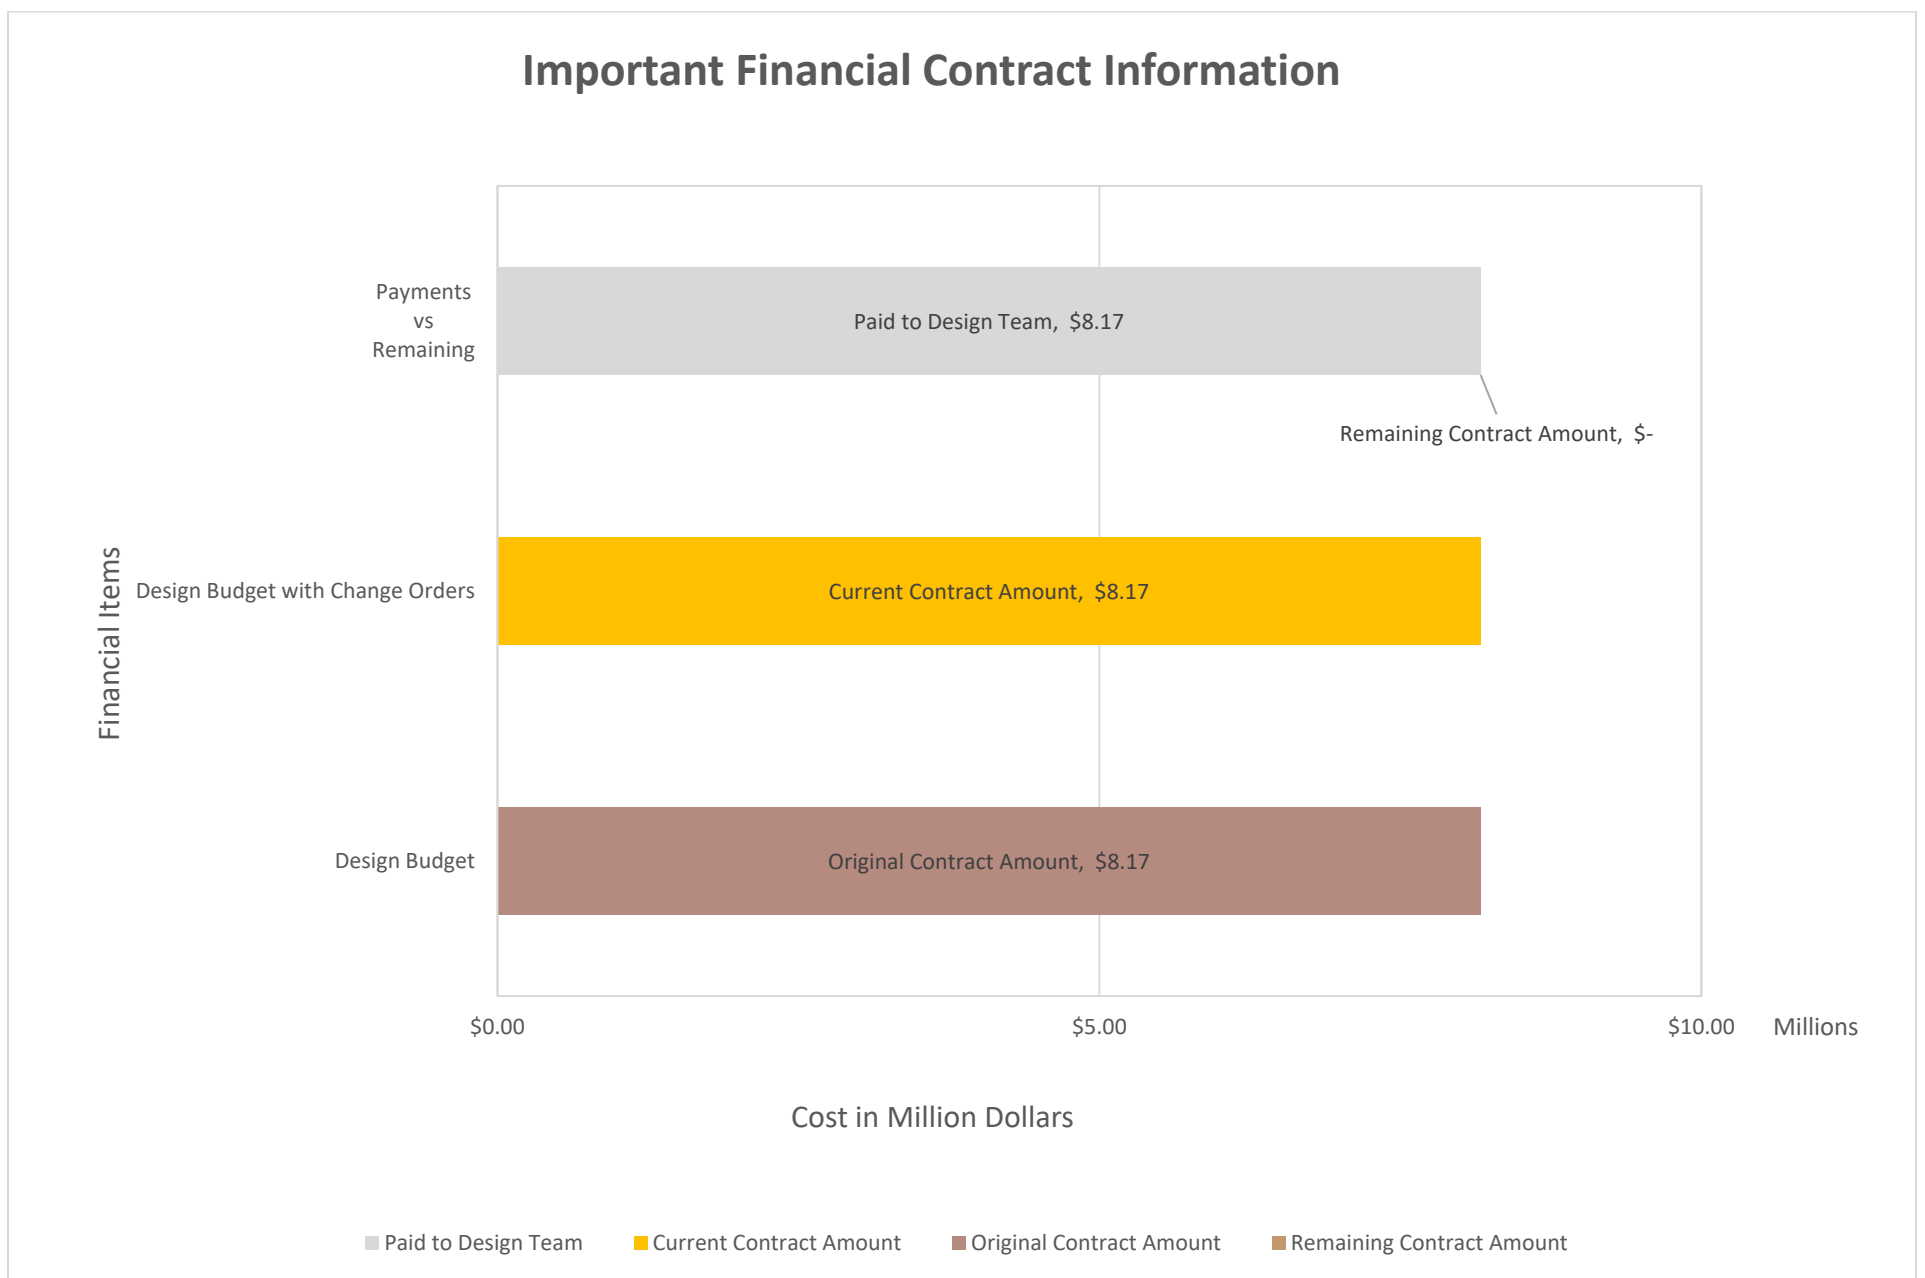

Initial Design Contract Value: \$8.17 Million

Design Payments to date: \$8.17 Million, Design Payments remaining: \$0

Current Contract Value: \$8.17 Million, Total Change Orders to Date: \$0


Project Name: I-70 Floyd Hill West Section

Project Number: 25175

Date: January 2024 Update

## Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

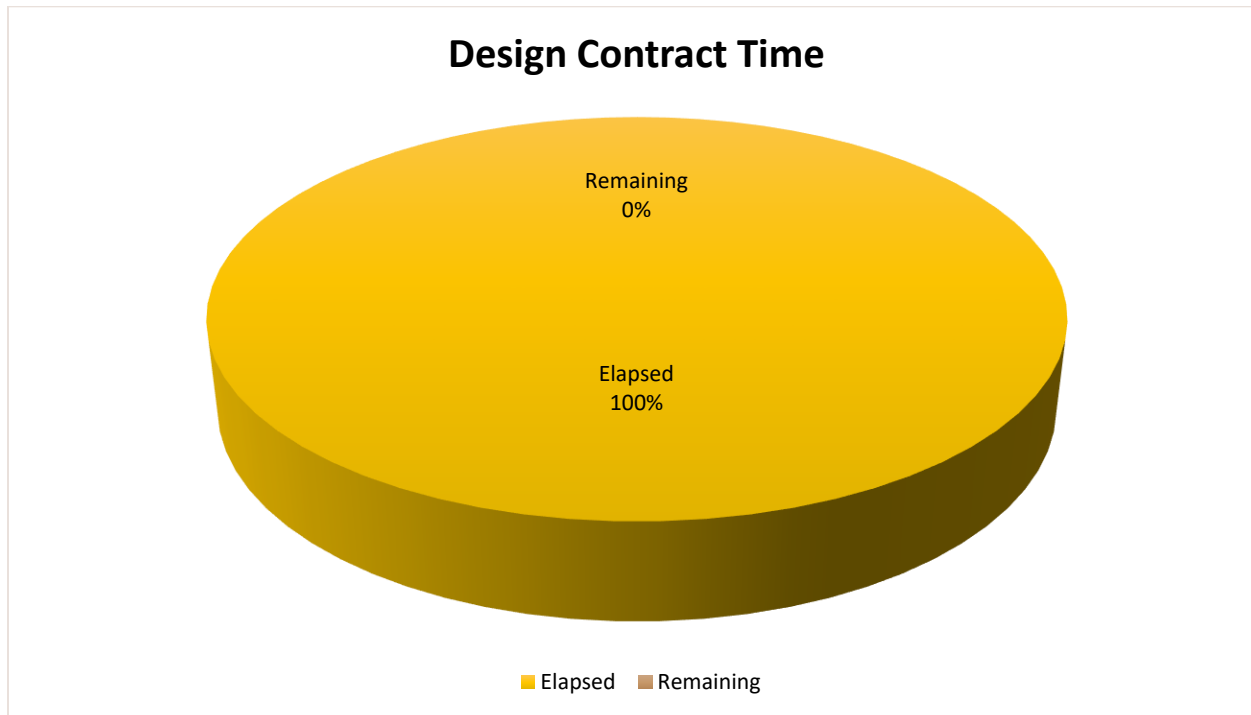

Total Design Contract time: 445 days

Elapsed Contact time: 445 days, 100%

Contract Time Remaining: 0 days , 0%
