

Project Name: US 6D STR F-06-A Elk Creek - New Castle
Project Number: 24493, FBR 0063-066
Date: October, 2026 Update

US 6D STR F-06-A Elk Creek - New Castle Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.




- Proposal Received: March 10, 2023
- Notice of Selection: March 31, 2023
- Award of Contract: August 28, 2023
- Notice to Proceed #1: September 18, 2025

Project Name: US 6D STR F-06-A Elk Creek - New Castle
Project Number: 24493, FBR 0063-066
Date: October, 2026 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

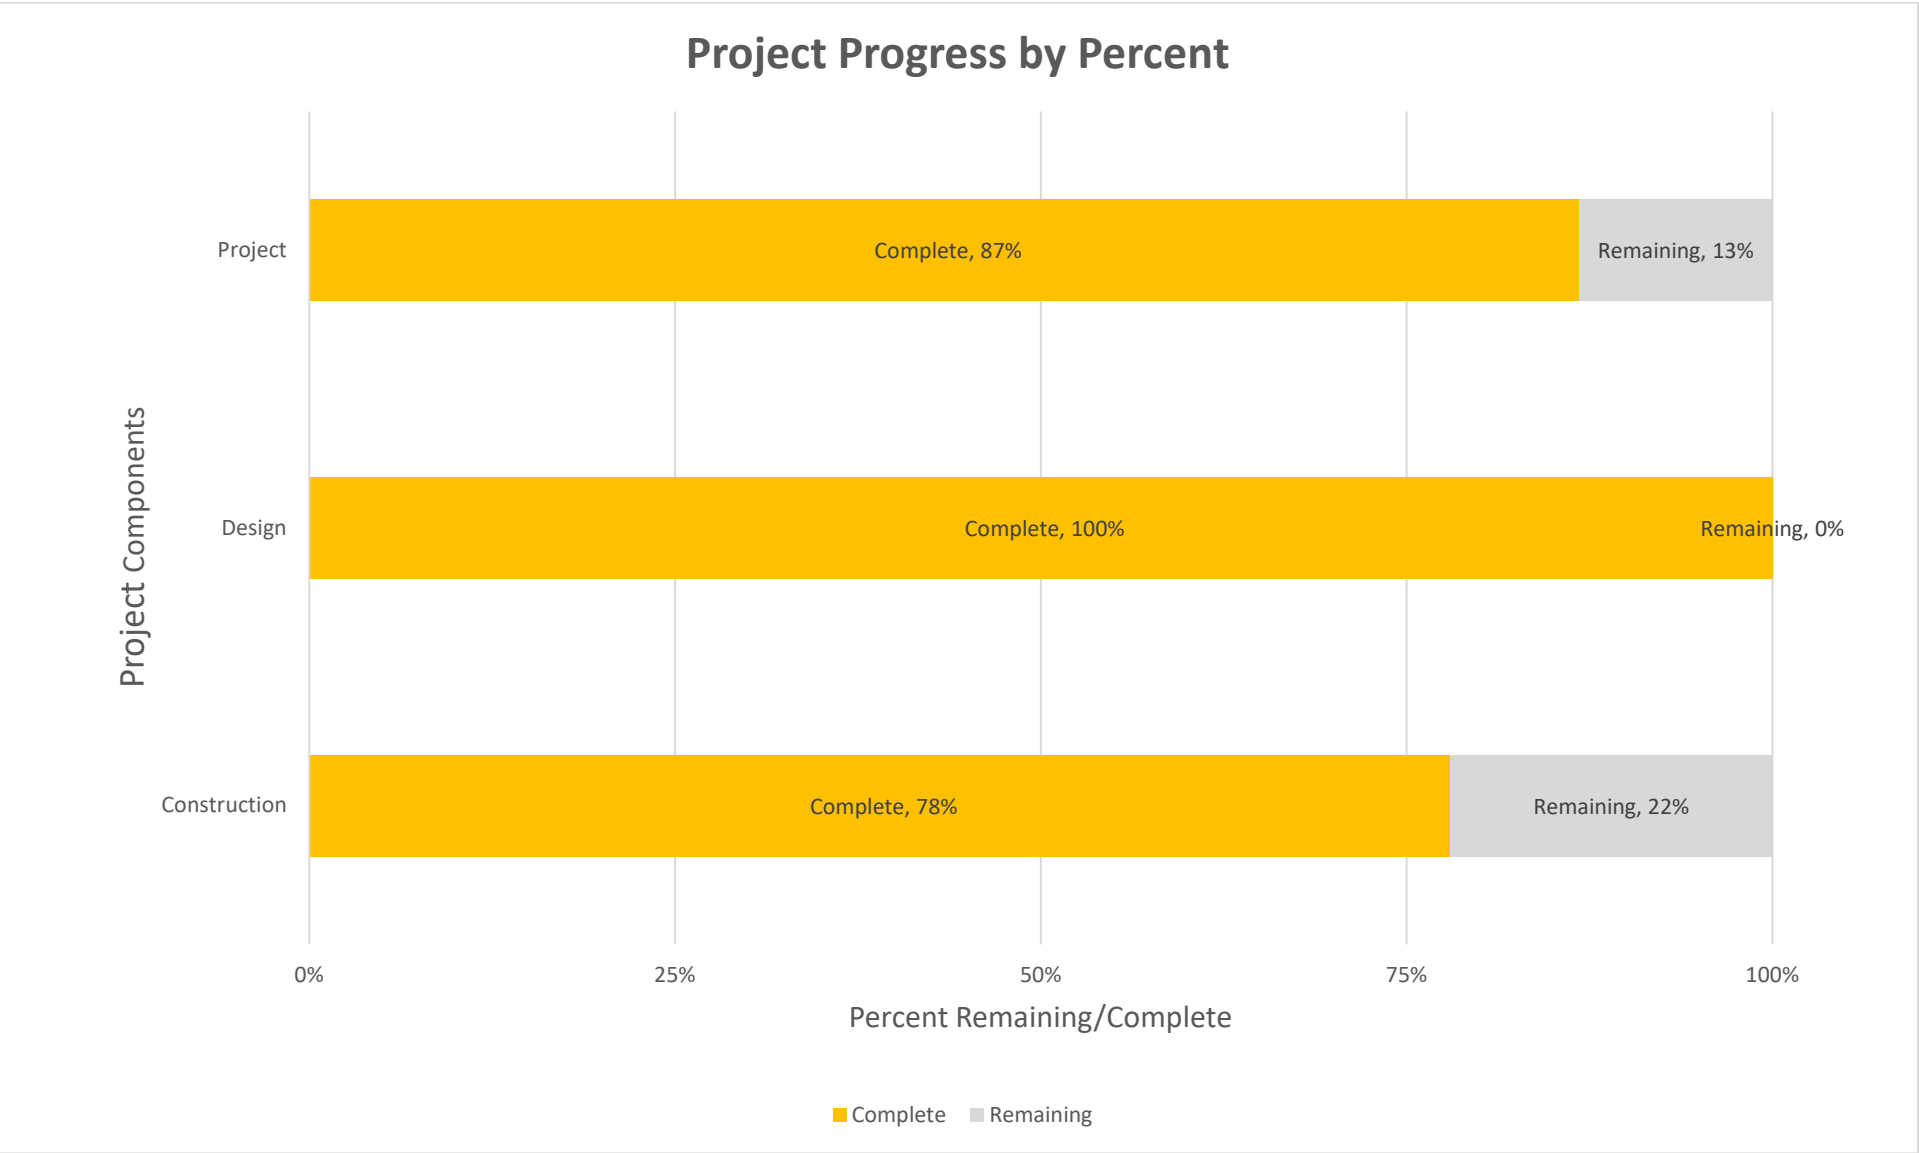


Overall Project: 87% Complete, 13% Remaining
Design: 100% Complete, 0% Remaining
Construction: 78% Complete, 22% Remaining

Project Name: US 6D STR F-06-A Elk Creek - New Castle
Project Number: 24493, FBR 0063-066
Date: October, 2026 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

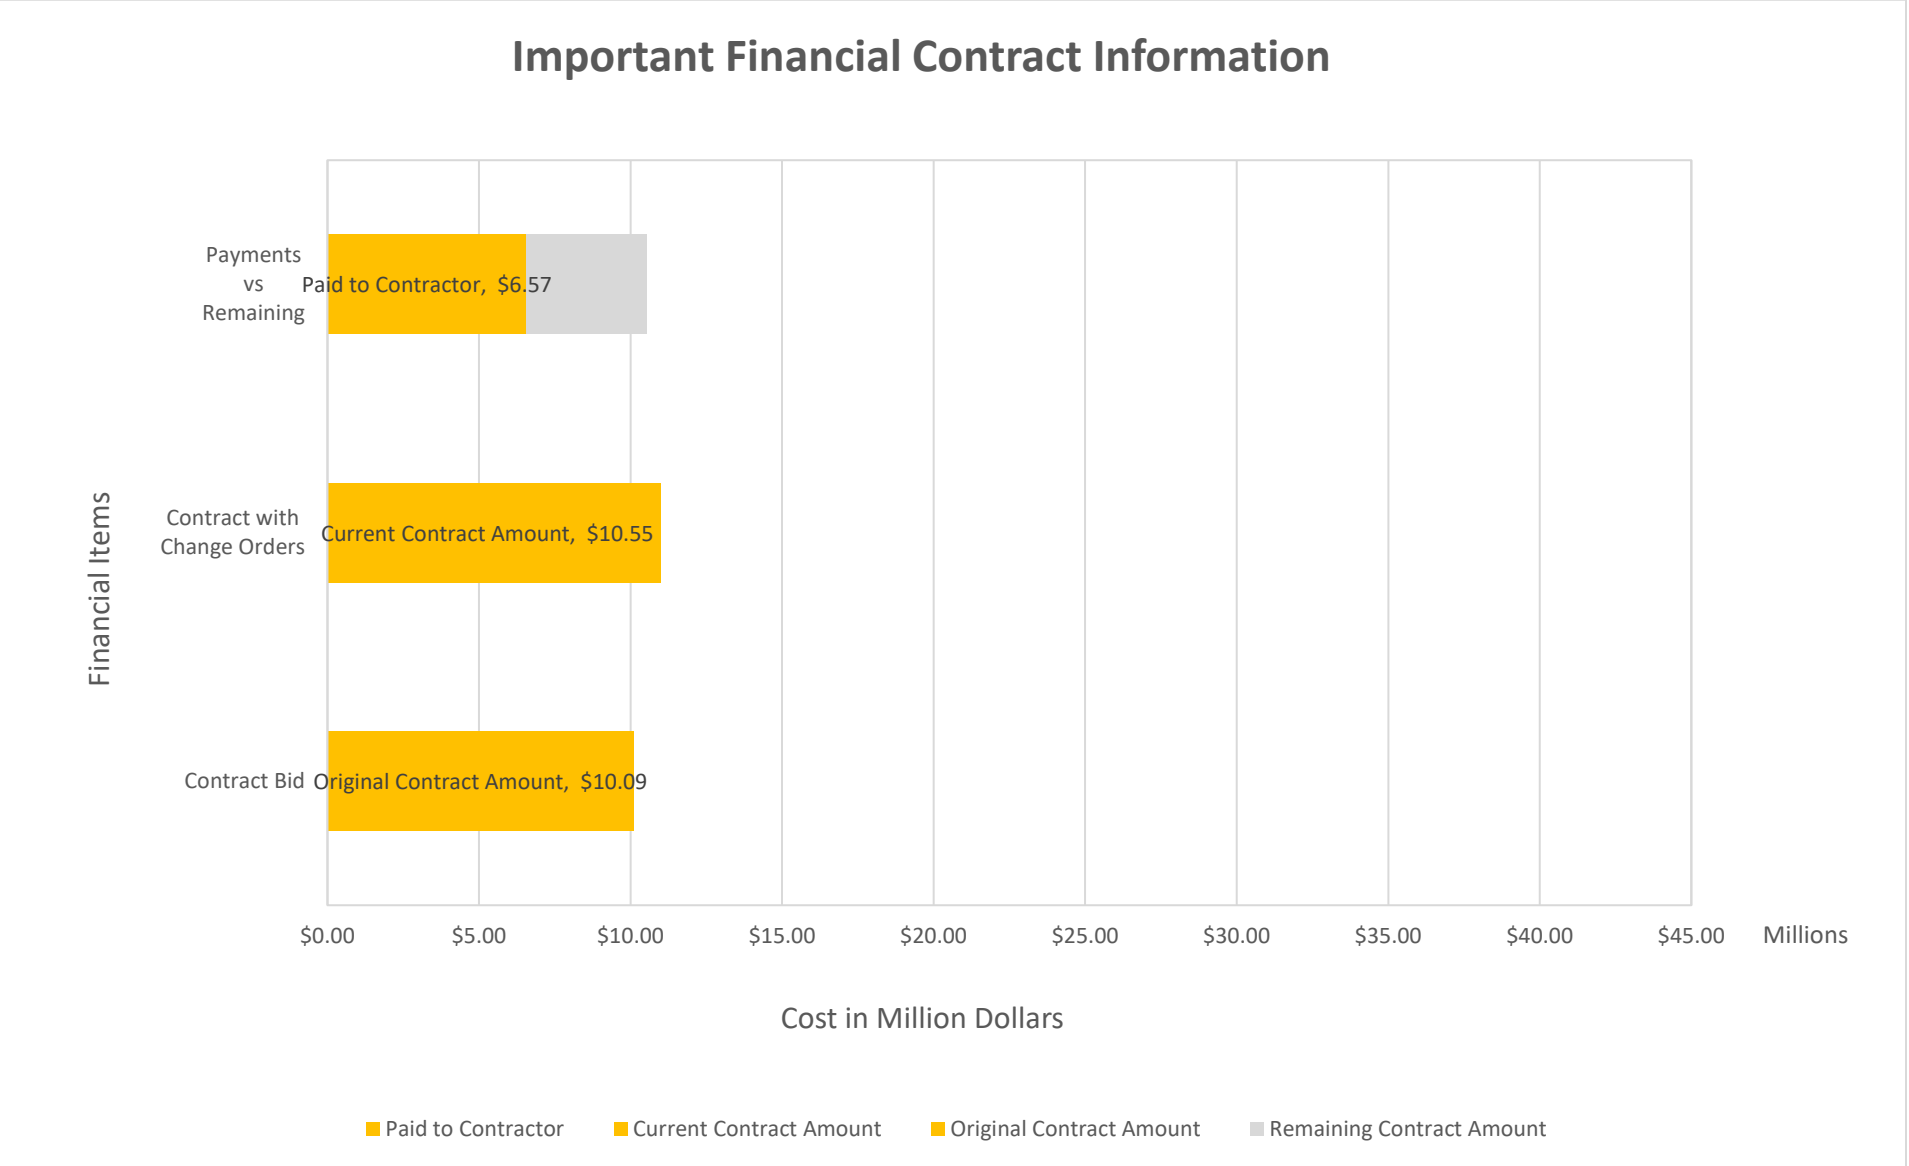


Initial Contract Value: \$10.09 Million
Payments to date: \$6.57 Million, Payments remaining \$3.98 Million
Current Contract Value: \$10.55 Million, Total Change Orders to Date: (\$0.46) Million
Initial Contract Value: \$10.09 Million

Project Name: US 6D STR F-06-A Elk Creek - New Castle
Project Number: 24493, FBR 0063-066
Date: October, 2026 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

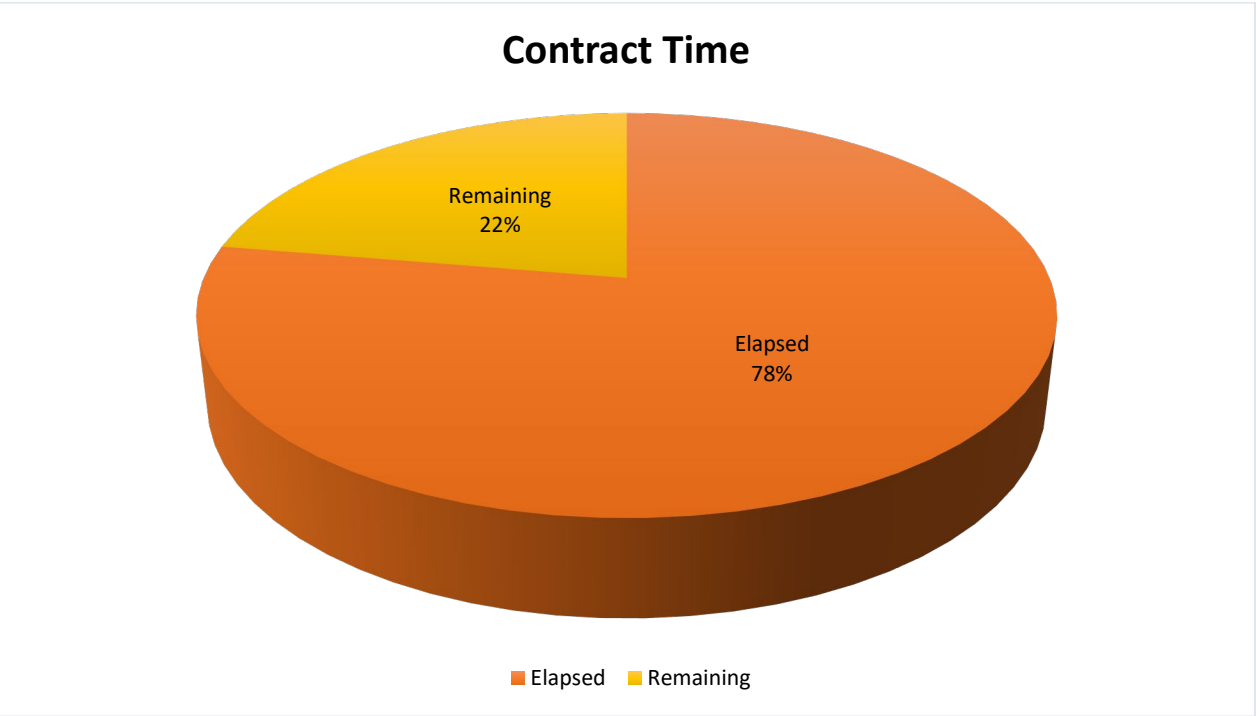

Total Contract time: 425 Calendar Days

Elapsed Contact time: 330 days, 78%

Contract Time Remaining: 95 days ,22%
