


## Status by Zone

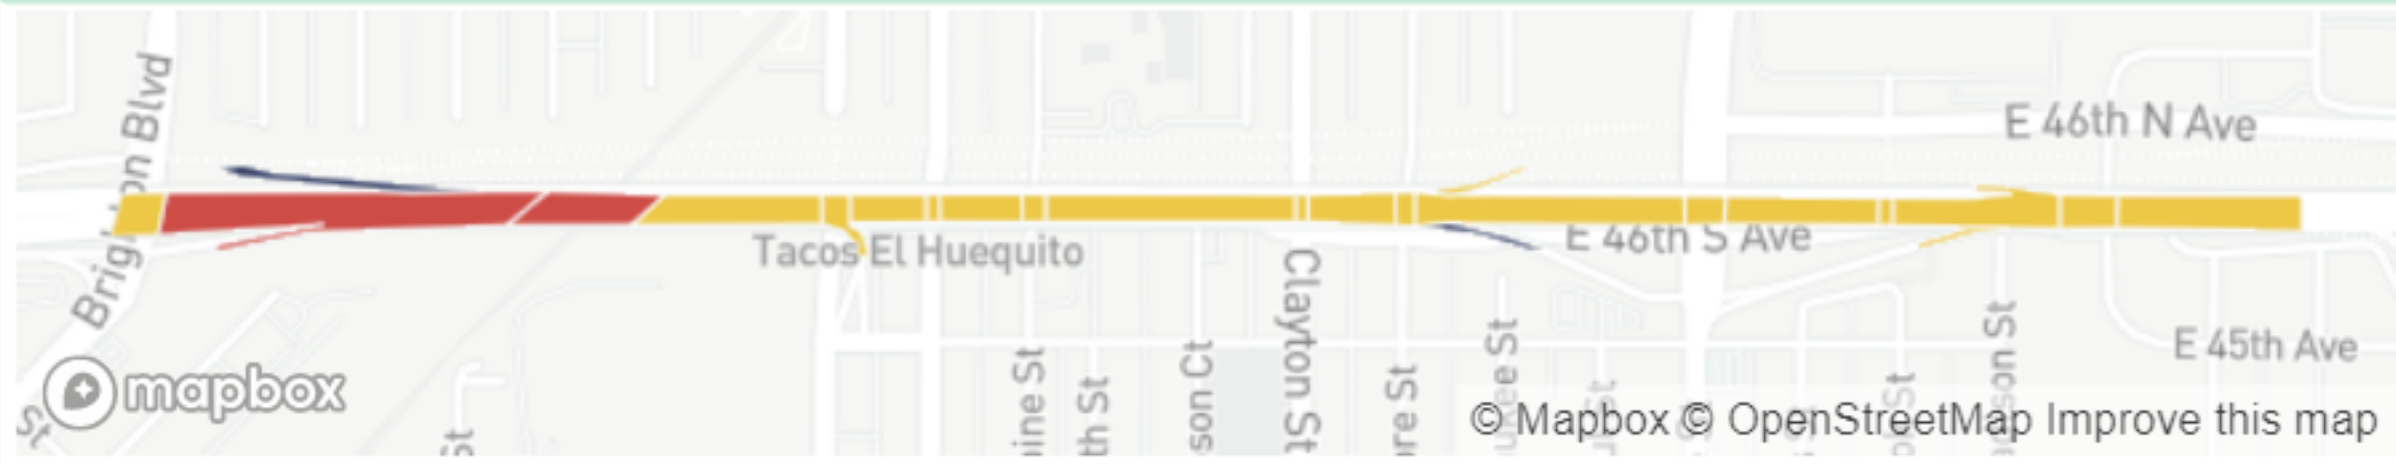

## Zone Details

Segment	Status	Work Start	Work Completion
01 - Over Brighton	Not Started	Jun 05, 2021	Jun 07, 2021
02 - WB Brighton Off Ramp	Completed		Aug 31, 2020
03 - UPRR to Brighton	In Progress	May 21, 2021	Jun 04, 2021
04 - Over UPRR	In Progress	May 24, 2021	Sep 24, 2021
05 - York to UPRR	Not Started	Jun 07, 2021	Jul 16, 2021
06 - Over York	Not Started	Jul 30, 2021	Aug 09, 2021
07 - Josephine to York	Not Started	Jul 21, 2021	Jul 30, 2021
08 - Over Josephine	Not Started	Jul 16, 2021	Jul 21, 2021
09 - Columbine to Josephine	Not Started	Jul 05, 2021	Jul 16, 2021
10 - Over Columbine	Not Started	Jun 30, 2021	Jul 05, 2021
11 - Clayton to Columbine	Not Started	Jun 04, 2021	Jun 30, 2021
12 - Over Clayton	Not Started	Jun 01, 2021	Jun 08, 2021
13 - Clayton to Fillmore	Not Started	Jun 04, 2021	Jun 18, 2021
14 - Over Fillmore	Not Started	Jun 18, 2021	Jun 24, 2021
15 - EB Steele Off Ramp	Not Started	Jun 12, 2021	Jun 14, 2021
16 - WB Steele On Ramp	Completed		Aug 31, 2020
17 - Fillmore to Steele	Not Started	Jun 24, 2021	Jul 23, 2021
18 - Over Steele	Not Started	Aug 09, 2021	Aug 18, 2021
19 - Steele to Cook	Not Started	Aug 18, 2021	Sep 01, 2021
20 - Over Cook	Not Started	Sep 01, 2021	Sep 06, 2021
21 - EB Steele On Ramp	Not Started	Jun 24, 2021	Jun 28, 2021
22 - Cook to BNSF	Not Started	Aug 13, 2021	Sep 02, 2021
23 - Over BNSF & Monroe	Not Started	Aug 03, 2021	Aug 13, 2021
24 - Monroe to Abutment	Not Started	Jul 23, 2021	Aug 03, 2021
