

Project Number: 24947/24527

Date: March 2025 Update

I-270 Critical Bridges Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

Final CAP
Proposals
Received:

TBD

Award of
Contract:
TBD

Notice To Proceed:

Begin Construction:

TBD

Final CAP Proposal Received: To Be Determined

Award of Contract: To Be Determined

Notice to Proceed: To Be Determined

Begin Construction: To Be Determined




Project Number: 24947/24527

Date: March 2025 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

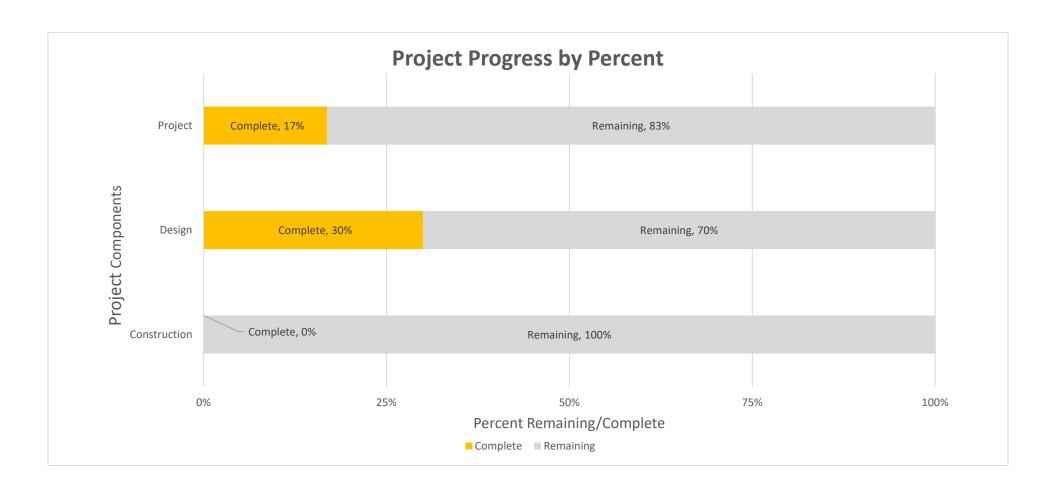

Overall Project: 17% Complete, 83% Remaining

Design: 30% Complete, 70% Remaining

Construction: 0% Complete, 100% Remaining



Project Number: 24947/24527

Date: March 2025 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract vale and change orders to date, and contract's bid amount.



Initial Pre-Construction Contracts Value: \$11.07 Million

Payments to date: \$6.19 Million, Payments remaining \$4.88 Million

Current Contracts Value: \$11.07 Million, Total Change Orders to Date: \$0

Initial Contracts Value: \$11.07 Million




Project Number: 24947/24527

Date: March 2025 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

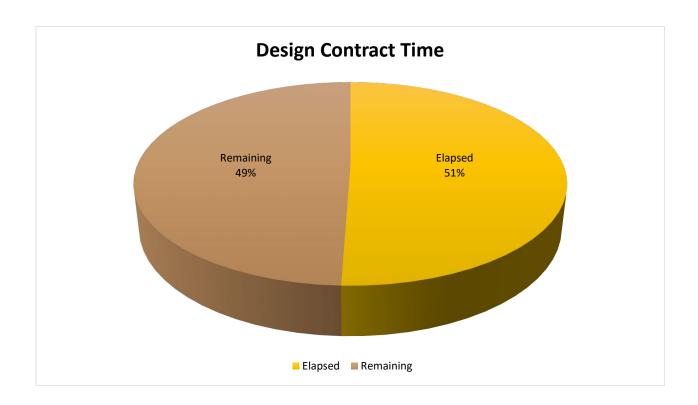

Total Contract time: 1410 Calendar Days

Elapsed Contact time: 713 days, 51%

Contract Time Remaining: 697 days ,49%
