

Project Number: 24947/24527

Date: July 2025 Update

## **I-270 Critical Bridges Project Dashboard**

This document provides monthly progress and financial updates on current CDOT projects.

## **Key Dates**

The following image shows the progression of the key project dates.

Final CAP
Proposals
Received:

TBD

Award of Notice To Begin
Contract: Proceed: Construction:
TBD TBD TBD

Final CAP Proposal Received: To Be Determined

Award of Contract: To Be Determined

Notice to Proceed: To Be Determined

Begin Construction: To Be Determined




Project Number: 24947/24527

Date: July 2025 Update

## **Project Progress by Percent**

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

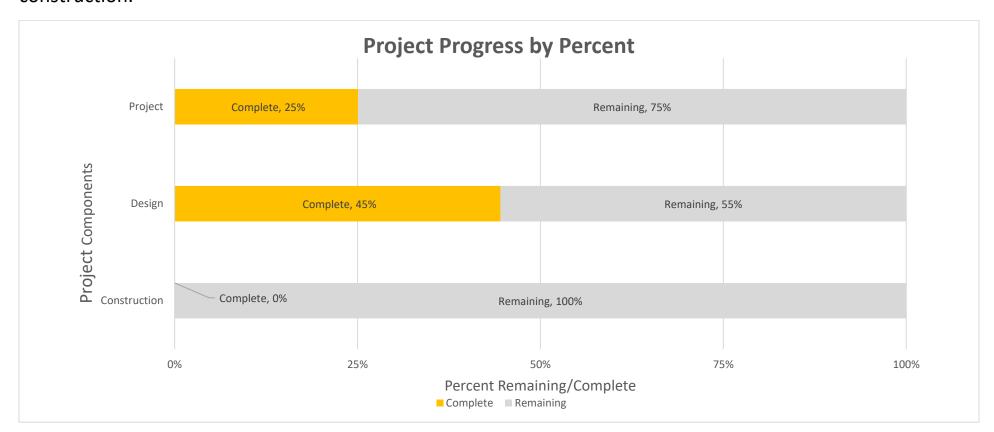

Overall Project: 25% Complete, 75% Remaining

Design: 45% Complete, 55% Remaining

Construction: 0% Complete, 100% Remaining




Project Number: 24947/24527

Date: July 2025 Update

# **Important Financial Contract Information**

The following Bar chart shows the projects payments vs remaining amount, total current contract vale and change orders to date, and contract's bid amount.

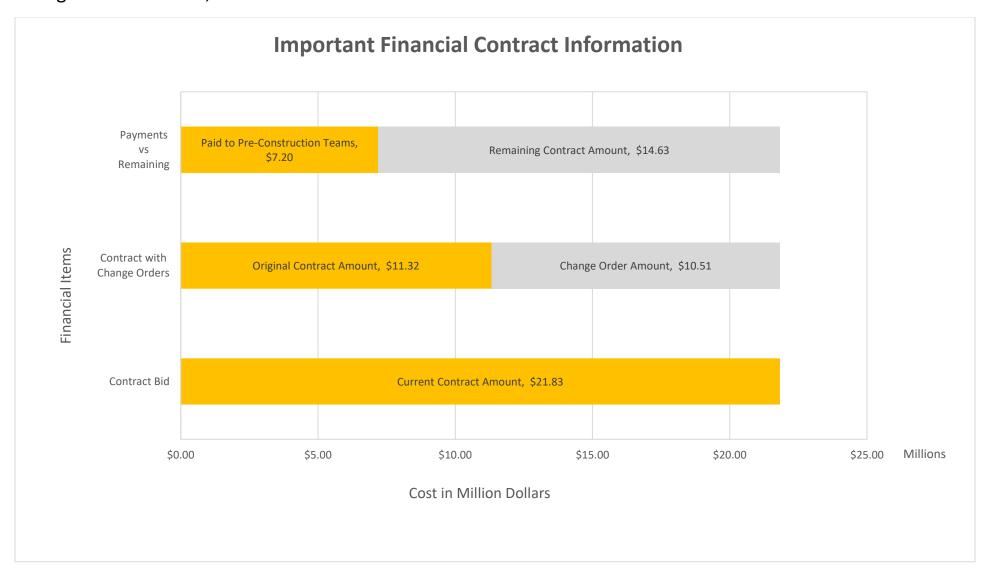

Payments to date: \$7.20 Million, Payments remaining \$14.63 Million

Initial Pre-Construction Contracts Value: \$11.32 Million

Current Contracts Value: \$21.83 Million, Total Change Orders to Date: \$10.51 Million




Project Number: 24947/24527

Date: July 2025 Update

### **Contract Time**

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

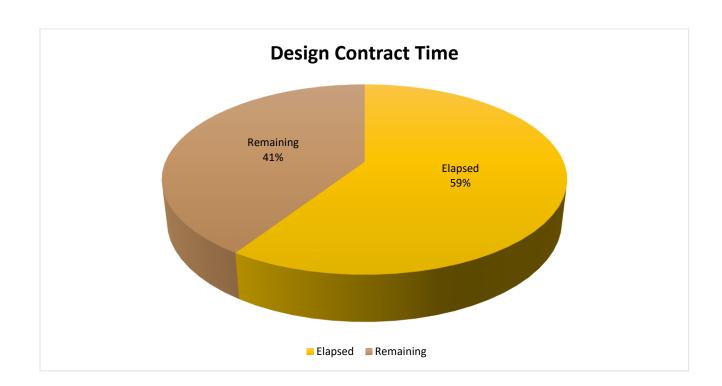

Total Contract time: 1410 Calendar Days

Elapsed Contact time: 835 days, 59%

Contract Time Remaining: 575 days, 41%
