


Project Name: I-270 Critical Bridges
Project Number: 24947/24527
Date: July 2026 Update

I-270 Critical Bridges Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

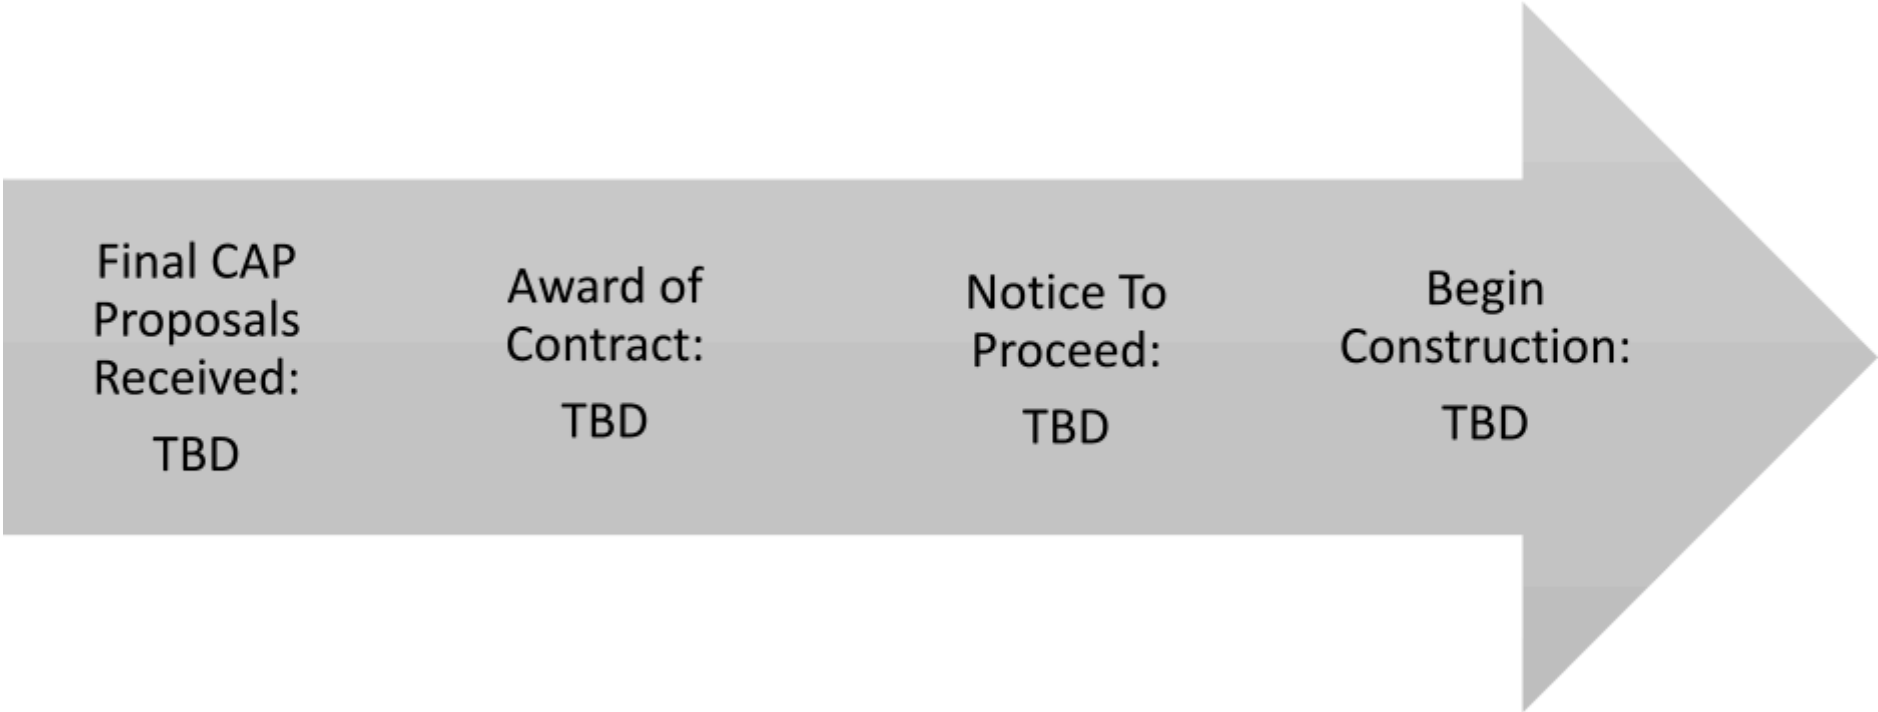


Final CAP Proposal Received: To Be Determined
Award of Contract: To Be Determined
Notice to Proceed: To Be Determined
Begin Construction: To Be Determined

Project Name: I-270 Critical Bridges
Project Number: 24947/24527
Date: July 2026 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

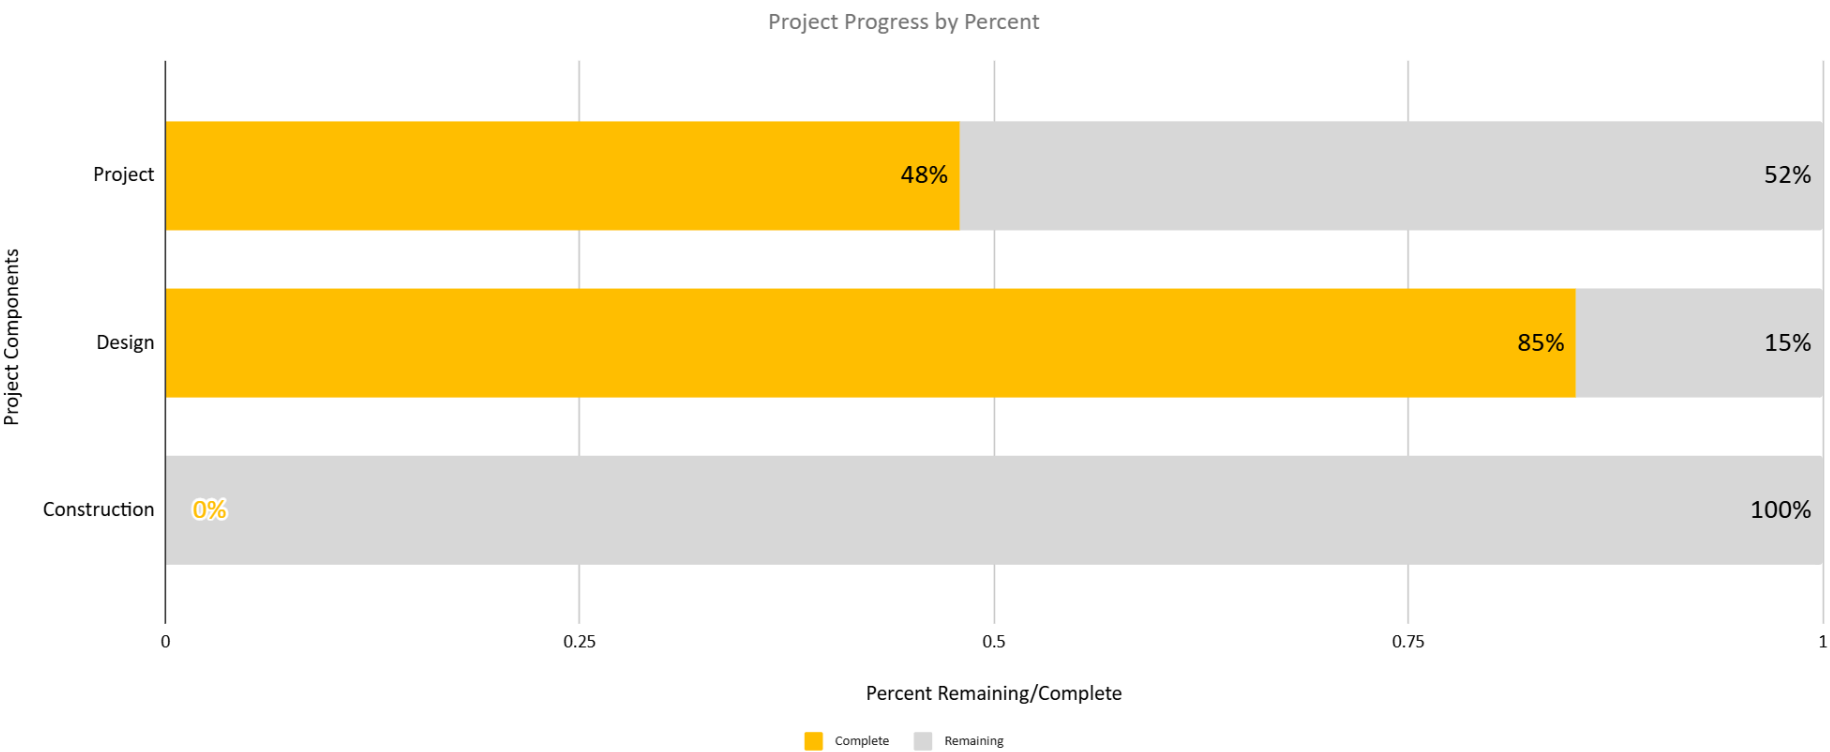


Overall Project: 48% Complete, 52% Remaining
Design: 85% Complete, 15% Remaining
Construction: 0% Complete, 100% Remaining

Project Name: I-270 Critical Bridges
Project Number: 24947/24527
Date: July 2026 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

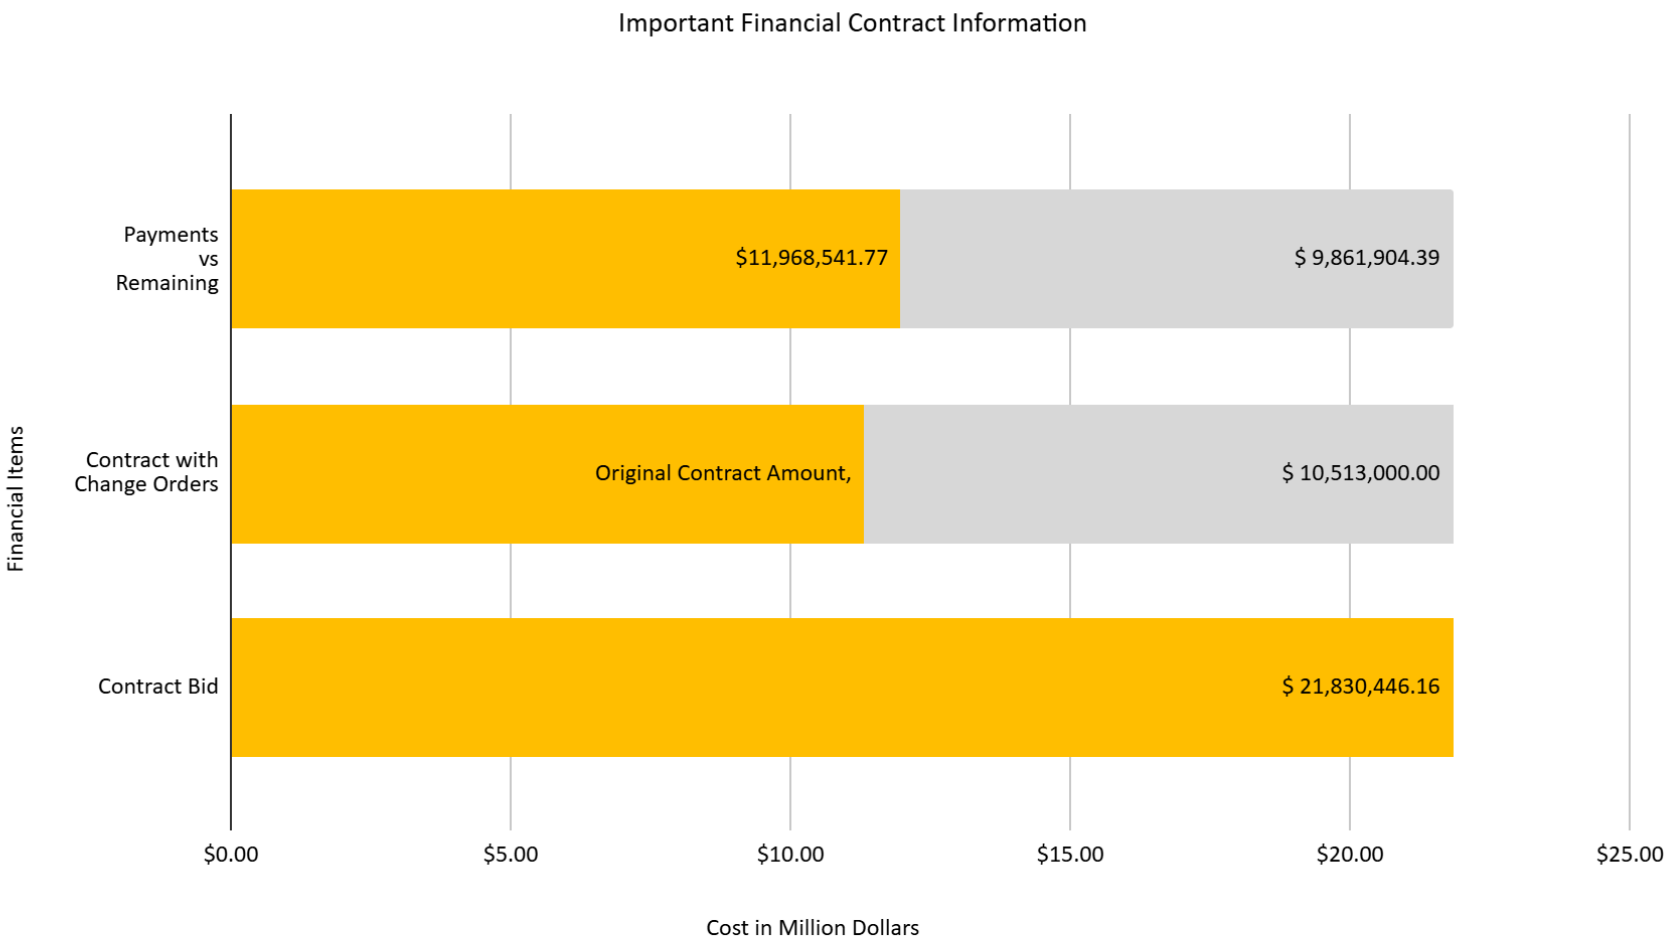


Payments to date: \$11.97 Million, Payments remaining: \$9.86 Million
Initial Pre-Construction Contract’s Value: \$10.51 Million
Current Contract’s Value: \$21.83 Million, Total Change Orders to Date: \$10.51 Million

Project Name: I-270 Critical Bridges
Project Number: 24947/24527
Date: July 2026 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

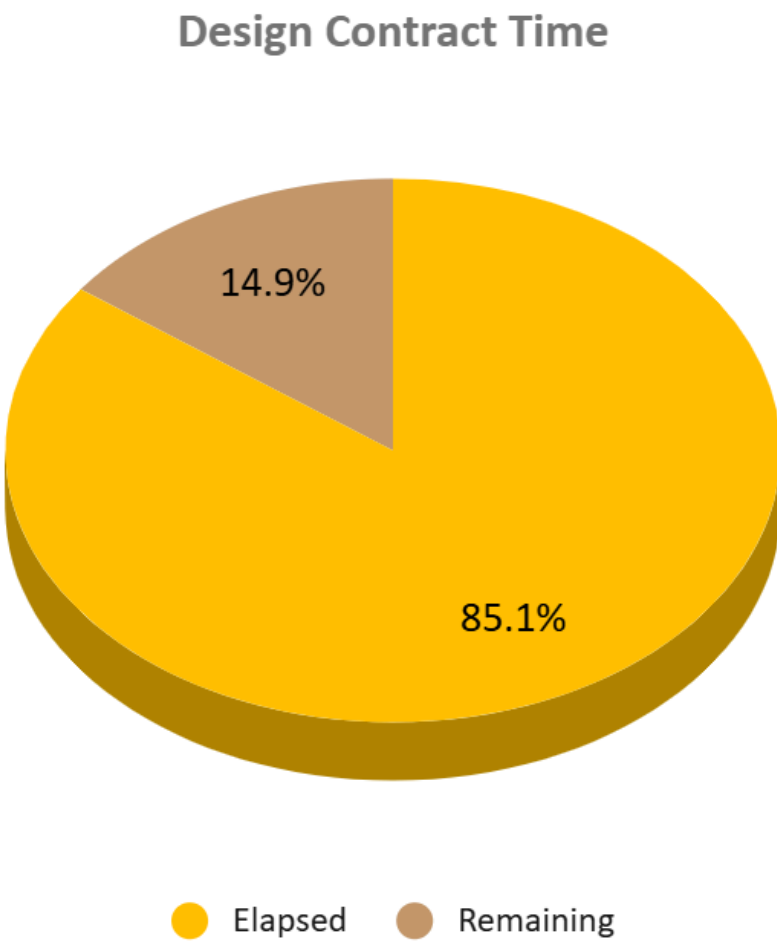

Total Contract time: 1410 Calendar Days
Elapsed Contract time: 1200 days, 85.1%
Contract Time Remaining: 210 days, 14.9%
