

Project Name: I-270 Critical Bridges

Project Number: 24947/24527


Date: March 2026 Update

I-270 Critical Bridges Project Dashboard

This document provides monthly progress and financial updates on current CDOT projects.

Key Dates

The following image shows the progression of the key project dates.

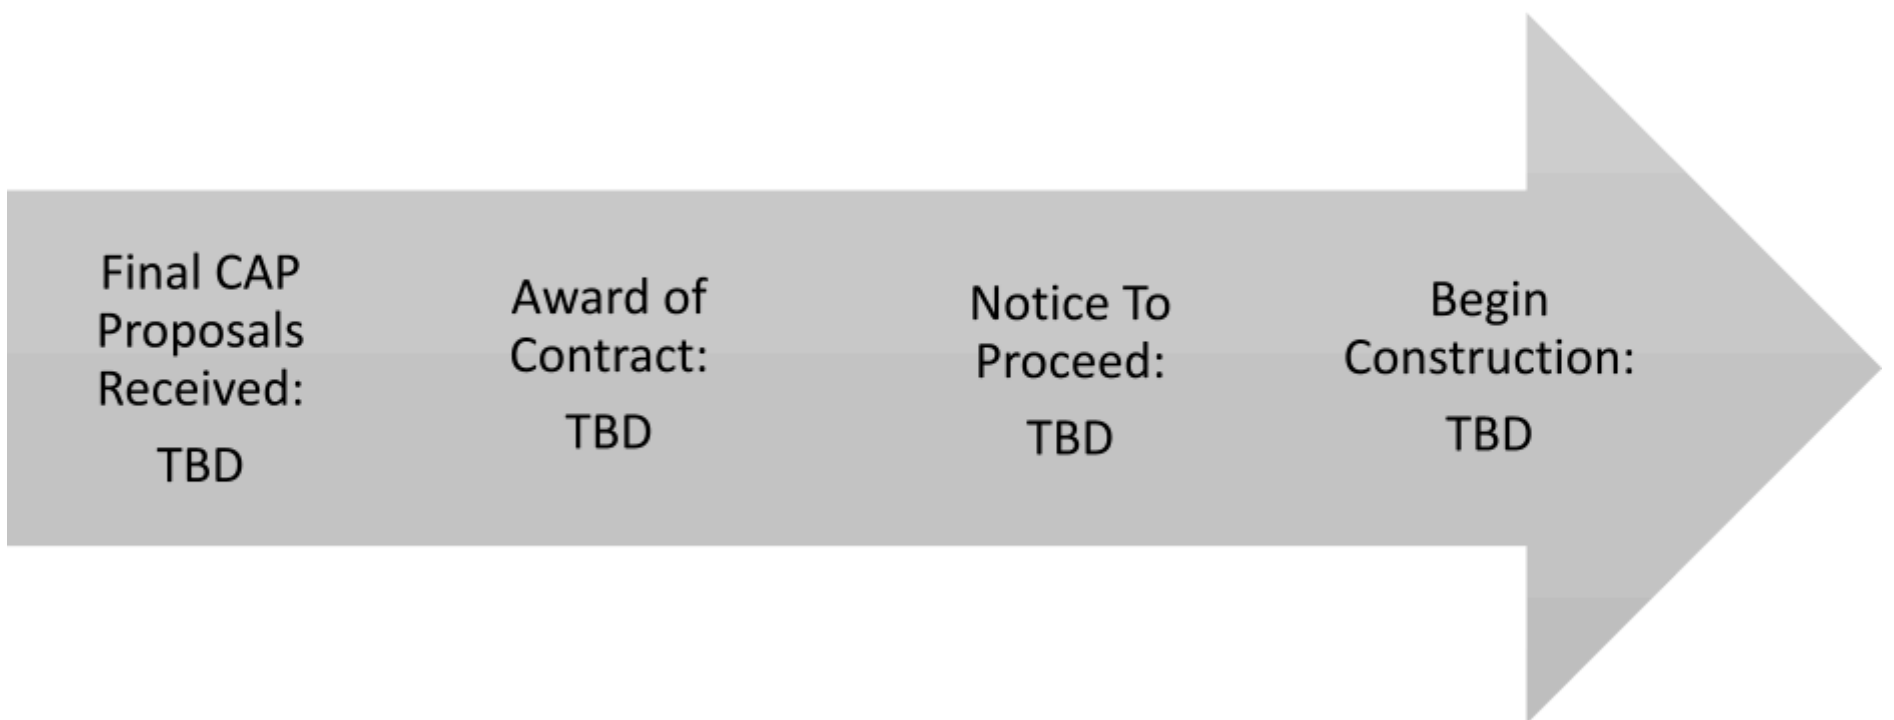

Final CAP Proposal Received: To Be Determined

Award of Contract: To Be Determined

Notice to Proceed: To Be Determined

Begin Construction: To Be Determined




Project Name: I-270 Critical Bridges

Project Number: 24947/24527

Date: March 2026 Update

Project Progress by Percent

The following Bar chart shows the percent complete and remaining for the overall project, design, and construction.

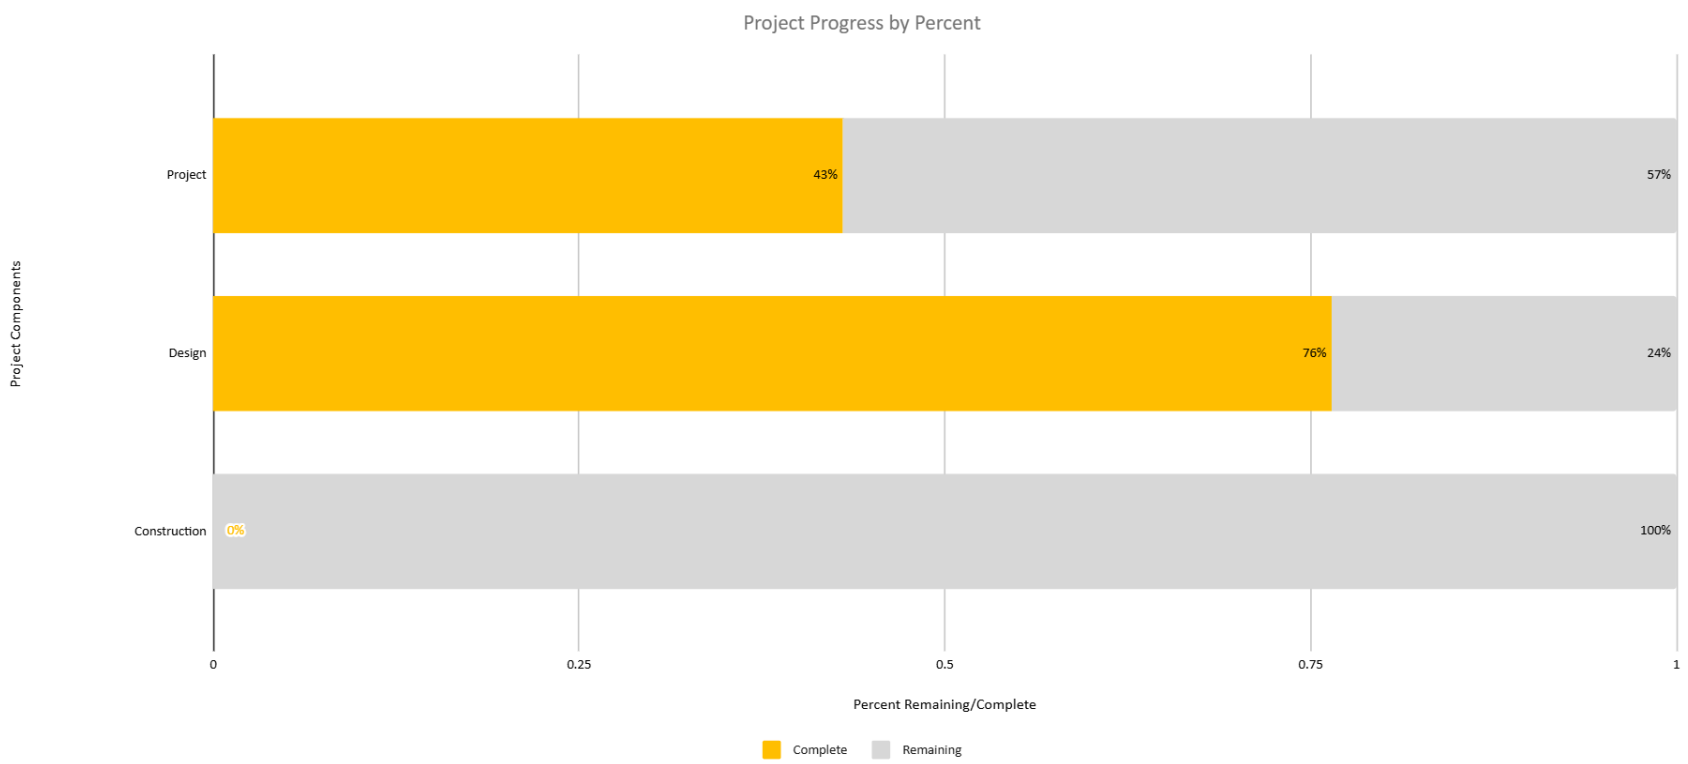

Overall Project: 43% Complete, 57% Remaining

Design: 76% Complete, 24% Remaining

Construction: 0% Complete, 100% Remaining




Project Name: I-270 Critical Bridges

Project Number: 24947/24527

Date: March 2026 Update

Important Financial Contract Information

The following Bar chart shows the projects payments vs remaining amount, total current contract value and change orders to date, and contract’s bid amount.

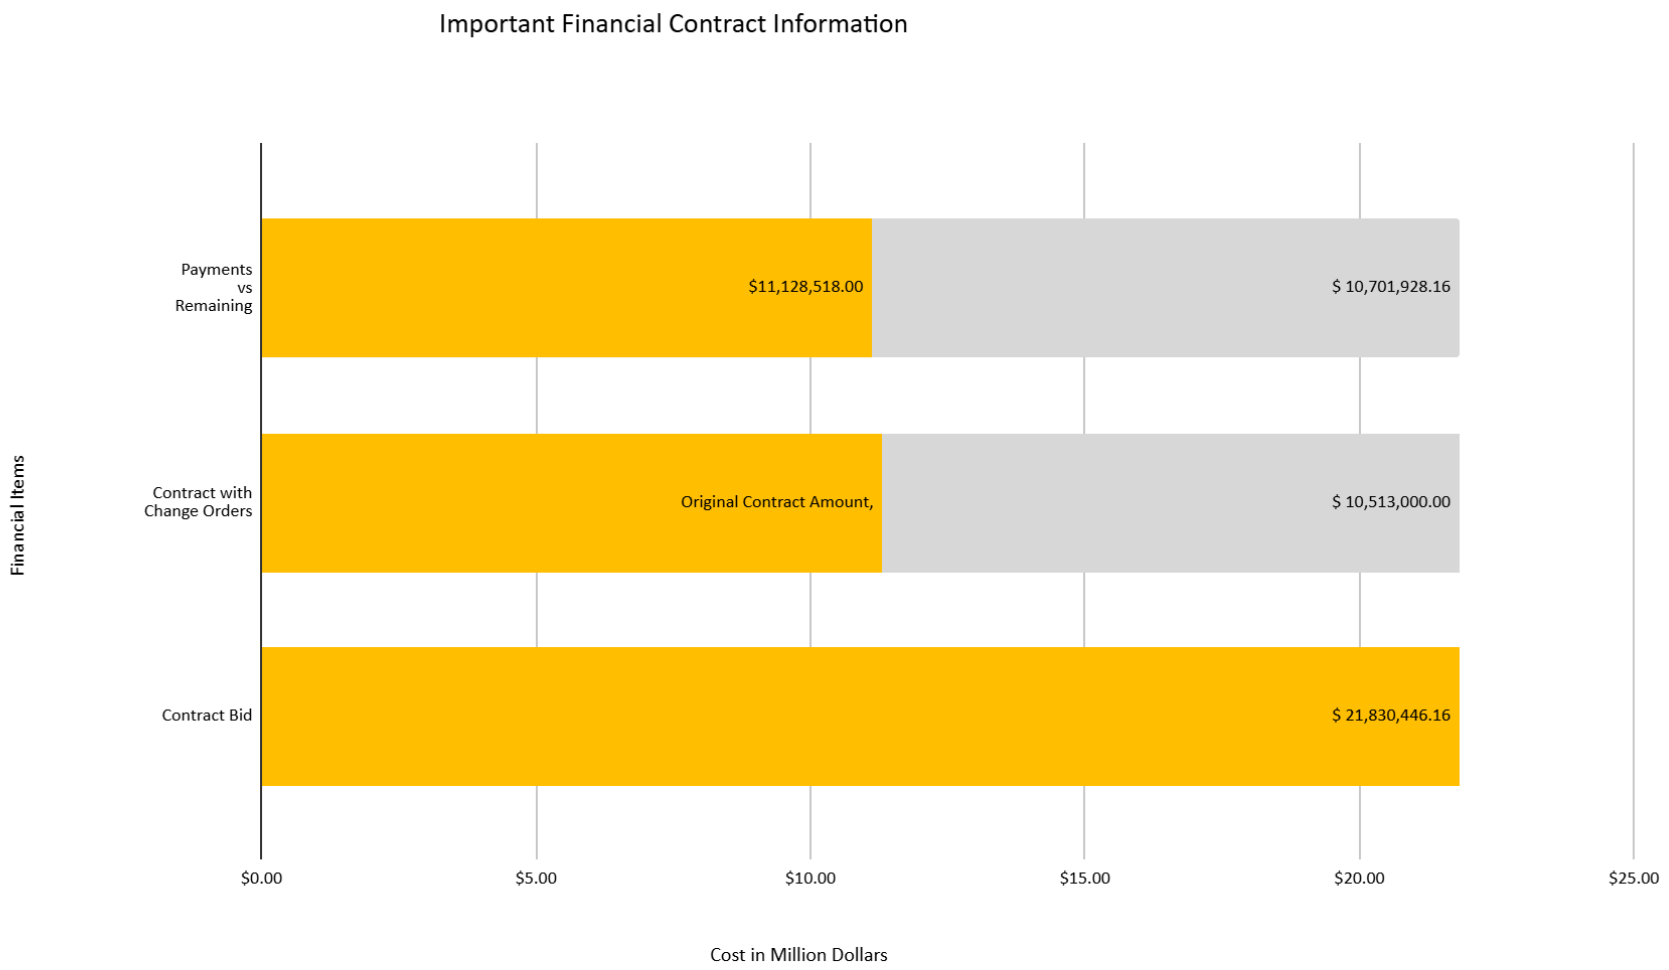

Payments to date: \$11.13 Million, Payments remaining: \$10.70 Million

Initial Pre-Construction Contract’s Value: \$10.51 Million

Current Contract’s Value: \$21.83 Million, Total Change Orders to Date: \$10.51 Million



Project Name: I-270 Critical Bridges


Project Number: 24947/24527

Date: March 2026 Update

Contract Time

The following pie chart shows total contract time, contract elapsed time, and contract remaining time.

Design Contract Time

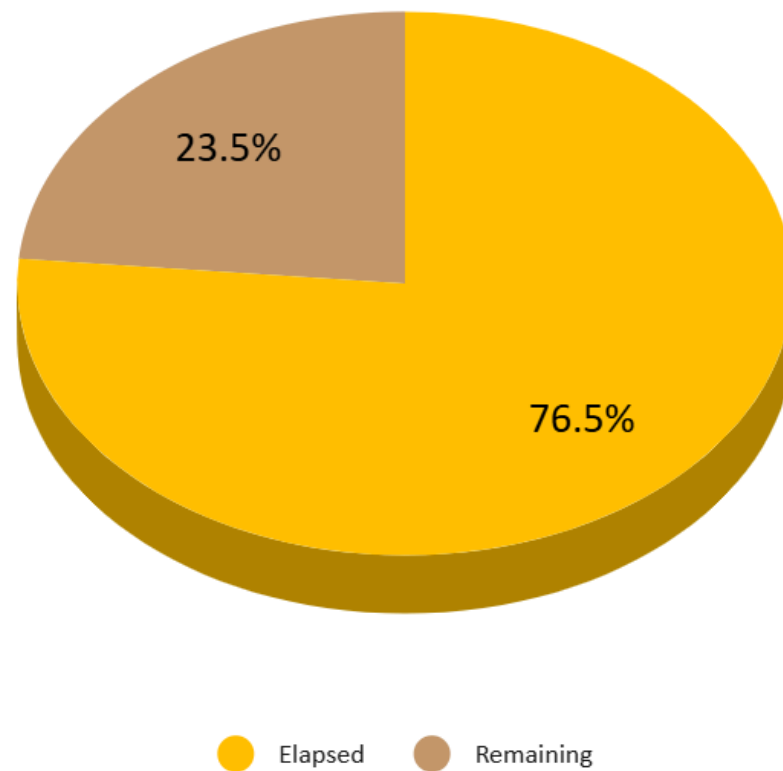

Total Contract time: 1410 Calendar Days

Elapsed Contract time: 1078 days, 76.5%

Contract Time Remaining: 332 days, 23.5%
