

**TRAFFIC DESIGN MEMORANDUM
PROJECT 23558/23559
M-21-I: US 350
OTERO COUNTY, COLORADO**

Submittal: December 15, 2020

Prepared for:



Colorado Department of Transportation – Region 2
5615 Wills Blvd.
Pueblo, CO 81008

Prepared by:



Stanley Consultants, Inc.
8000 S Chester Street, Ste. 500
Centennial, CO 80112
Phone (303) 799-6806
Fax (303) 799-8107

Project Description

The CDOT Region 2 Bridge Bundle Design Build Project consists of the replacement of a total of nineteen (19) structures bundled together as a single project. These structures are rural bridges on essential highway corridors (US 350, US 24, CO 239 and CO 9) in southeastern and central Colorado. These key corridors provide rural mobility, intra- and interstate commerce, movement of agricultural products and supplies, and access to tourist destinations. The design build project consists of seventeen (17) bridges and two (2) Additionally Requested Elements (AREs) structures.

The fourteen (14) of the structures in this design build project are jointly funded by the USDOT FHWA Competitive Highway Bridge Program grant and the Colorado Bridge Enterprise (Project No. 23558). The remaining five (5) structures are funded solely by the Colorado Bridge Enterprise (Project No. 23559). These projects are combined to form one design-build project. The two ARE structures are part of the five bridges funded by the Colorado Bridge Enterprise.

The nineteen bridges identified to be included in the 'Region 2 Bridge Bundle' were selected based on similarities in the bridge conditions, risk factors, site characteristics, and probable replacement type, with the goal of achieving economy of scale. Seventeen of the bridges being replaced are at least 80 years old. Five of the bridges are Load Restricted, limiting trucking routes through major sections of the US 24 and US 350 corridors. The bundle is comprised of nine timber bridges, four concrete box culverts, one corrugated metal pipe (CMP), four concrete I-beam bridges, and one I-beam bridge with corrugated metal deck.

Project Site

Structure M-21-I is at US 350 milepost 56.454 in Otero County, Colorado, and crosses a seasonal wash. Categorized as a R-B Rural Highway in the CDOT State Highway Access Code, US 350 traverses rolling terrain with a 65 mph posted speed limit. In the area of the structure, the highway is approximately 28 feet wide, with two 11-foot lanes and no separation of opposing traffic. US 350 is also a Colorado Scenic & Historic Byway known as the Santa Fe Trail. **Figure 1** shows the project area.

Traffic Data

This segment of US 350 has a 2020 Annual Average Daily Traffic (AADT) of 500 vehicles per day, and a projected 2040 AADT of 781 vehicles per day, according to CDOT's Online Transportation Information Systems (OTIS). Of these daily traffic volumes, 18% are heavy vehicles. This roadway has the capacity to accommodate 2,250 vehicles every hour, resulting in a volume to capacity ratio of 0.03. In the year 2040, the volume to capacity ratio results in 0.05.

No crashes were recorded in the vicinity of the structure location (mileposts 56.00 to 57.00) between January 1, 2015 and December 31, 2019, therefore no crashes occurred at structure location. No pattern of crash history can be derived from the data available and therefore no specific design modifications are concluded.

Construction Phasing Alternatives

Three construction phasing alternatives have been identified to complete the construction of the proposed replacement structure.

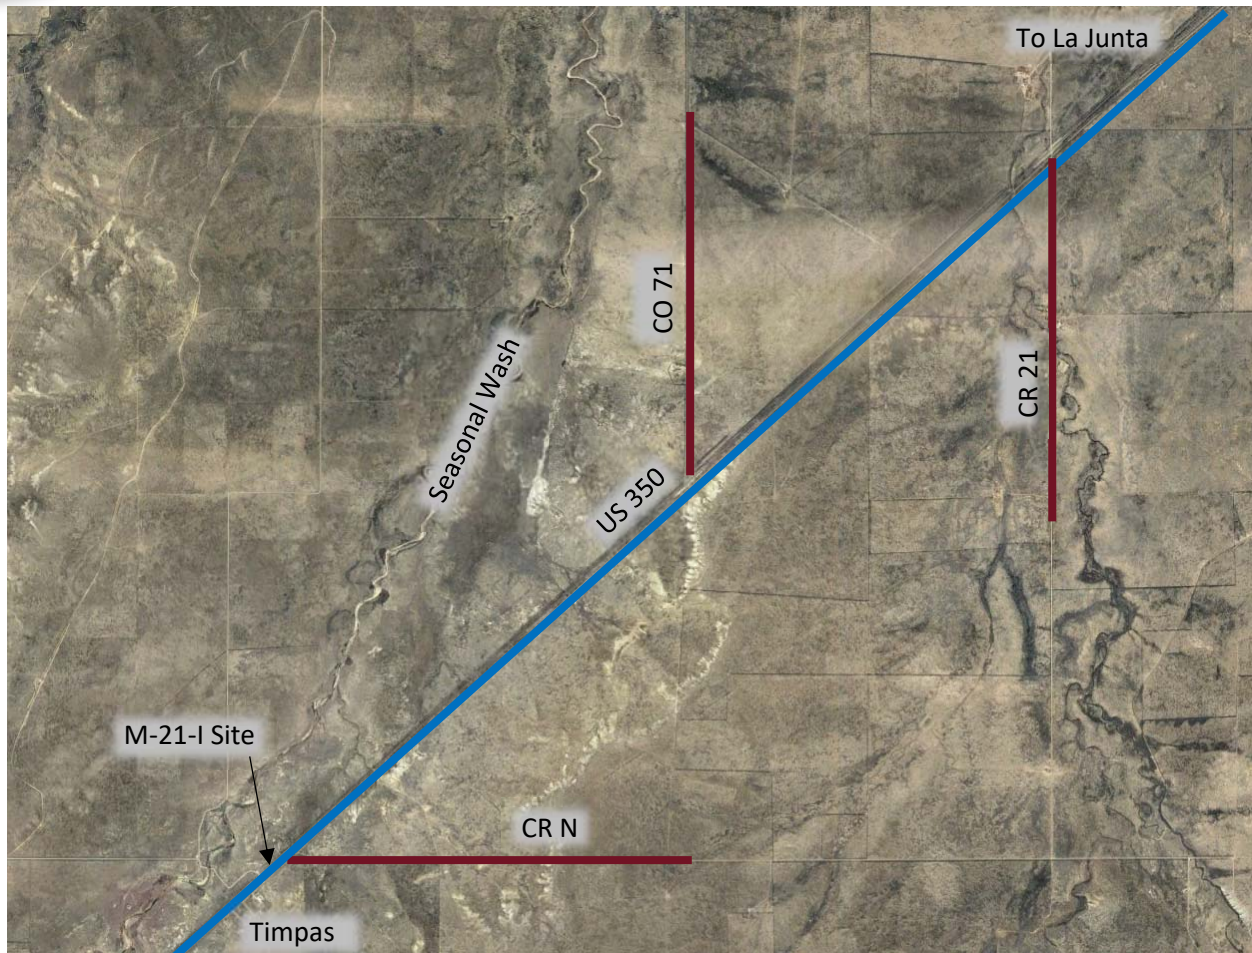


Figure 1: Vicinity Map

Complete Closure with Detour Route

The grant application states that the roadway should not be closed during construction due to lengths of the detour routes. A complete closure of this structure location is not practical as there is no ideal detour route to maintain traffic operations, as the structure is located just south of the intersection of County N.

Single Lane – Two Way Traffic Operations

Phasing the construction to accommodate a single lane of traffic operations along the route at all times should be studied further by a structural engineer retained by the Contractor. Preliminary structural analysis has determined that a phased approach to construction should be avoided out of concern for the structural integrity and maintaining traffic operations on the manipulated bridge.

Shoofly

A shoofly has been evaluated at this structure location. With an abundance of available right-of-way to the north, a two-lane shoofly can be accommodated with minimal impacts to the area terrain, with few obstructions to consider. Anticipated conflicts with utility poles shall be the Contractor's responsibility to coordinate with the appropriate utility companies to determine appropriate mitigation. The shoofly would provide the least impacts to traffic operations, maintain a 45 mph posted speed limit, and be entirely within the owner's right-of-way. Standards and guidance from Typical Application 7 of the Manual on Uniform Traffic Control Devices shall be followed. The minimum criteria within the construction zone are

11-foot lanes with two-foot shoulders on both sides. **Figure 2** illustrates the shoofly typical section, and **Figure 3** found at the end of the memorandum illustrates the shoofly plan.

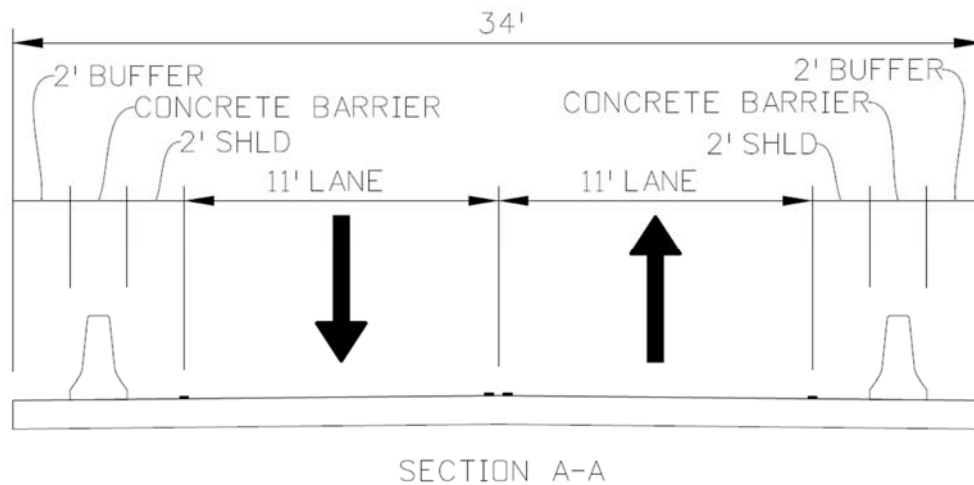


Figure 2: Shoofly Typical Section

Conclusions:

The recommended traffic control at this structure location, is a shoofly operation. There are no practical or effective area detour routes to consider. In addition, preliminary analysis indicates traffic operations should not be maintained on a manipulated timber structure being deconstructed, without further analysis by the Contractor. Consequently, the preferred handling of traffic is recommended by way of a two-lane shoofly.

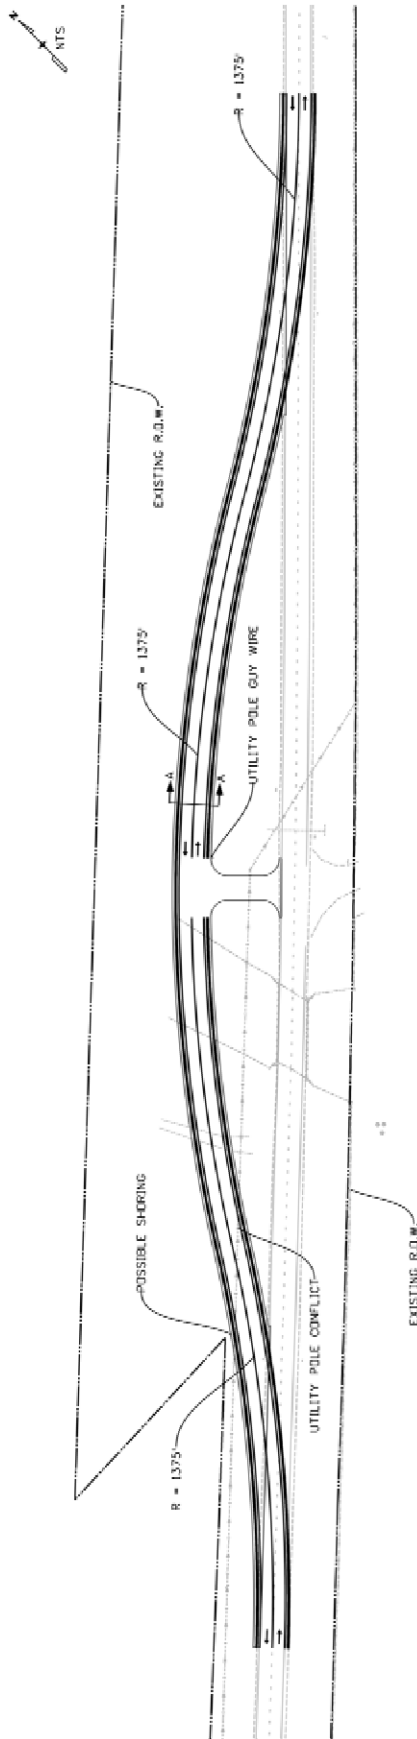


Figure 3: Shoofly
