

**DRAFT - TRAFFIC DESIGN MEMORANDUM  
PROJECT 23558/23559  
J-14-C: CO 9  
PARK COUNTY, COLORADO**

Submittal: January 29, 2021

*Prepared for:*



Colorado Department of Transportation – Region 2  
5615 Wills Blvd.  
Pueblo, CO 81008

*Prepared by:*



Stanley Consultants, Inc.  
8000 S Chester Street, Ste. 500  
Centennial, CO 80112  
Phone (303) 799-6806  
Fax (303) 799-8107

## Project Description

The CDOT Region 2 Bridge Bundle Design Build Project consists of the replacement of a total of nineteen (19) structures bundled together as a single project. These structures are rural bridges on essential highway corridors (US 350, US 24, CO 239 and CO 9) in southeastern and central Colorado. These key corridors provide rural mobility, intra- and interstate commerce, movement of agricultural products and supplies, and access to tourist destinations. The design build project consists of seventeen (17) bridges and two (2) Additionally Requested Elements (AREs) structures.

The fourteen (14) of the structures in this design build project are jointly funded by the USDOT FHWA Competitive Highway Bridge Program grant and the Colorado Bridge Enterprise (Project No. 23558). The remaining five (5) structures are funded solely by the Colorado Bridge Enterprise (Project No. 23559). These projects are combined to form one design-build project. The two ARE structures are part of the five bridges funded by the Colorado Bridge Enterprise.

The nineteen bridges identified to be included in the 'Region 2 Bridge Bundle' were selected based on similarities in the bridge conditions, risk factors, site characteristics, and probable replacement type, with the goal of achieving economy of scale. Seventeen of the bridges being replaced are at least 80 years old. Five of the bridges are Load Restricted, limiting trucking routes through major sections of the US 24 and US 350 corridors. The bundle is comprised of nine timber bridges, four concrete box culverts, one corrugated metal pipe (CMP), four concrete I-beam bridges, and one I-beam bridge with corrugated metal deck.

## Project Site

Structure J-14-C is at CO 9 milepost 20.107 in Park County, Colorado, and crosses the Louis Gulch. Categorized as a R-B Rural Highway in the CDOT State Highway Access Code, CO 9 traverses rolling terrain with a 55 mph posted speed limit. In the area of the structure, the highway is approximately 25 feet wide, with two 11-foot lanes and no separation of opposing traffic. **Figure 1** shows the project area.

## Traffic Data

This segment of CO 9 has a 2020 Annual Average Daily Traffic (AADT) of 1,200 vehicles per day, and a projected 2040 AADT of 1,675 vehicles per day, according to CDOT's Online Transportation Information Systems (OTIS). Of these daily traffic volumes, 7.4% are heavy vehicles. This roadway has the capacity to accommodate 850 vehicles every hour, resulting in a volume to capacity ratio of 0.25. In the year 2040, the volume to capacity ratio results in 0.34.

A total of nine crashes were recorded in the vicinity of the structure location (mileposts 19.54 to 20.68) between January 1, 2015 and December 31, 2019. Five crashes occurred at the structure itself. Two crashes were caused by overturning due to the curve not meeting the 55 MPH design speed. This will be corrected by the new roadway alignment. In four instances, there was no apparent contributing factors to the crashes. No impairment was suspected in three of the crashes, while alcohol was report in the remaining two. There does not appear to be any pattern of crash type, contributing factors, or impairment of drivers. The lack of any crash related pattern results in no specific modified design features.

## Construction Phasing Alternatives

Three construction phasing alternatives have been identified to complete the construction of the proposed replacement structure.



**Figure 1: Vicinity Map**


#### Complete Closure with Detour Route

The grant application states that the roadway should not be closed during construction due to the lengths of the detour routes. A complete closure of this structure location is not practical as the ideal detour route would require major improvements to maintain traffic operations including the over 7% of heavy vehicles.

#### Single Lane – Two Way Traffic Operations

Phasing the construction to accommodate a single lane of traffic operations along the route at all times appears to be feasible at this structure location. CDOT's Region 2 Lane Closure Strategy allows for a single lane closure at all hours of the day at this structure location, so long as the lane closure does not exceed  $\frac{1}{4}$  mile. Construction at this location may exceed  $\frac{1}{4}$  mile in which a variance may be necessary. Structure J-14-C is currently a two-lane timber structure. Preliminary structural and hydraulic analysis have determined that this structure may be replaced with a two-span bridge. In Phase 1, traffic will utilize the existing northbound/westbound lane for two-way operations. Construction of the proposed southbound traffic lane will be constructed while traffic is in this configuration. For Phase 2, traffic will move to the newly constructed southbound lane remaining in a two-way operation. The entire existing bridge will be removed at this time to allow for the construction of the remaining proposed bridge and northbound lane. **Figure 2** illustrates the phasing suggested to accommodate the alternative. By accommodating traffic operations in the current alignment, two-way traffic would utilize a single lane, likely by use of temporary traffic signals. Standards and guidance from Typical Application 12 of the Manual on Uniform Traffic Control Devices shall be followed. The use of temporary traffic signals must follow the 630 Traffic Signal (Portable) special provision. Preliminary traffic analysis indicates an acceptable level of service (LOS) of less than 55 seconds of delay (LOS D or better) on average, given the roadway traffic volumes, length between traffic signals, and speed limit. An acceptable level of service indicates the use of this alternative as feasible.

For the preliminary evaluation we are assuming the following variables: 1000-foot maximum distance between stop bars, speed limit of 40 mph, and a timing plan that uses a 45 second all red and enough green in each direction to clear the queue each cycle. The timing plan we are using for the evaluation is conservative to evaluate the worst-case scenario. The Contractor will be required to submit a traffic control plan to CDOT with a proposed timing plan for evaluation before implementation.

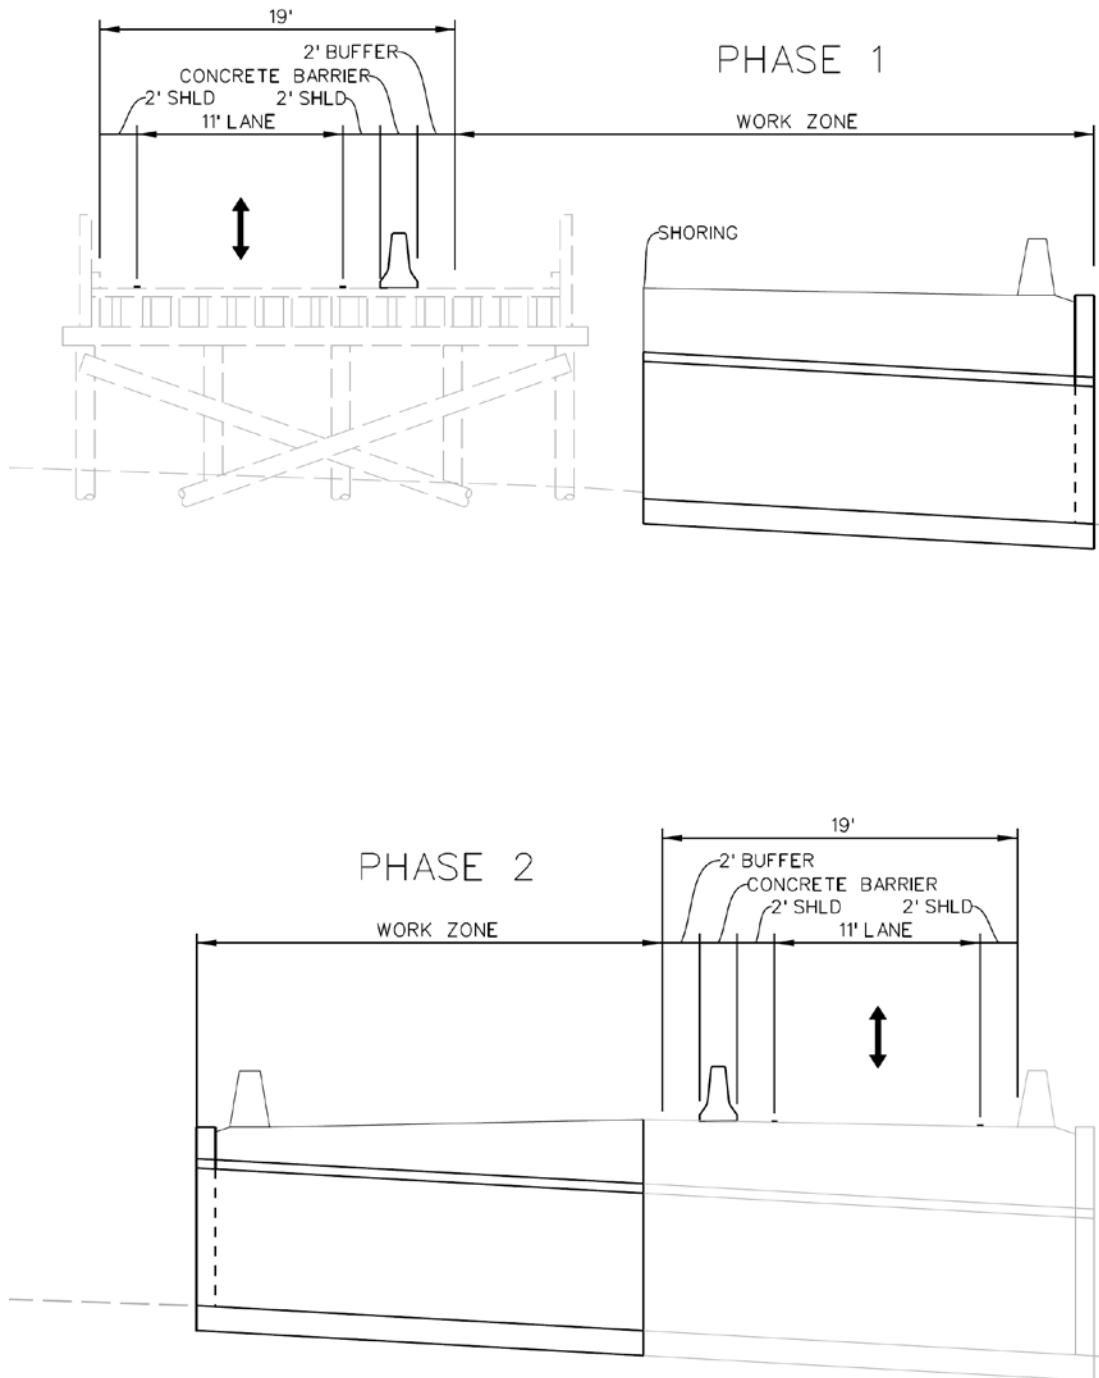

**Figure 2: Single Lane – Two Way Phasing**

### Shoofly

A shoofly alternative was evaluated at this structure location. The proposed alignment for all intentions acts as a shoofly, but in permanent form. A shoofly to the north to avoid construction activity is not practical given the mountainous terrain.

### **Conclusion:**

The recommended traffic control at this structure location, is a single lane, two-way operation. A variance for this operation may be required, but still remains the preferred alternative. Neither a detour route nor a shoofly is practical at this location. Geographical constraints eliminate a practical detour route, as well as opportunities to route traffic around the structure construction.
