COLORADO
Department of Transportation

North I-25 Segment 5: Mead to Berthoud (CO 66 to CO 56)
Delivery: CMGC

I. Project Dashboard

The purpose of this document is to provide a progress and financial update pertaining to the design and construction of the North I-25 Segment 5 Project and the following associated project numbers:


- **Design:** Project Number 24309
- **Construction Package 1:** Project Number 25986
- **Construction Package 2:** Project Number 25987
- **Construction Package 3:** Project Number 25988

II. Milestone Dates


Design




Construction Package 1

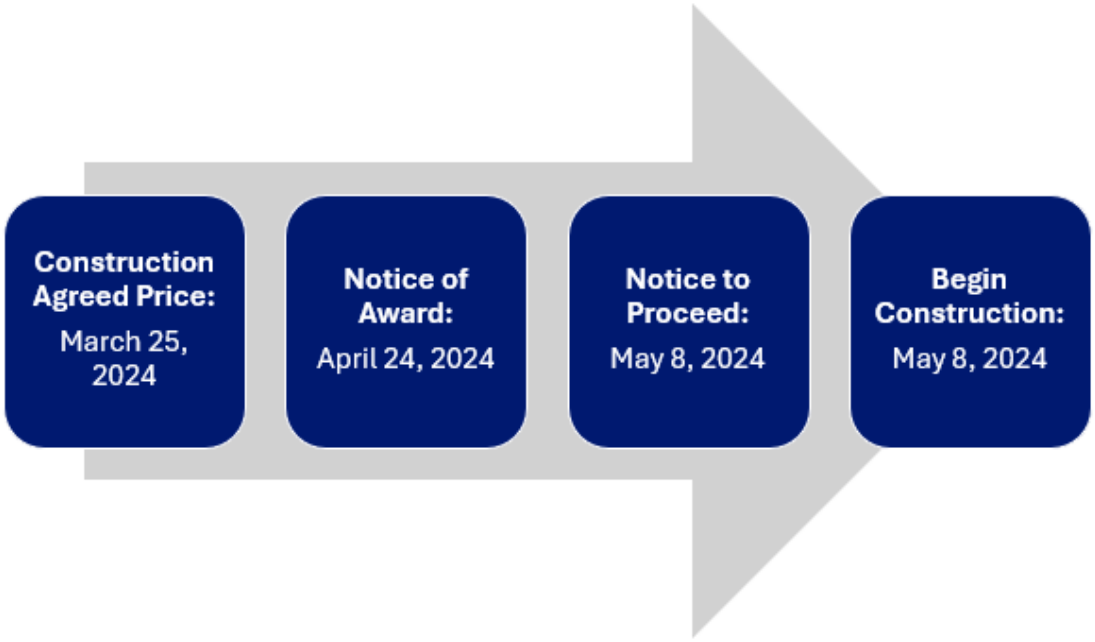


Construction Package 2

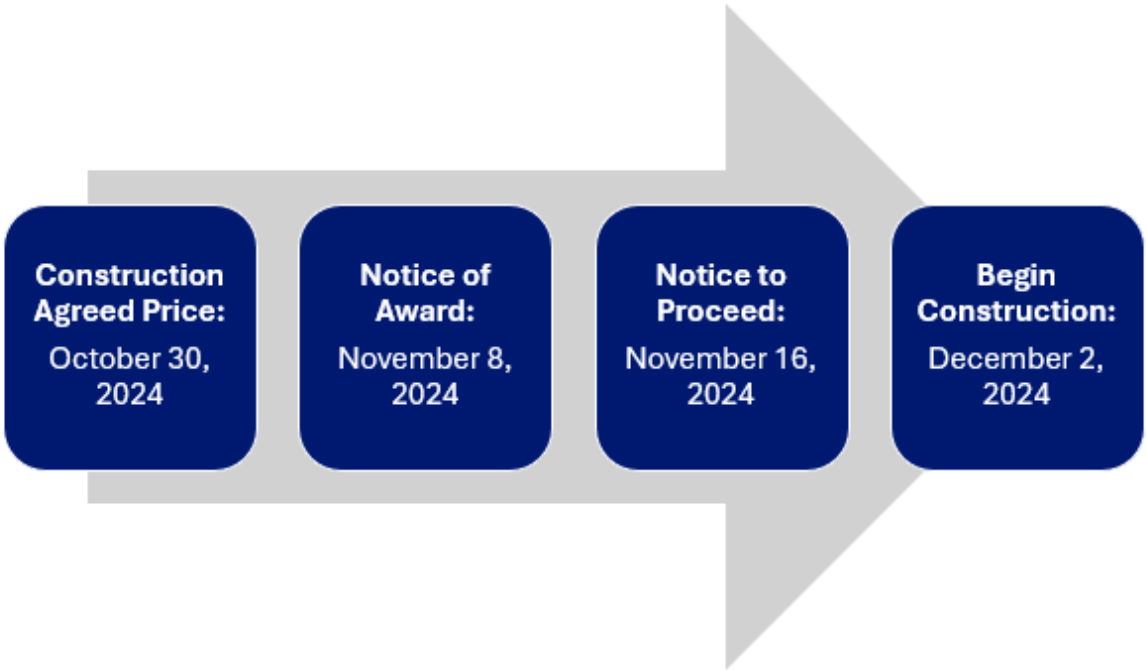

Construction Package 3

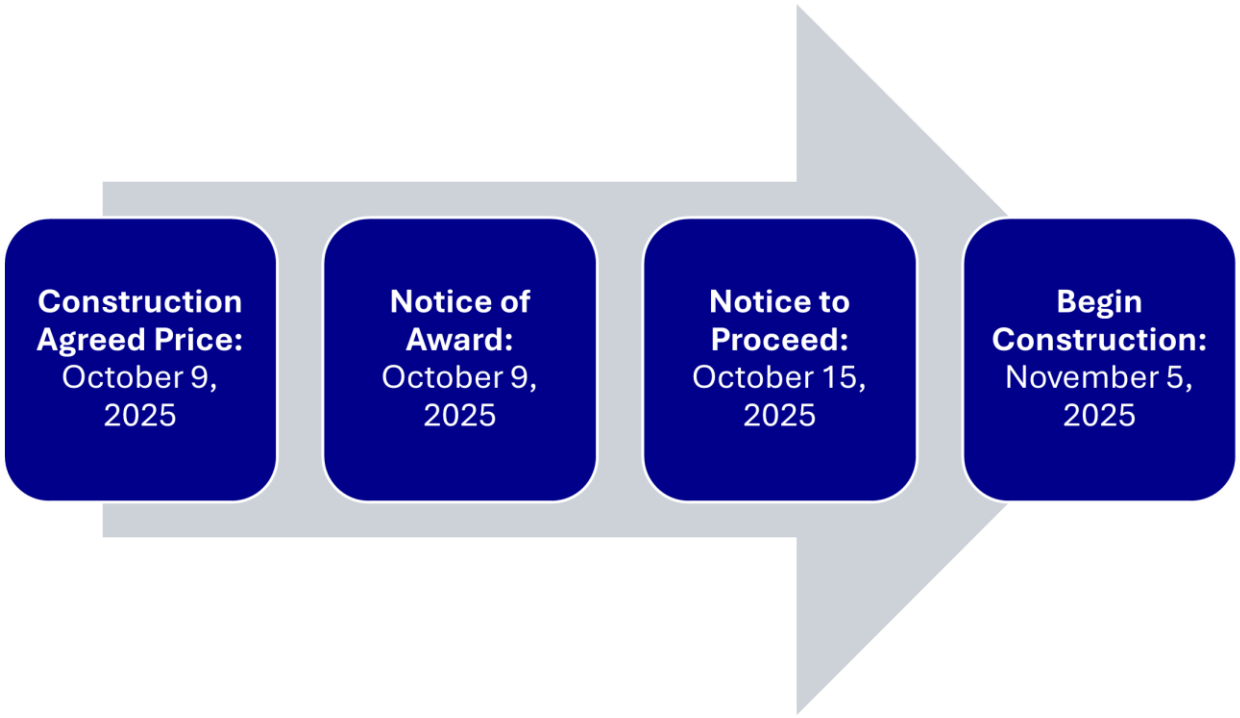


III. Project Progress by Percent

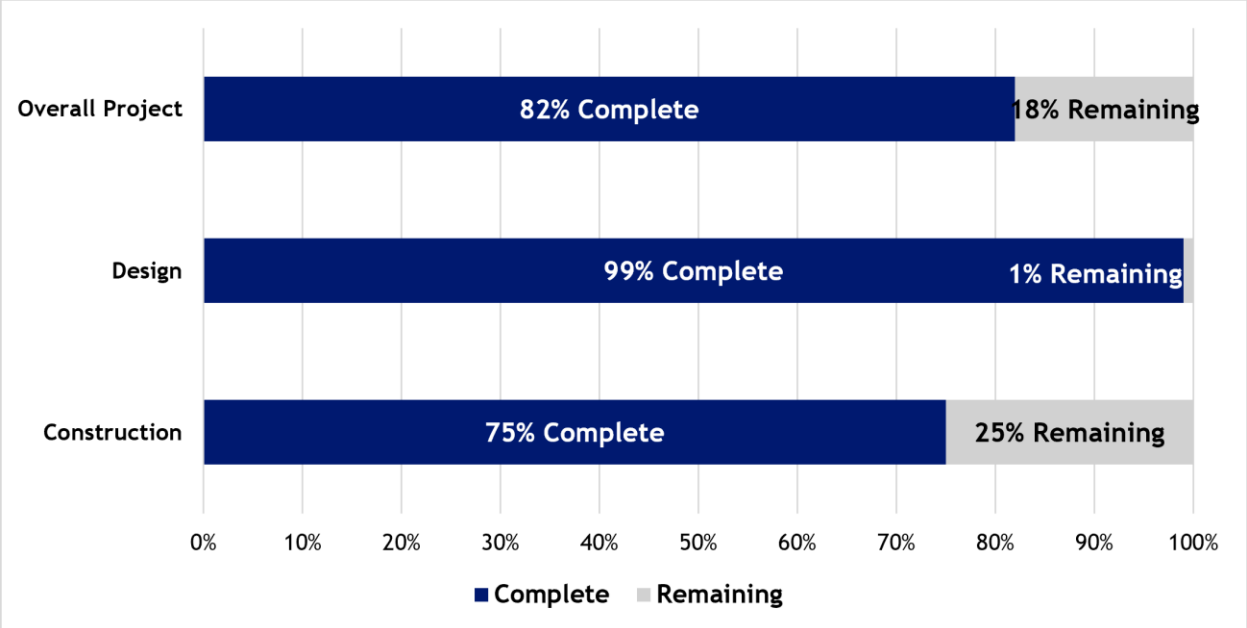


IV. Financial Contract Information

The following bar charts display the project construction payments versus remaining funds, the current contract total, and the original contract amount for Construction Package 1, Construction Package 2, and Construction Package 3. There have been no change orders to date.


Construction Package 1

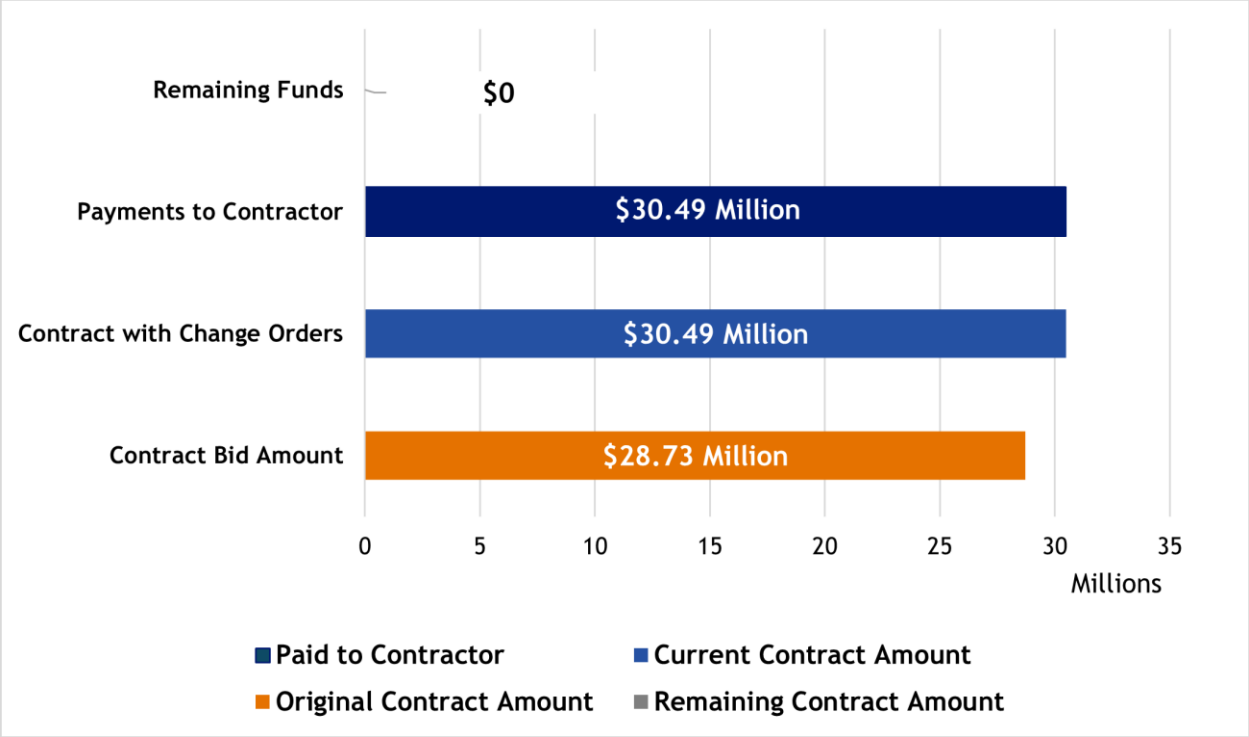

Construction Package 2

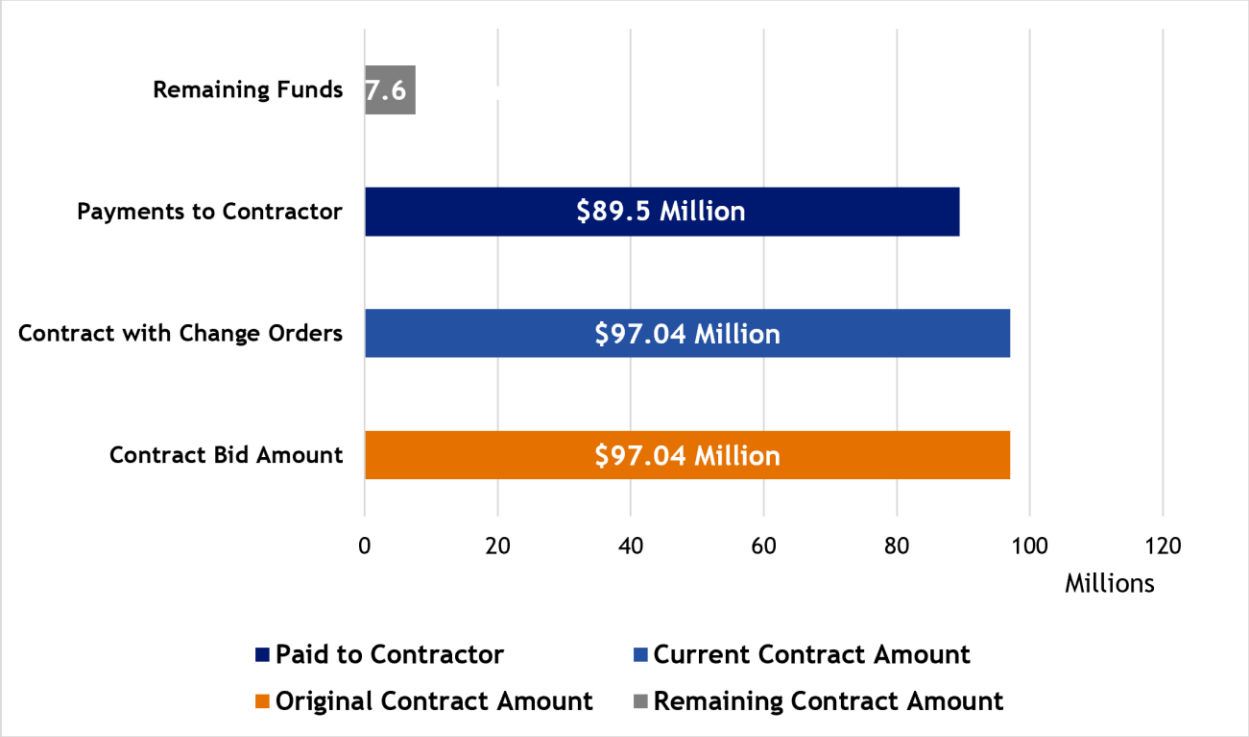


Construction Package 3

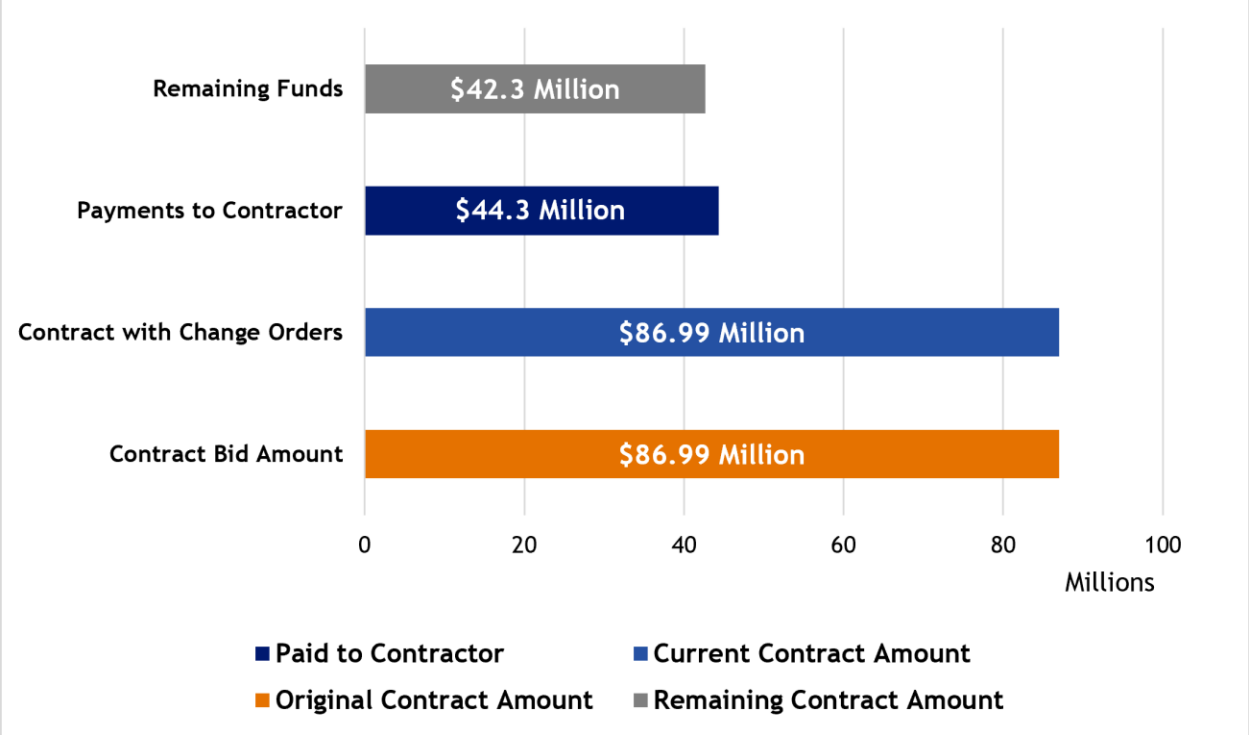

V. Contract Time


Design

The Notice-to-Proceed (NTP) was granted on August 31, 2023. The contact expiration date is May 4, 2028. The total contract time is 1708 days.

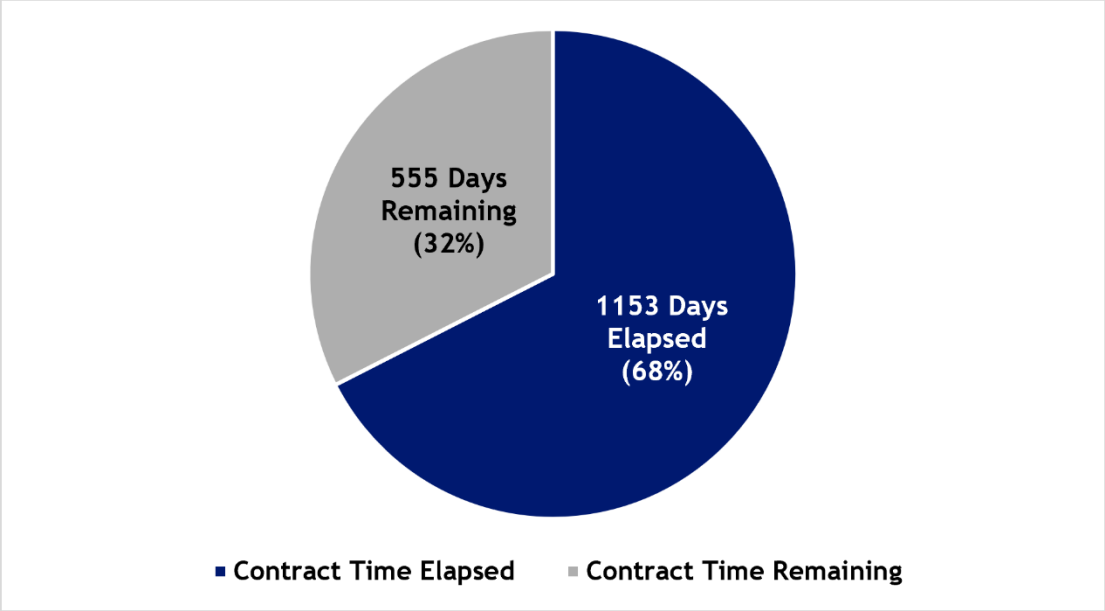


Construction Package 1 - Complete

The fixed completion date for Construction Package 1 is December 31, 2024. The total contract time is 237 days.

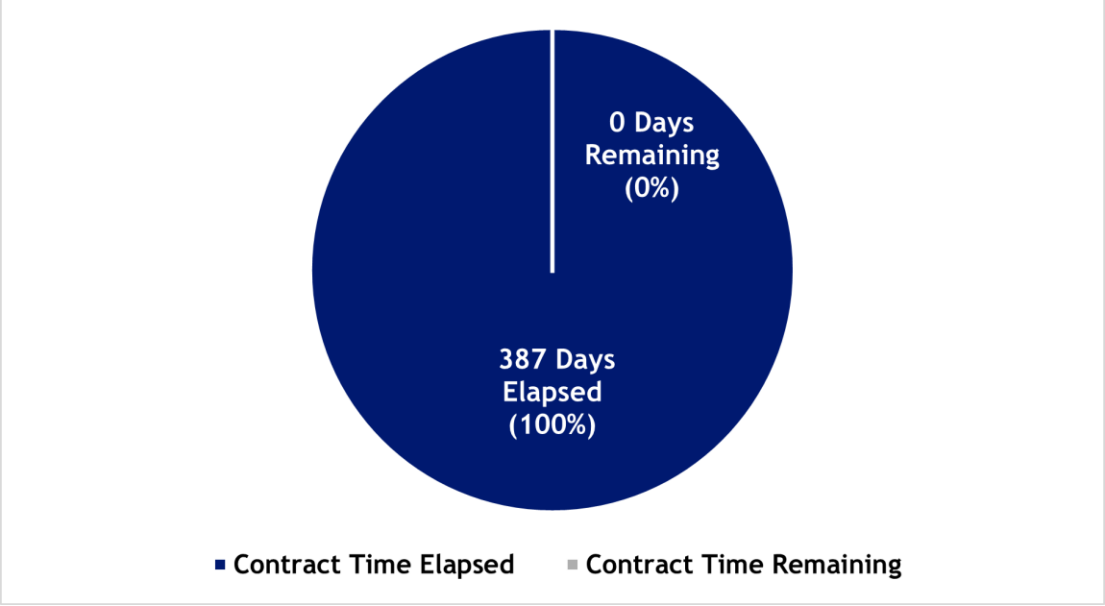

Construction Package 2

The fixed completion date for Construction Package 2 is June 30, 2027. The total contract time is 956 days.

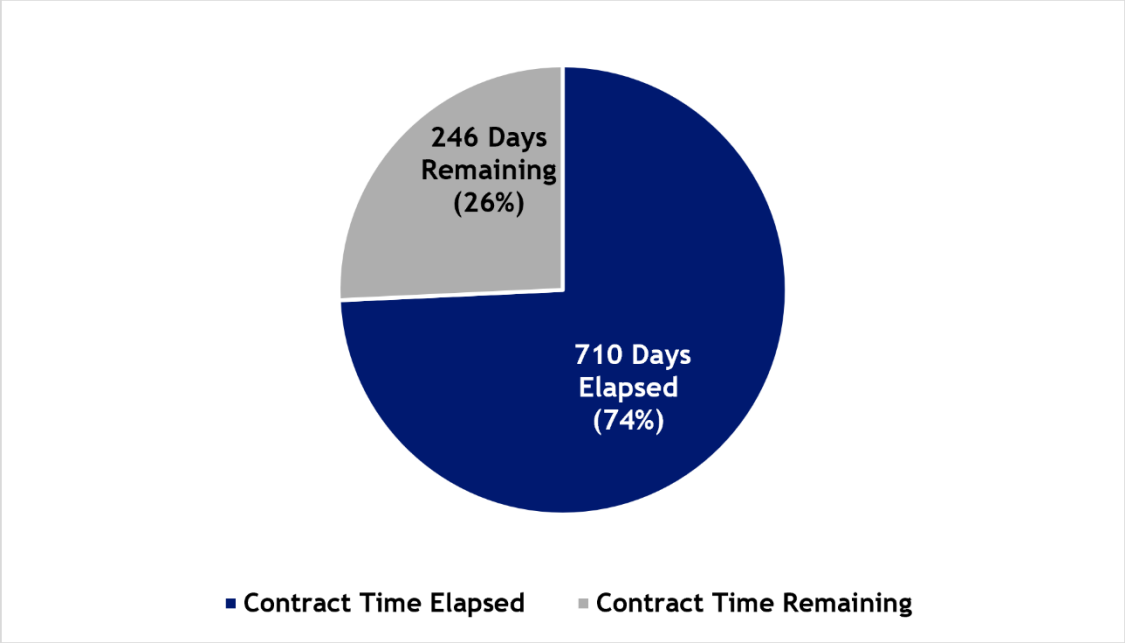

Construction Package 3

The fixed completion date for Construction Package 3 is January 28, 2028. The total contract time is 835.

