I-25 402 to SH 14 Procurement Schedule

ID	Task Mode	Task Name	Duration	Start	Finish
1		Project NTP	1 day	Mon 6/6/16	Mon 6/6/16
2		**Roadway**	**110 days**	**Tue 6/7/16**	**Mon 11/7/16**
3		Determine base configuration cross section and limits	20 days	Tue 6/7/16	Mon 7/4/16
4		Set Geometry and Run Base Configuration model	30 days	Tue 7/5/16	Mon 8/15/16
5		Prepare procurement set	60 days	Tue 8/16/16	Mon 11/7/16
6		Review Design Exceptions	20 days	Tue 8/16/16	Mon 9/12/16
7		**Tolling**	**120 days**	**Tue 6/7/16**	**Mon 11/21/16**
8		Update Tolling Service Agreement	120 days	Tue 6/7/16	Mon 11/21/16
9		**Utilities and Ditch companies**	**200 days**	**Tue 6/7/16**	**Mon 3/13/17**
10		Verify Mapping and Utility matrix	30 days	Tue 6/7/16	Mon 7/18/16
11		Meet with Utility and Ditch companies	30 days	Tue 7/19/16	Mon 8/29/16
12		Conflict identification and design (Set R/W Requirements)	60 days	Tue 8/30/16	Mon 11/21/16
13		Utility Relocations (URA's)	80 days	Tue 11/22/16	Mon 3/13/17
14		**ROW Plans (watch for outlet protection and Utilities)**	**341 days?**	**Tue 6/7/16**	**Tue 9/26/17**
15		Complete ROW Delineation (Rdwy, Drainage, Utilities)	1 day?	Tue 8/16/16	Tue 8/16/16
16		Title Search, Field Survey, and ROW Mapping	80 days	Tue 6/7/16	Mon 9/26/16
17		Right of plans (Requires a ROD for completion if fed funds used)	60 days	Tue 9/27/16	Mon 12/19/16
18		Appraisal and reviews	80 days	Tue 12/20/16	Mon 4/10/17
19		Acquisition	120 days	Tue 4/11/17	Mon 9/25/17
20		Relocations if needed	1 day	Tue 9/26/17	Tue 9/26/17
21		**Railroad Coordination**	**200 days**	**Tue 8/16/16**	**Mon 5/22/17**
22		Layout Bridges at RR's	60 days	Tue 8/16/16	Mon 11/7/16
23		Meet with GWRR and UPRR to confirm design and requirements	20 days	Tue 11/8/16	Mon 12/5/16
24		Construction and Maintenance Agreements	120 days	Tue 12/6/16	Mon 5/22/17
25		**Prepare ROD**	**120 days**	**Tue 6/7/16**	**Mon 11/21/16**
26		Prepare Decision Document	60 days	Tue 6/7/16	Mon 8/29/16
27		CDOT Review	10 days	Tue 8/30/16	Mon 9/12/16
28		Decision Document Revisions	10 days	Tue 9/13/16	Mon 9/26/16
29		FHWA Review	20 days	Tue 9/27/16	Mon 10/24/16
30		Final Document and Signed ROD	20 days	Tue 10/25/16	Mon 11/21/16
31		**Procurement**	**458 days?**	**Tue 6/7/16**	**Thu 3/8/18**
32		Develop RFQ and RFP Processes	100 days	Tue 6/7/16	Mon 10/24/16
33		Issue Requests for letter of Interest	1 day?	Tue 10/25/16	Tue 10/25/16
34		LOI's Due	30 days	Wed 10/26/16	Tue 12/6/16
35		Issue Draft RFQ	1 day?	Wed 12/28/16	Wed 12/28/16
36		Issue Final RFQ	1 day?	Thu 1/26/17	Thu 1/26/17
37		Teams Sumbit SOQ's	1 day	Fri 2/24/17	Fri 2/24/17

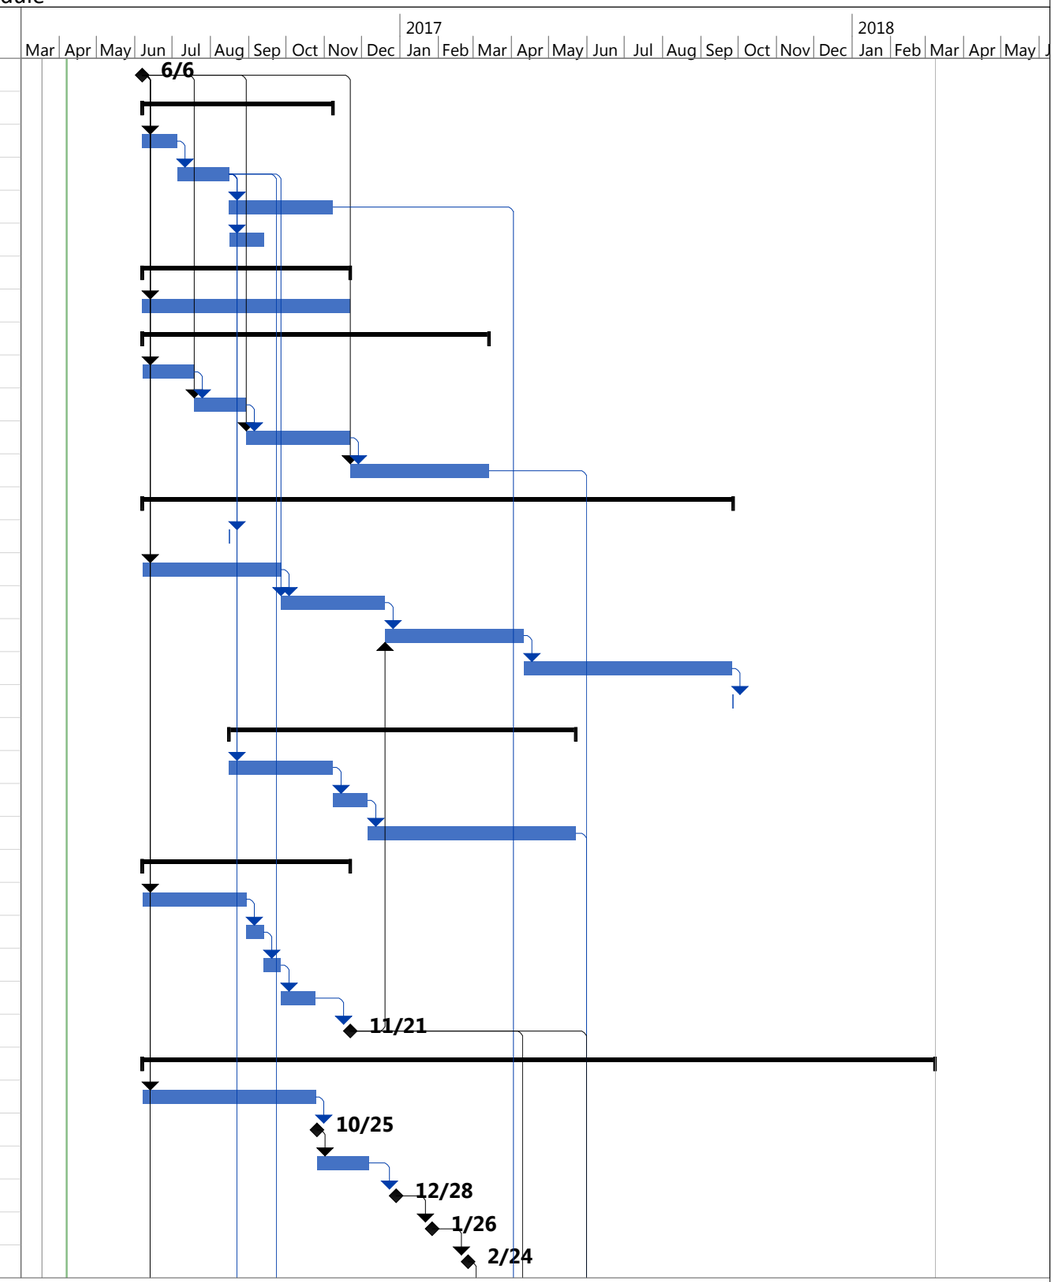

Project: DB Procurement Sched
Date: Thu 4/7/16

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

I-25 402 to SH 14 Procurement Schedule

ID	Task Mode	Task Name	Duration	Start	Finish
38		Review and Short list	30 days	Mon 2/27/17	Fri 4/7/17
39		**RFP Documents**	**408 days?**	**Tue 8/16/16**	**Thu 3/8/18**
40		**Draft RFP**	**180 days**	**Mon 9/26/16**	**Fri 6/2/17**
41		Develop Draft RFP	140 days	Mon 9/26/16	Fri 4/7/17
42		Issue Draft RFP	0 days	Fri 4/7/17	Fri 4/7/17
43		Industry Review Meetings	40 days	Mon 4/10/17	Fri 6/2/17
44		Prepare Base Configuration Plans and References	60 days	Tue 8/16/16	Mon 11/7/16
45		**Final RFP**	**101 days?**	**Mon 4/10/17**	**Mon 8/28/17**
46		Develop Final RFP	40 days	Mon 4/10/17	Fri 6/2/17
47		Isuue Final RFP	1 day?	Mon 6/5/17	Mon 6/5/17
48		1 on 1 meetings and contractor comments after RFP	60 days	Tue 6/6/17	Mon 8/28/17
49		Final Addendum	0 days	Mon 8/28/17	Mon 8/28/17
50		Teams Submit Proposals	1 day?	Tue 9/19/17	Tue 9/19/17
51		CDOT Evaluates proposals	20 days	Wed 9/20/17	Tue 10/17/17
52		NTP 1	1 day	Wed 12/13/17	Wed 12/13/17
53		NTP 2	1 day	Thu 3/8/18	Thu 3/8/18
54		**FHWA Major Projects Requirements**	**121 days?**	**Tue 6/7/16**	**Tue 11/22/16**
55		Project Management Plan	120 days	Tue 6/7/16	Mon 11/21/16
56		Risk Register	120 days	Tue 6/7/16	Mon 11/21/16
57		Cost Estimate Review	120 days	Tue 6/7/16	Mon 11/21/16
58		Concept of Operations	120 days	Tue 6/7/16	Mon 11/21/16
59		Systems engineering Document (90 days)	120 days	Tue 6/7/16	Mon 11/21/16
60		FHWA Approval	1 day?	Tue 11/22/16	Tue 11/22/16

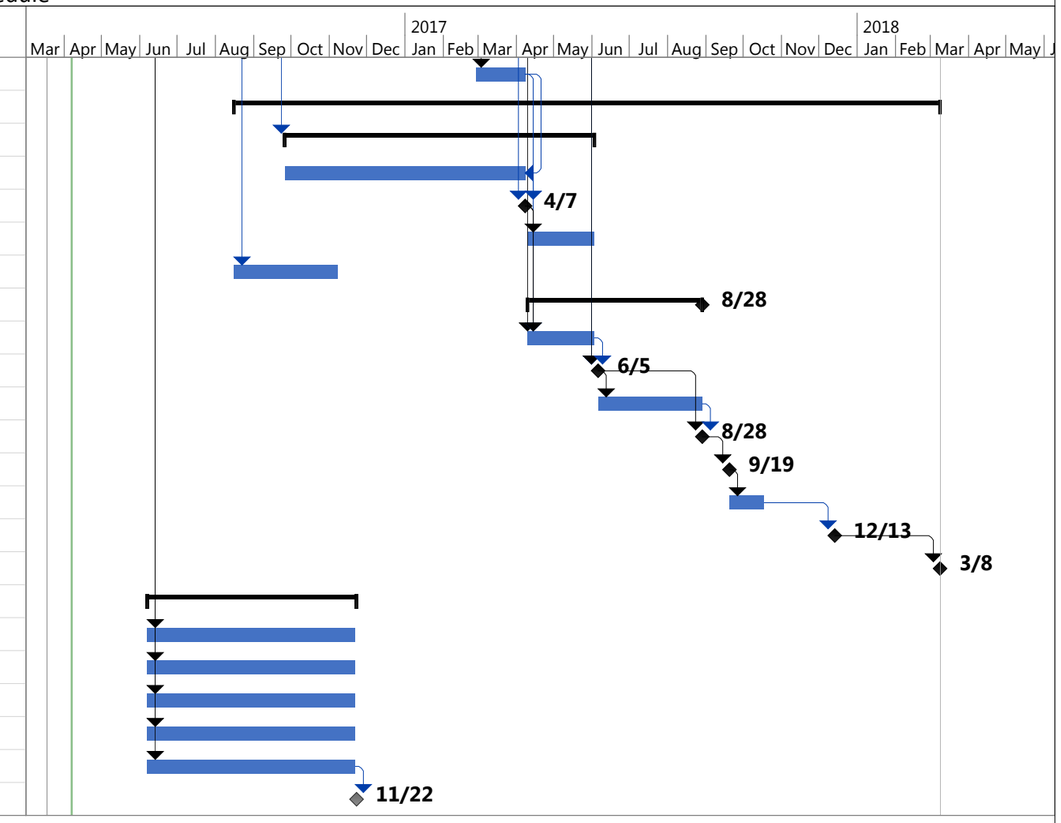

Project: DB Procurement Sched
Date: Thu 4/7/16

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
